




**PRE-STAGE C REMOVAL**  
074-0069 (EB) (Looking East)  
074-0070 (WB) (Looking West)

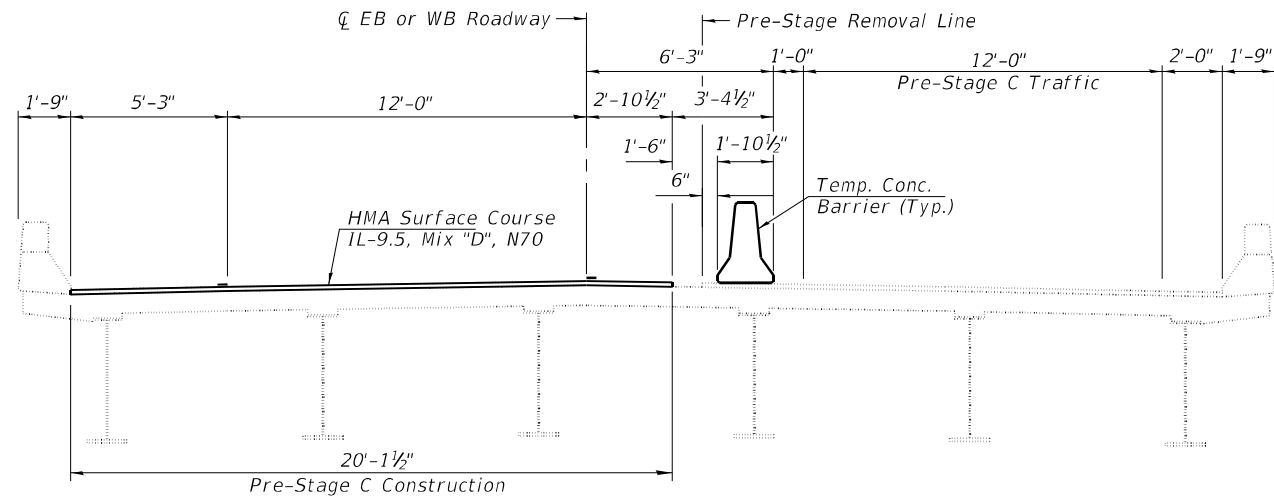

**PRE-STAGE C CONSTRUCTION**  
074-0069 (EB) (Looking East)  
074-0070 (WB) (Looking West)

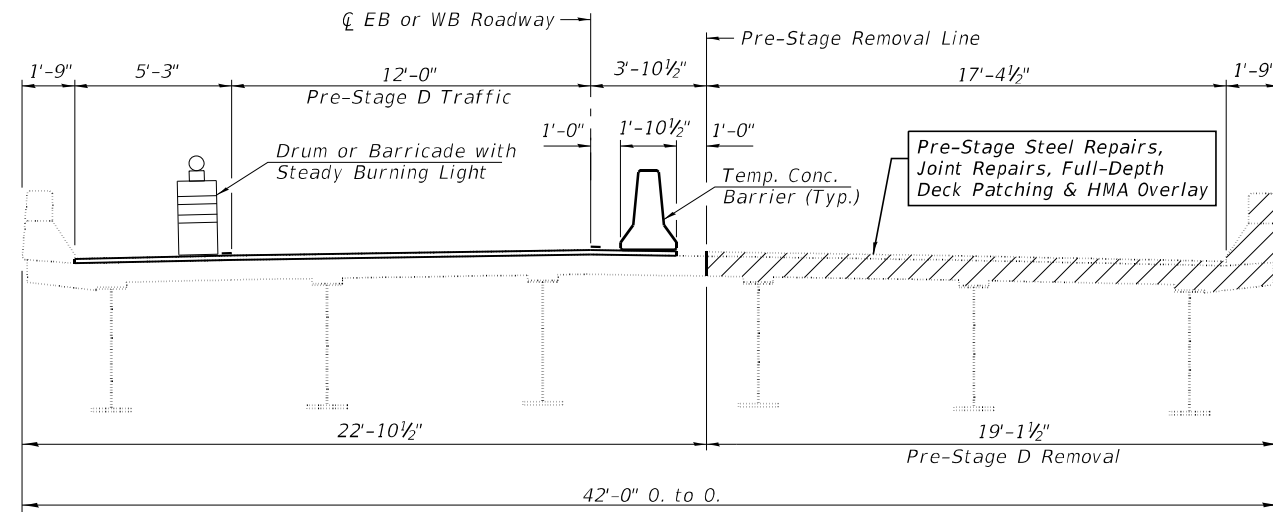

**PRE-STAGE D REMOVAL**  
074-0069 (EB) (Looking East)  
074-0070 (WB) (Looking West)

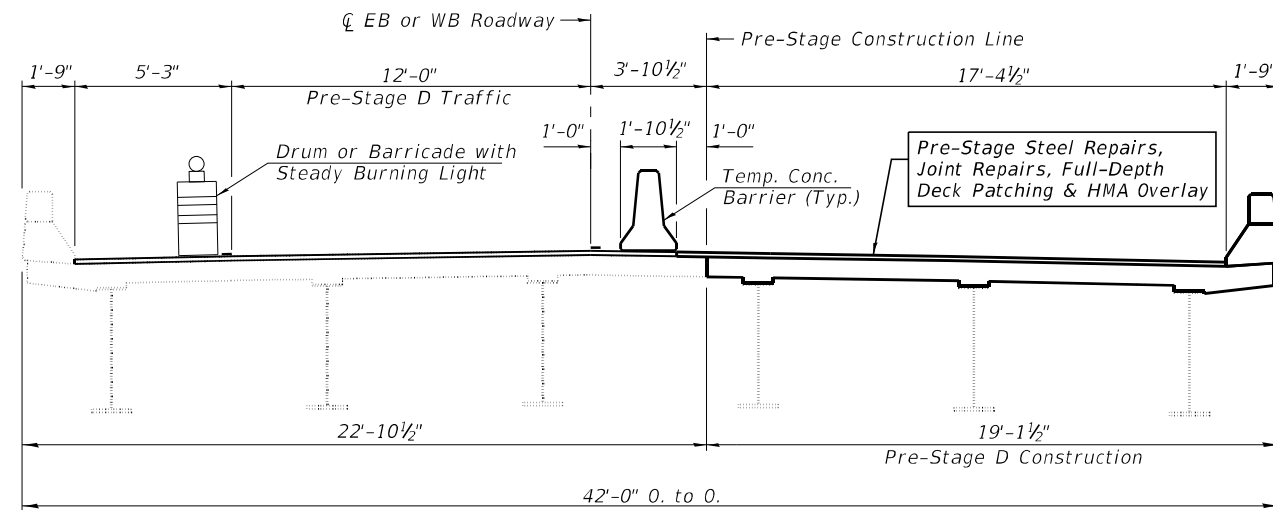

**PRE-STAGE D CONSTRUCTION**  
074-0069 (EB) (Looking East)  
074-0070 (WB) (Looking West)

**PRE-STAGE SEQUENCE OF CONSTRUCTION**

1. See Roadway Plans for all Traffic Control including Pre-Stage A and B Traffic Control.
2. Set up Pre-Stage C Traffic Control and switch traffic to outside of each structure.
3. Remove and replace HMA wearing surface on median side of each structure.
4. Set up Pre-Stage D Traffic Control and switch traffic to median side of each structure.
5. Remove existing HMA surface, perform full-depth deck patching, remove and replace expansion joints, perform steel repairs and place new HMA wearing surface on outside of each structure.

**Notes:**

- Pre-Stage Removal & Construction Line for repairs = Stage Removal Line.
- For quantities of Temporary Concrete Barrier, see Roadway Plans.
- For Temporary Concrete Barrier Details, see sheet 16 of 49.
- All Pre-Stage Construction Work will be done during Pre-Stage D Construction.
- These repairs will be at outside lanes of both WB and EB Structures as shown.

1 REVISD SHEET 7-16-2025

<div>CEC</div> <div>Cummins Engineering Corporation</div> <div>ENGINEERS &amp; SURVEYORS</div>	JOB : 2564.3	DESIGNED - AAN	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	PRE-STAGE CONSTRUCTION DETAILS STRUCTURE NO. 074-0069 (EB) AND 074-0070 (WB)	F.A.I.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	FILE : 0740069.0070-70024-003-PrestageSec	CHECKED - MDC	REVISED -			72	174-68VB/B	PIATT	93	39
	DATE : 3/10/2025	DRAWN - TSH	REVISED -			CONTRACT NO. 70024				
	SHEET NO. 3 OF 49 SHEETS					ILLINOIS FED. AID PROJECT				
