


STA. 404+50 TO STA. 411+00



TEMP STRIPE


TEMP STRIPE

TEMP STRIPE

STAGE I DRIVING

STAGE I CONSTRUCTION

STA. 404+50 TO STA. 411+00

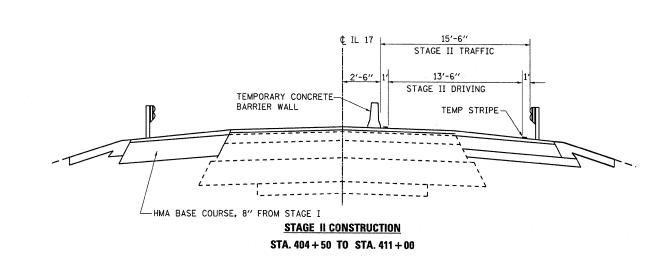

## STAGE I CONSTRUCTION

- 1. INSTALL TRAFFIC CONTROL PER STANDARD 701326
- 2. CONSTRUCT HMA BASE COURSE & TEMPORARY PAVEMENT
- 3. INSTALL TRAFFIC CONTROL PER STANDARD 701321 AND AS DETAILED IN THESE PLANS
- 4. REMOVE EXISTING EASTBOUND GUARDRAIL
- 5. REMOVE EXISTING EASTBOUND PAVEMENT
- 6. REMOVE EASTBOUND PORTION OF EXISTING STRUCTURE
- 7. CONSTRUCT EASTBOUND PORTION OF STRUCTURE, BRIDGE APPROACH & RIPRAP
- 8. CONSTRUCT EASTBOUND SHOULDER & TEMPORARY PAVEMENT (FOR STAGE II)
- 9. PLACE HOT-MIX ASPHALT OVERLAY
- 10. INSTALL GUARDRAIL

## STAGE II CONSTRUCTION

- 1. RELOCATE TRAFFIC CONTROL PER STANDARD 701321 AND AS DETAILED IN THESE PLANS
- 2. REMOVE TEMPORARY PAVEMENT AND PORTIONS OF HMA BASE COURSE (AS NECESSARY)
- 3. REMOVE EXISTING WESTBOUND PAVEMENT
- 4. REMOVE EXISTING GUARDRAIL
- 5. REMOVE WESTBOUND PORTION OF EXISTING STRUCTURE
- 6. CONSTRUCT WESTBOUND PORTION OF STRUCTURE, BRIDGE APPROACH & RIPRAP
- 7. CONSTRUCT WESTBOUND SHOULDER
- 8. PLACE HOT-MIX ASPHALT OVERLAY
- 9. INSTALL GUARDRAIL

## STAGE III CONSTRUCTION

- 1. TRAFFIC CONTROL PER STANDARD 701201
- 2. ANY HMA OVERLAY NOT PLACED IN PREVIOUS STAGES
- 3. PLACE PERMANENT PAVEMENT MARKINGS ON EASTBOUND AND WESTBOUND LANES
- 4. LANDSCAPE RESTORATION

-		<del></del>					
FII	LE NAME =	USER NAME = duncanbd	DESIGNED -	i i	REVISED -		
c:,	\pw_work\pwidot\duncanbd\dms32420\d36	6833-sht-details.dgn	DRAWN -		REVISED -		
		PLOT SCALE = 50.0000 '/ IN.	CHECKED -		REVISED -		
L	·	PLDT DATE = Oct 08, 2009 - 03:28:55 PM	DATE -		REVISED -		

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

TRAFFIC CONTROL CONSTRUCTION STAGING NOTES & DETAILS							SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
							(15BR-3)-1	LIVINGSTON	45	10
								CONTRACT	NO. 6	6833
ALE:	SHEET NO.	OF	SHEETS	STA.	TO STA.		ILLINOIS FED. AI	D PROJECT		
