


IL 13 /15
STAGE I – TRAFFIC STAGING TYPICAL



IL 13 /15 STAGE II – TRAFFIC STAGING TYPICAL

STAGE I - CONSTRUCT ENTRANCE AND SHOULDER IMPROVEMENTS

CHANGEABLE MESSAGE SIGNS WILL BE USED ON IL 13/15 EAST AND WEST OF THE IMPROVEMENT AND ON GREEN MOUNT RD NORTH AND SOUTH OF IL 13/15 TO NOTIFY THE PUBLIC OF THE ENTRANCE CLOSURES INTO ECKERT'S COUNTRY STORE AND FARMS.

INSTALL TRAFFIC CONTROL PER STANDARD 701421 AND THESE TRAFFIC CONTROL PLANS REDUCING TRAFFIC TO ONE INSIDE LANE FOR DAY OPERATIONS ONLY.

EXISTING ENTRANCE AT STA. 137+50 RT MUST REMAIN OPEN DURING STAGE I. THREE ENTRANCES AT STA. 142+25, 143+75, AND 145+00 LT SHALL BE CLOSED.

TWO LANES OF TRAFFIC EASTBOUND AND WESTBOUND SHALL BE OPERATIONAL AND CLEAR AT THE END OF EACH WORKDAY. NO OVERNIGHT CLOSURES WILL BE ALLOWED.

STAGE II - CONSTRUCT MEDIAN IMPROVEMENTS (COMPLETED IN 2 PHASES)

RELOCATE TRAFFIC CONTROL PER STANDARD 701421 AND THESE TRAFFIC CONTROL PLANS REDUCING TRAFFIC TO ONE OUTSIDE LANE FOR DAY OPERATIONS ONLY.

NEW CITY STREET TO REMAIN CLOSED DURING STAGE II WORK.


CONSTRUCT STAGE II MEDIAN IMPROVEMENTS IN TWO PHASES TO MAINTAIN ACCESS TO SOUTH ENTRANCES.

EXISTING PAVEMENT MARKING SHALL BE REMOVED AND REPLACED AT THE COMPLETION OF STAGE II PHASE II USING STANDARD 701426 FOR TRAFFIC CONTROL.

COUNTY TOTAL SHEET NO. ST. CLAIR 50 22

CONTRACT NO. 76D15

TWO LANES OF TRAFFIC EASTBOUND AND WESTBOUND SHALL BE OPERATIONAL AND CLEAR AT THE END OF EACH WORKDAY. NO OVERNIGHT CLOSURES WILL BE ALLOWED.

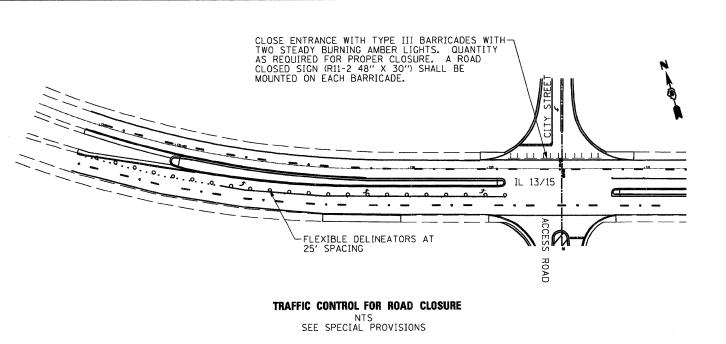

FILE NAME =	USER NAME = dwozniarski	DESIGNED -	REVISED -		SUGGESTED MAINTENANCE OF TRAFFIC SECTIONS AND NOTES		F.A.I. RTE.	SECTION	COUNTY
D876D15-sht-stagingl.dgn		DRAWN - DMW	REVISED -	STATE OF ILLINOIS			103	27-1-N	ST. CLAIR
	PLOT SCALE = 15.00 '/ IN.	CHECKED -	REVISED -	DEPARTMENT OF TRANSPORTATION					CONTRAC
	PLOT DATE = 9/14/2010	DATE - 7/9/2010	REVISED -		SCALE: NONE	SHEET NO. 1 OF 3 SHEETS STA. TO STA.	FED. ROAD DIST.	NO. ILLINOIS FED.	AID PROJECT
