
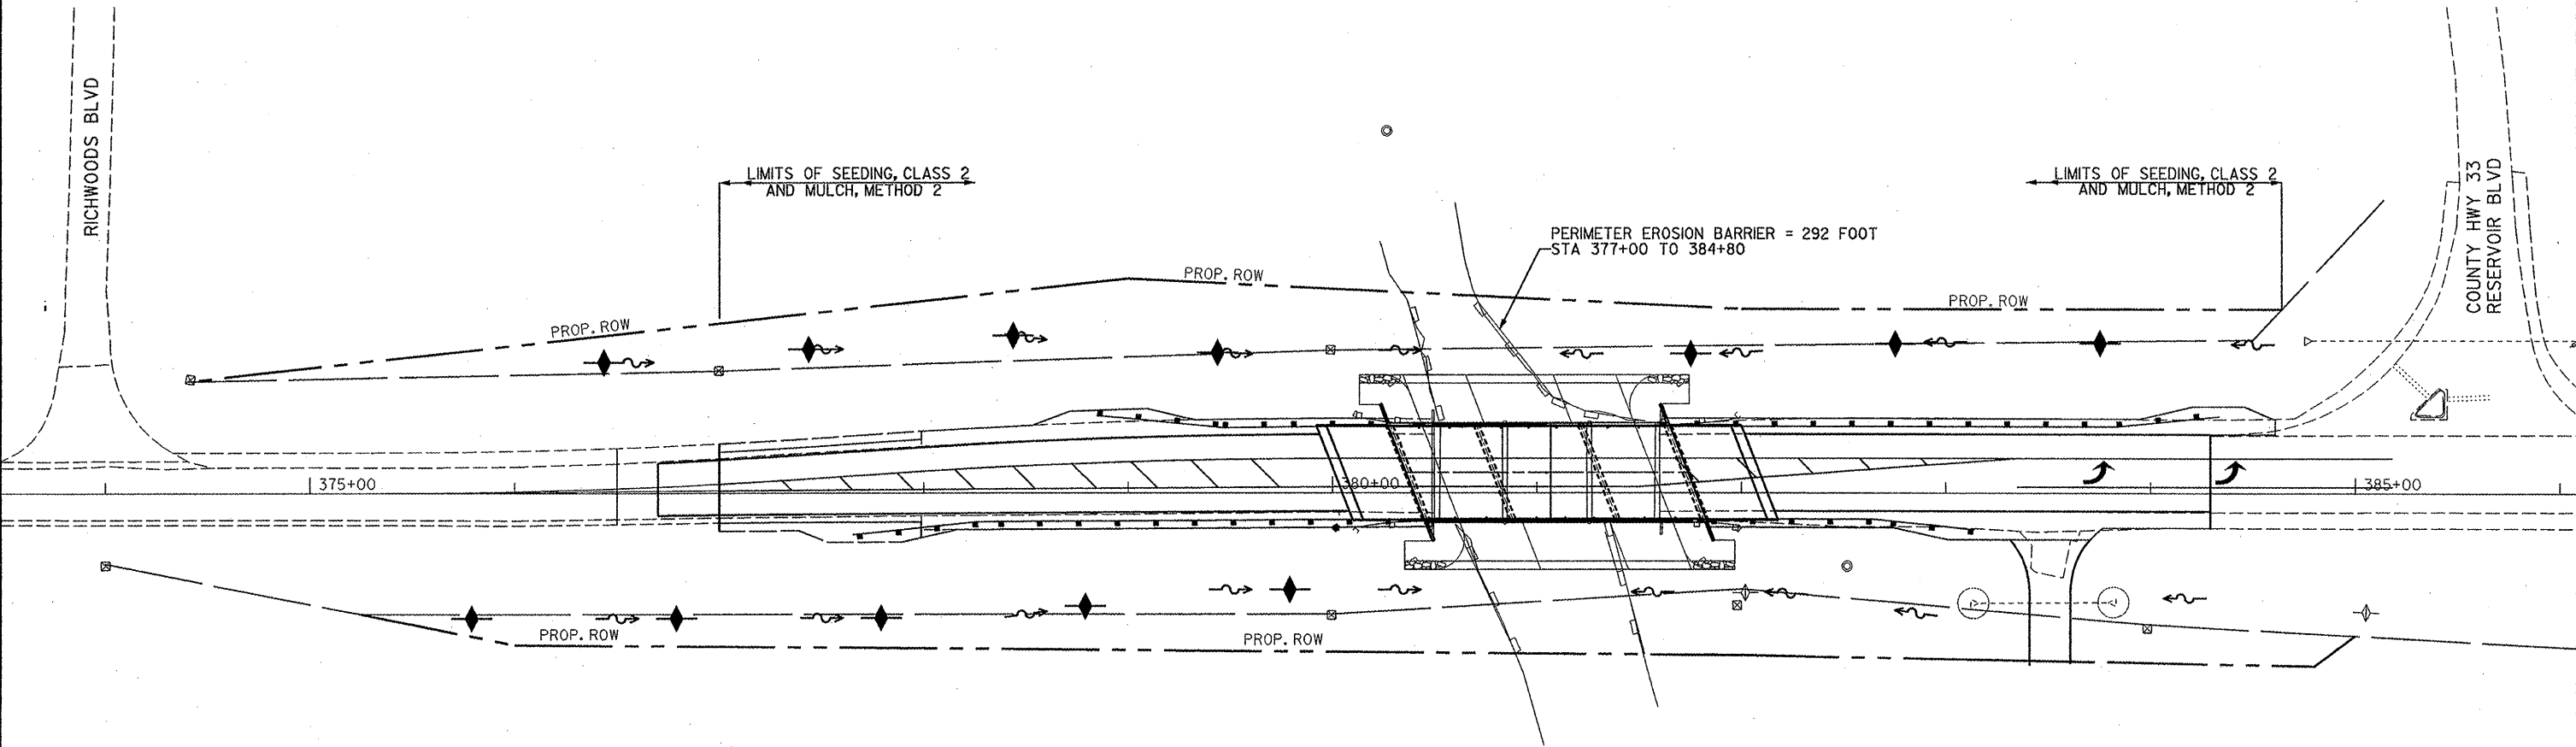


STATE OF ILLINOIS  
DEPARTMENT OF TRANSPORTATION



EROSION CONTROL SYSTEMS INSTALLATION SEQUENCE

1. REFER TO THE STAGE CONSTRUCTION AND MAINTENANCE OF TRAFFIC PLAN SHEETS FOR THE DETAILED SEQUENCE OF CONSTRUCTION AND STAGING PLAN.
2. PLACE THE PERIMETER EROSION BARRIER PRIOR TO STARTING ANY WORK.
3. INSTALL TEMPORARY EROSION CONTROL MEASURES IN PLACE PRIOR TO ANY GRADING OR DRAINAGE.
4. MAINTAIN ALL EROSION CONTROL SYSTEMS UNTIL SUCH TIME THAT THEY CAN BE REMOVED AS DIRECTED BY THE ENGINEER.
5. SEED, FERTILIZE AND MULCH AS SOON AS FINAL GRADING AND SHAPING IS COMPLETED.
6. REMOVE AND CLEANUP ALL REMAINING EROSION CONTROL SYSTEMS AS DIRECTED BY THE ENGINEER.

NOTES

1. THE TEMPORARY EROSION CONTROL SYSTEMS SHALL BE INSTALLED AND MAINTAINED BY THE CONTRACTOR AT THE LOCATIONS SHOWN ON THE STORM WATER POLLUTION PREVENTION PLAN AND AS DIRECTED BY THE ENGINEER. THE PLACEMENT OF THE TEMPORARY EROSION CONTROL SYSTEMS IS NECESSARY TO SATISFY THE REQUIREMENTS OF THE NPDES PERMIT. THE WORK SHALL BE IN ACCORDANCE WITH STANDARD 280001 AND SECTION 280 OF THE STANDARD SPECIFICATIONS.
2. ADDITIONAL TEMPORARY EROSION CONTROL SYSTEMS MAY BE REQUIRED DURING CONSTRUCTION. THE SYSTEMS SHALL BE PLACED AS DIRECTED BY THE ENGINEER AND SHALL BE PAID FOR IN ACCORDANCE WITH SECTION 280 OF THE STANDARD SPECIFICATIONS.
3. TEMPORARY SEEDING SHALL BE DONE AS DIRECTED BY THE ENGINEER AND IN ACCORDANCE WITH SECTION 280 OF OF THE STANDARD SPECIFICATIONS. A QUANTITY FOR TEMPORARY EROSION CONTROL SEEDING EQUAL TO THE PERMANENT SEEDING QUANTITY HAS BEEN ALLOWED FOR THIS PROJECT.
4. PERMANENT SEEDING, FERTILIZING OR MULCHING OF DISTURBED EARTH AREAS SHALL BE DONE AS SOON AS POSSIBLE AFTER FINAL GRADING IS COMPLETE FOR EACH STAGE OF THE PROJECT TO EXPEDITE THE ESTABLISHMENT OF VEGETATION AS SOON AS FINAL GRADING IS COMPLETE.
5. SEE THE PLAN AND PROFILE SHEETS AND CROSS SECTIONS FOR ADDITIONAL INFORMATION.

LEGEND

- INDICATED TEMPORARY DITCH CHECK
- INDICATES INLET AND PIPE PROTECTION
- INDICATES PERIMETER EROSION BARRIER
- FLOW ARROW
- EX DITCH CHECK

FILE NAME = 11 EROSION.dgn	USER NAME =	DESIGNED - GWM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	TEMPORARY/PERMANENT EROSION CONTROL SHEET	F.A.U. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - ALP	REVISED -			6658	(ZC-150-BR) BR	PEORIA	49	11
	PLOT SCALE = 40'	CHECKED - DEA/ENC	REVISED -			CONTRACT NO. 68478				
	PLOT DATE = 07/28/09	DATE - 07/28/09	REVISED -			ILLINOIS    FED. AID PROJECT				
	SCALE:					SHEET NO. OF SHEETS		STA. TO STA.		
