PRE-STAGE:

-- ESTABLISH TRAFFIC CONTROL SIGNS, AND BARRICADES ON FLEMING ROAD AND IL ROUTE 120

- REMOVE EXISTING SHOULDER ON NORTHBOUND SIDE OF FLEMING ROAD FROM STATION 209+00 TO 219+17.

- INSTALL TEMPORARY PAVEMENT ON NORTHBOUND SIDE OF FLEMING ROAD FROM STATION 209+00 TO 219+17.

STAGE 1:

- ESTABLISH STAGE 1 TEMPORARY TRAFFIC CONTROL SIGNS, AND BARRICADES, ON IL ROUTE 120 AND FLEMING ROAD.

- REMOVE EXISTING PAVEMENT AND SHOULDER ON SOUTHBOUND SIDE OF FLEMING ROAD FROM STATION 211+29 TO 219+15.

- INSTALL NEW PAVEMENT WITH SUBRGADE ON SOUTHBOUND SIDE OF FLEMING ROAD FROM STATION 211+29 TO 219+15.

- INSTALL TEMPORARY PAVEMENT ON SOUTHBOUND SIDE OF FLEMING ROAD FROM STATION 209+00 TO 218+12.4

- INSTALL NEW SHOULDER ON THE EASTBOUND LANE OF IL ROUTE 120 WEST OF FLEMING ROAD.

- PERFORM DITCH IMPROVEMENT WORK ON EASTBOUND SIDE OF IL ROUTE 120 WEST OF FLEMING ROAD.

LEGEND:

- A TEMPORARY PAVEMENT MARKING, TYPE III 4" SOLID WHITE EDGE LINE
- TEMPORARY PAVEMENT MARKING, TYPE III
 4" SOLID SINGLE YELLOW
- © TEMPORARY PAVEMENT MARKING, TYPE III 4" SOLID DOUBLE YELLOW



. WORK ZONE




TEMPORARY PAVEMENT, 9"




PAVEMENT AND SHOULDER REMOVAL

NOTE:
"PCC TEMPORARY PAVEMENT SHALL CONSIST OF CLASS PV CONCRETE
CONCRETE MEETING THE REQUIREMENTS OF ART, 1020 OF THE
STANDARD SPECIFICATIONS".

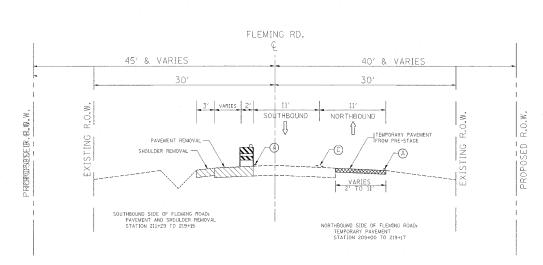

FLEMING ROAD STAGE 1 REMOVALS STA 211+29 TO 219+15

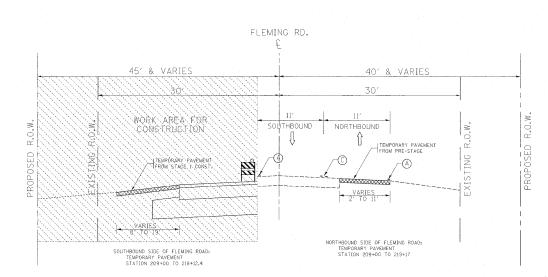

FLEMING ROAD STAGE 1 CONSTRUCTION STA 211+29 TO 219+15

FILE NAME =	USER NAME ≃ galbanjr	DESIGNED -	REVISED -			STAGING DESCRIPTION AND TYPICAL SECTIONS	F.A.P	SECTION	COUNTY TOTAL SHEET	
c:\pw_work\pwidot\galbanjr\d0107803\P113	07-Design.dgn	DRAWN -	REVISED -	STATE OF ILLINOIS				15-N-6	MCHENRY 67 16	
	PLDT SCALE = 50.000 1/ in.	CHECKED -	REVISED -	DEPARTMENT OF TRANSPORTATION	FOR MAINTANCE OF TRAFFIC		333	13 11 0	CONTRACT NO 60127	
	PLOT DATE = 9/24/2011	DATE -	REVISED -		SCALE:	SHEET NO. OF SHEETS STA. TO STA.		ILLINOIS FED. AID PROJECT		
