
**→**®→Z SCALE IN FEET

ROUTE NO.	SECTION	COUNTY KANKAKEE		TOTAL SHEETS	SHEET NO.
FAP 330	16BR			37	7
ILLINOIS					

CONTRACT NO. 66365

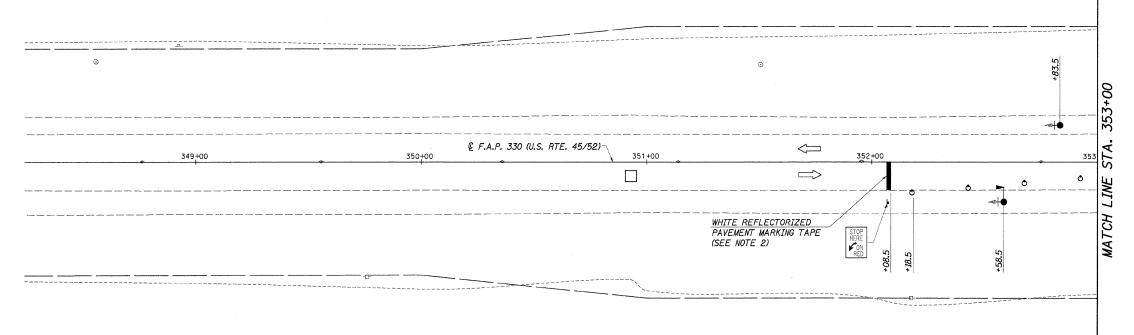

#### STAGING NOTES

- 1. PRIOR TO STAGE I, CONSTRUCT TEMPORARY BITUMINOUS BASE COURSE TO THE WEST.
  2. WIDENING SHALL PROVIDE FOR A MINIMUM 15.5' TRAFFIC LANE.

### STAGE I


- REMOVE EAST HALF OF EXISTING BRIDGE STRUCTURE AND APPROACH PAVEMENT
- PLACE EAST HALF OF PROPOSED BRIDGE STRUCTURE AND PAVEMENT.
- PLACE EAST GUARDRAIL AND BITUMINOUS SHOULDERS ON EAST SIDE.

## STAGE II

- REMOVE WEST HALF OF EXISTING BRIDGE STRUCTURE AND APPROACH PAVEMENT.
  PLACE WEST HALF OF PROPOSED BRIDGE STRUCTURE AND PAVEMENT.
  PLACE GUARDRAIL AND BITUMINOUS SHOULDER ON WEST SIDE.

## STAGE III

- MILLING AND RESURFACING
- 2. FINAL SEEDING

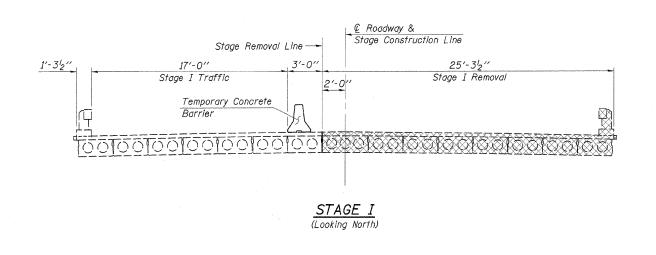

# MONODIRECTIONAL LIGHT ARROW BOARD TEMPORARY CONCRETE BARRIER IMPACT ATTENUATOR, TEMPORARY (NON-REDIRECTIVE), TEST LEVEL 3

<u>LEGEND</u>

DRUM WITH STEADY BURNING

TYPE C MONODIRECTIONAL REFLECTOR

 $\Rightarrow$ DIRECTION OF TRAFFIC

TT TYPE III BARRICADE

STAGE REMOVAL

TEMPORARY BITUMINOUS BASE COURSE -≪-TRAFFIC SIGNAL WITH BACKPLATE

DETECTOR LOOPS

\_\_\_\_

AGGREGATE SHOULDER

MICROWAVE ON ARM

#### **NOTES**

- 1. THE PLACEMENT OF TEMPORARY CONCRETE BARRIERS, IMPACT ATTENUATORS, TEMPORARY SIGNALS AND STOP LINES ARE AS SHOWN. PLACE REMAINING TRAFFIC CONTROL ITEMS PER
- 2. PAVEMENT MARKING TAPE, TYPE III, 24" SHALL BE 6 STRIPS OF PAVEMENT MARKING TAPE, TYPE III, 4", COST INCIDENTAL TO TRAFFIC CONTROL
- 3. ALL CONFLICTING PAVEMENT MARKINGS SHALL BE REMOVED. (PAID FOR AS PAVEMENT MARKING REMOVAL)

MAINTENANCE OF TRAFFIC STAGE I FAP ROUTE 330 (U.S. RTE. 45/52) OVER SOUTH BRANCH ROCK CREEK SECTION 16BR KANKAKEE COUNTY S.N. 046-0047

OZYURT AND STONE, INC. CONSULTING ENGINEERS

JOB NO.: 0306.3 DATE: 09-07-04
