



MATCHLINE STA. 16038+00

MATCHLINE STA. 209+00
SEE RAMP B

RAMP B

16040+00

16045+00

16080+00

STUENKEL ROAD

MATCHLINE STA. 16052+00

LEGEND:


- TRAFFIC MOVEMENT
- WORK ZONE
- BARRICADE, TYPE III
- VERTICAL BARRICADE WITH BI-DIRECTIONAL STEADY-BURNING LIGHT, 50' C-C IN TANGENTS, 20' IN TAPERS
- VERTICAL PANEL (POST MOUNTED)
- TEMPORARY AGGREGATE
- MOT WORK ZONE SIGN
- TEMPORARY PAVEMENT

MATCHLINE STA. 331+00
SEE RAMP C

RAMP C

NOTES:

1. SEE STUENKEL ROAD MAINTENANCE OF TRAFFIC - DETOUR PLAN FOR ADVANCED SIGNING.
2. AN ADDITIONAL QUANTITY OF 175 FT FOR TEMPORARY CONCRETE BARRIER AND RELOCATE TEMPORARY CONCRETE BARRIER QUANTITY WAS PROVIDED IN STAGE 1 FOR USE BY THE ENGINEER ON BOTH SIDES OF THE BRIDGE DURING CONSTRUCTION.
3. THE EXISTING R.O.W. IS NOT DEPICTED WITHIN THE PROJECT LIMITS FOR CLARITY.

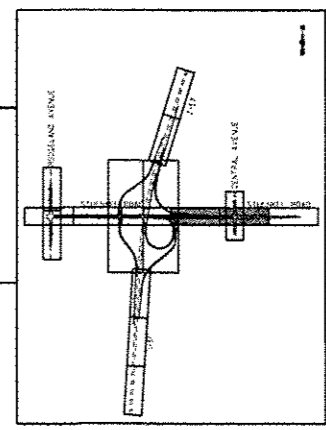

0 50 100
SCALE: 1" = 50'-0"



MATCHLINE STA. 16052+00

MATCHLINE STA. 802+00

- 4" LINE YELLOW DOUBLE CENTER
- TEMPORARY PAVEMENT
- CENTRAL AVE C
- 4" LINE (WHITE)

STUENKEL ROAD

STUENKEL ROAD C

CENTRAL AVENUE

16055+00

16060+00

16065+00

MATCHLINE STA. 16066+00

PROPOSED ACCESS CONTROL

PROPOSED R.O.W.

ROAD CLOSED
R11-2
48" x 30"
QTY. 2
STA. 16056+37

ROAD CLOSED
R11-2
48" x 30"
QTY. 2
STA. 16056+60

MATCHLINE STA. 798+00

0 50 100
SCALE: 1" = 50'-0"

TYLIN INTERNATIONAL	USER NAME	DESIGNED JTP	REVISED 12/04/2013	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	STUENKEL ROAD AT I-57 RIDGELAND AVENUE TO CENTRAL AVENUE MAINTENANCE OF TRAFFIC STAGE 2 - STUENKEL ROAD			F.A. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.	
	PL01 SCALE	DRAWN JTP	REVISED					57	99-1HB-R1	WILL	679	109	
	PL01 DATE	CHECKED JPM	REVISED					SCALE: 1" = 50' SHEET 1 OF 4 SHEETS STA. 16038+00 TO STA. 16066+00			CONTRACT NO. 60L69		ILLINOIS FED. AID PROJECT
		DATE 05/10/2013	REVISED										

PA6026120-57 - Stuenkel Road AC, 30m to change AC, Stuenkel MOT, DOC 2-1.dgn

10:30:36 AM 12/5/2013
