


**MEDIAN DETAIL AT SOUTHBOUND INTERSECTION**

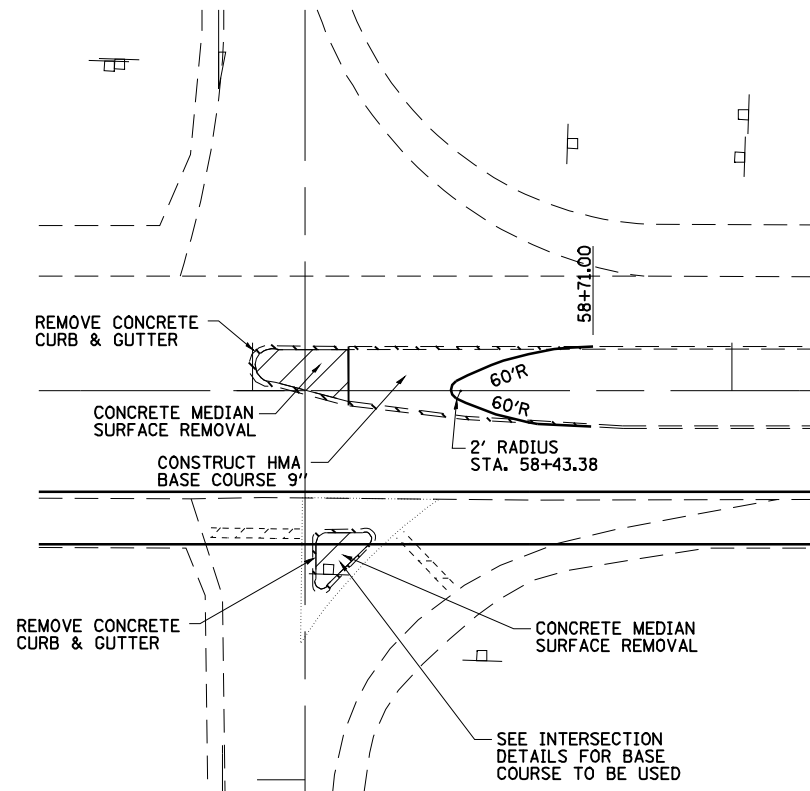

**MEDIAN DETAIL AT NORTHBOUND INTERSECTION**

**GENERAL NOTES FOR STAGE CONSTRUCTION**

1. ALL SIGNAGE, SPACING, TRAFFIC CONTROL EQUIPMENT AND TEMPORARY MARKINGS SHALL BE IN ACCORDANCE WITH THE LATEST VERSION OF HIGHWAY STANDARD 701331, AND SHALL BE INCLUDED IN THE CONTRACT UNIT LUMP SUM PRICE FOR TRAFFIC CONTROL AND PROTECTION STANDARD 701331.
2. REMOVAL OF EXISTING PAVEMENT MARKING THAT CONFLICTS WITH THE TEMPORARY PAVEMENT MARKINGS FOR TRAFFIC CONTROL WILL BE PAID FOR AT THE CONTRACT UNIT PRICE PER SQUARE FOOT FOR PAVEMENT MARKING REMOVAL.
3. REMOVAL OF TEMPORARY PAVEMENT MARKING FOR TRAFFIC CONTROL & PROTECTION STAGING WILL BE PAID FOR AT THE CONTRACT UNIT PRICE PER SQUARE FOOT FOR WORK ZONE PAVEMENT MARKING REMOVAL.
4. PRIOR TO ROUTING TRAFFIC ONTO THE SHOULDERS AS SHOWN IN THE STAGING PLANS, THE CONTRACTOR SHALL SECURE THE GRATINGS ON SHOULDER INLETS AS DIRECTED BY THE ENGINEER. THE COST OF THIS WORK WILL BE INCLUDED IN THE TRAFFIC CONTROL STANDARD 701331 PAY ITEM.

**STAGE I NOTES/ANTICIPATED SEQUENCE**

1. CONSTRUCT TEMPORARY MEDIAN CROSSOVER AT THE I-55 RAMPS/STAUNTON ROAD INTERSECTIONS UTILIZING HIGHWAY STANDARD 701201.
2. CONSTRUCT HMA BASE COURSE, 11", FOR STAGE I TRAFFIC, UTILIZING TRAFFIC CONTROL STD. 701326.
3. ERECT SIGNS, TEMPORARY BARRIERS, TEMPORARY PAVEMENT MARKINGS ACCORDING TO THESE PLANS AND TRAFFIC PROTECTION AND CONTROL 701331.
4. REMOVE THE STAGE I PORTION OF THE EXISTING STRUCTURE AND PAVEMENT.
5. CONSTRUCT THE STAGE I PORTION OF THE BRIDGE REPAIR AND PAVEMENT RESURFACING.
6. CONSTRUCT HMA BASE COURSE, 11", FOR STAGE II TRAFFIC.

**COMBINATION CURB & GUTTER REMOVAL**

STATION TO	STATION	OFFSET	FEET
41+12.34	41+92.44	LT	81
41+12.34	41+92.44	RT	101
58+07.57	58+71.00	LT	84
58+07.57	58+71.00	RT	65
58+12.00	58+25.00	RT	45
TOTAL			376


**HOT-MIX ASPHALT BASE COURSE 9"**

STATION TO	STATION	OFFSET	SQ.YD.
41+12.34	41+98.00	LT&RT	92
57+99.00	58+71.00	LT&RT	67
TOTAL			159

**CONCRETE MEDIAN SURFACE REMOVAL**

STATION TO	STATION	SQ.FT.
41+80	42+00	116
57+99	58+20	158
58+12	58+25	85
TOTAL		359

**LEGEND**

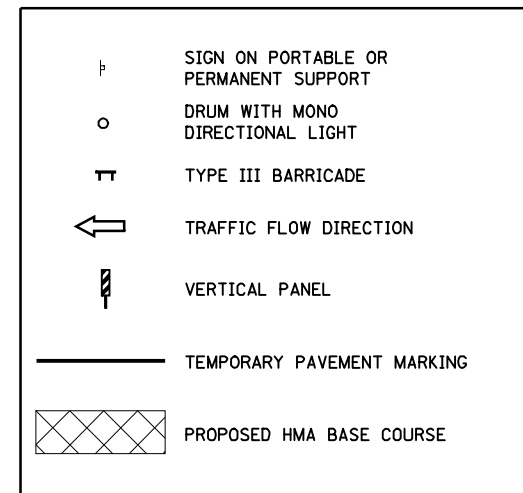

FILE NAME =	USER NAME = coxte	DESIGNED -	REVISED -
es:\pwork\PWIDOT\COXTE\d0190279\0672400-ahs-Staging0045.dgn		DRAWN -	REVISED -
PLOT SCALE = 40.0000' / IN.		CHECKED -	REVISED -
PLOT DATE = Mar-23-2010 03:23:53PM		DATE -	REVISED -

**STATE OF ILLINOIS  
DEPARTMENT OF TRANSPORTATION**

**STAGE I CONSTRUCTION (SN 059-0045)**

SCALE: SHEET NO. 4 OF 8 SHEETS STA. TO STA.

F.A. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
55	59RS-2, BR	MACOUPIN	100	74
CONTRACT NO. 72A60				
FED. ROAD DIST. NO. ILLINOIS FED. AID PROJECT				
