
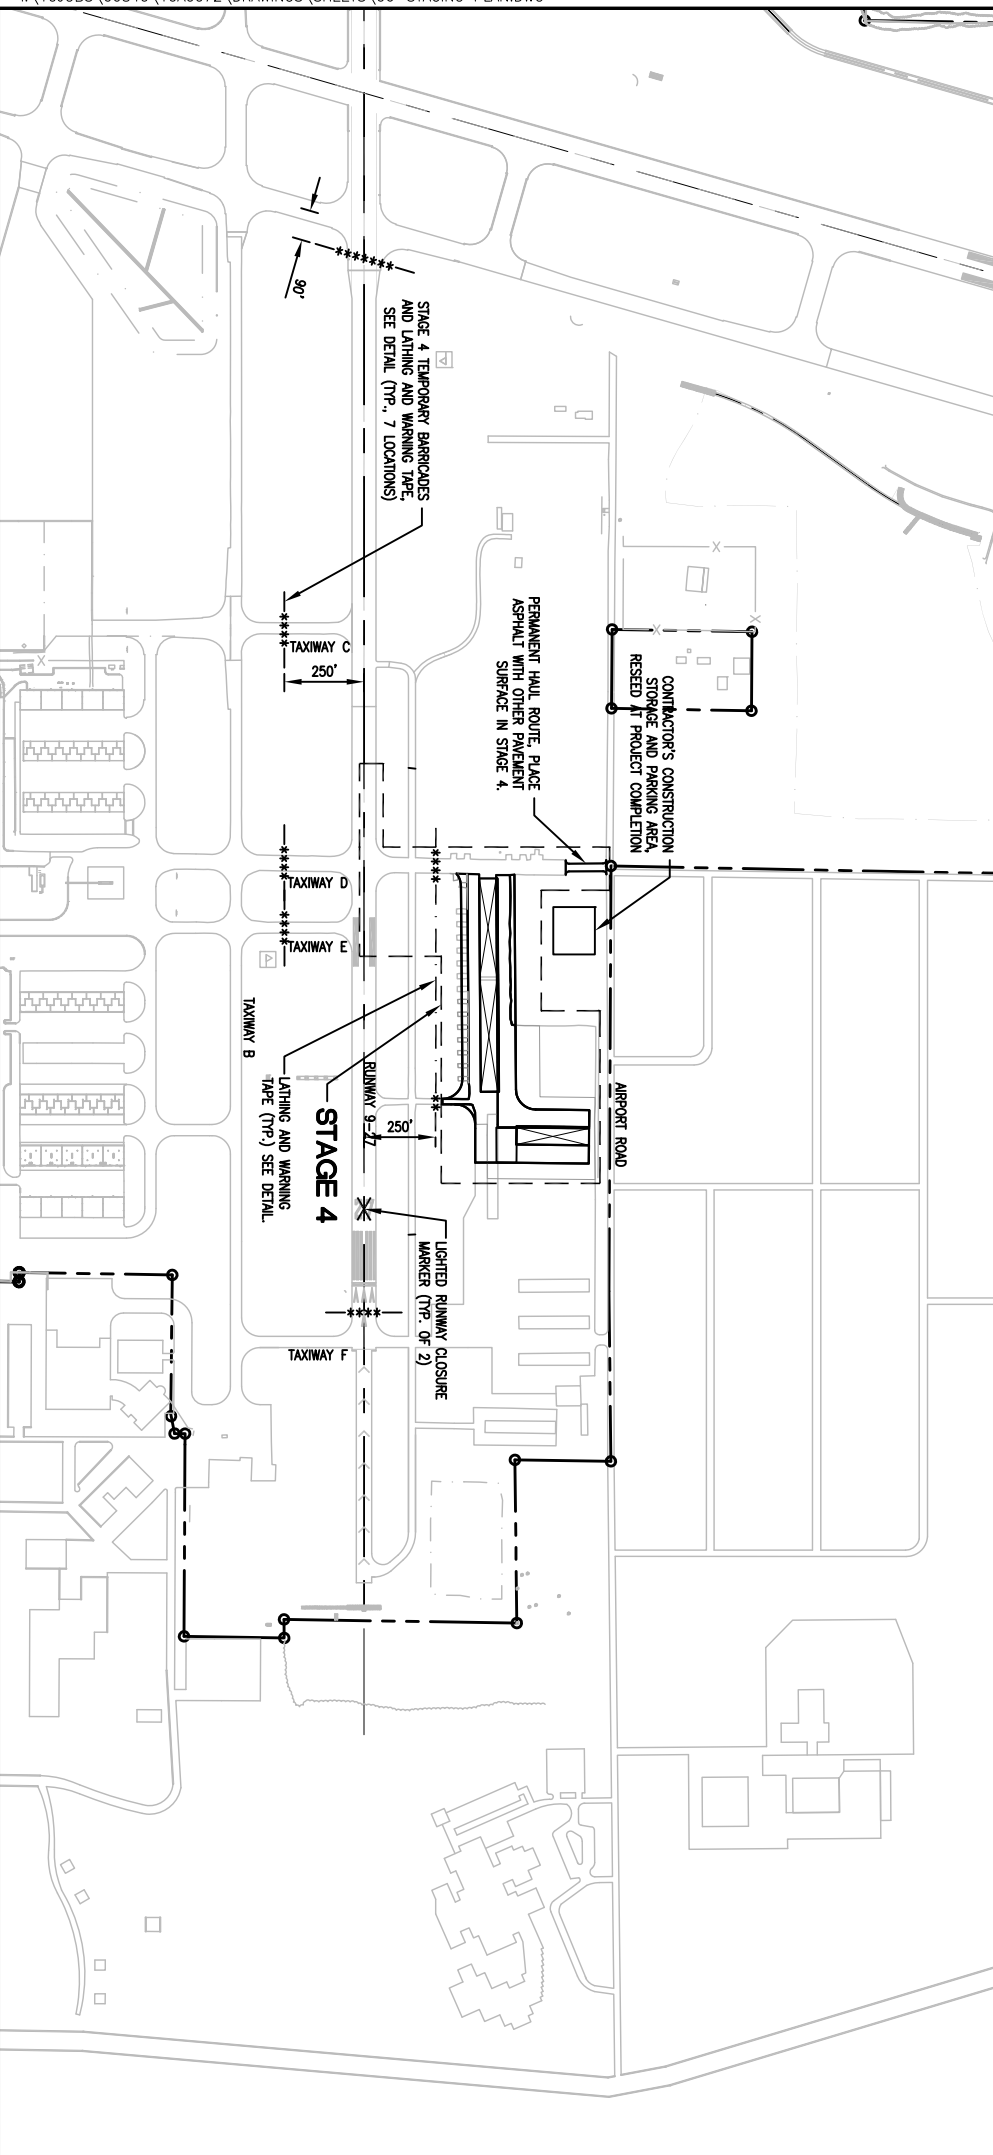


STAGE 3

- NOTES:**
- ALL CONTRACTOR ACTIVITIES SHALL TAKE PLACE WITHIN CONSTRUCTION LIMIT LINES AS SHOWN.
 - ALL CONSTRUCTION EQUIPMENT WILL BE LIMITED TO A HEIGHT OF 29 FEET UNLESS PRIOR APPROVAL GIVEN BY THE ENGINEER.
 - CONTRACTOR'S EQUIPMENT MAY NOT DISRUPT FLIGHT OPERATIONS ON RUNWAY 9-27 AT ANY TIME.
 - SEE CONSTRUCTION AND SAFETY NOTES, SHEET 4.
 - **THE FOLLOWING ITEMS ARE TO BE COMPLETED IN STAGE 3:**
 - MILL EXISTING PAVEMENTS WITHIN STAGE 3 LIMITS.
 - REMOVE EXISTING PAVEMENTS WITHIN STAGE 3 LIMITS.
 - INSTALL AGGREGATE BASE COURSE WITHIN STAGE 3 LIMITS.
 - TOPSOIL, SEEDING AND MULCHING WITHIN STAGE 3 LIMITS.



STAGE 4

- NOTES:**
- ALL CONTRACTOR ACTIVITIES SHALL TAKE PLACE WITHIN CONSTRUCTION LIMIT LINES AS SHOWN.
 - ALL CONSTRUCTION EQUIPMENT WILL BE LIMITED TO A HEIGHT OF 29 FEET UNLESS PRIOR APPROVAL GIVEN BY THE ENGINEER.
 - **RUNWAY 9-27 WILL HAVE TO BE CLOSED TO COMPLETE THE MARKING. ALL MARKING THAT REQUIRES THE RUNWAY CLOSURE (WITHIN 250 FEET) SHALL BE COMPLETED WITHIN ONE DAY.**
 - SEE CONSTRUCTION AND SAFETY NOTES, SHEET 4.
 - **THE FOLLOWING ITEMS ARE TO BE COMPLETED IN STAGE 4:**
 - INSTALL SURFACE COURSE WITHIN STAGE 4 LIMITS.
 - MARKING WITHIN STAGE 4 LIMITS.

