
SUGGESTED SEQUENCE OF CONSTRUCTION:

STAGE 2 CONSTRUCTION

- 1. STAGE 2 CONSTRUCTION SHALL CONSIST OF CONSTRUCTING THE HMA RESURFACING TO MEET THE PROPOSED PROFILE, CONSTRUCTING THE PROPOSED STRUCTURE TO THE LIMITS SHOWN, REMOVAL OF ANY PAVEMENT NECESSARY TO COMPLETE THE STRUCTURE REMOVAL, PLACING THE PROPOSED SPBGR-TA, RECONSTRUCTING LONE STAR ROAD, AND REMOVAL OF THE TEMPORARY SIDEROAD AND HAUL ROAD.
- 2. THE TEMPORARY SIDEROAD SHALL BE MAINTAINED ACCORDING TO SECTION 402 OF THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION AND TO THE SATISFACTION OF THE RESIDENT ENGINEER. THE HAUL ROAD WILL BE MAINTAINED ACCORDING TO THE NOTES INCLUDED IN THE HAUL ROAD DETAILS.
- 3. TRAFFIC CONTROL FOR THIS WORK SHALL BE IN ACCORDANCE WITH THE APPLICABLE PORTIONS OF TRAFFIC CONTROL AND PROTECTION, STANDARD 701321 (SPECIAL). ANY ADDITIONAL SIGNING OR TRAFFIC CONTROL DEVICES SHOWN ON THE STAGE CONSTRUCTION PLANS SHALL BE CONSIDERED AS INCLUDED IN THE APPLICABLE TRAFFIC CONTROL AND PROTECTION STANDARD.

NOTES:

- 1. THE BOTTOM 6" OF THE TEMPORARY CONCRETE BARRIER SHALL BE PAINTED WITH TEMPORARY PAVEMENT MARKING "YELLOW". THE COST FOR THIS SHALL BE CONSIDERED AS INCLUDED IN THE COST OF TEMPORARY CONCRETE BARRIER.
- 2. ALL CONFLICTING PAVEMENT MARKING SHALL BE REMOVED PRIOR TO PLACING PAVEMENT MARKING NECESSARY FOR STAGE CONSTRUCTION. THE COST FOR THIS SHALL BE INCLUDED IN THE APPLICABLE TRAFFIC CONTROL AND PROTECTION STANDARD.
- 3. THE CONTRACTOR WILL NOT BE ALLOWED THE OPTION OF USING SAND MODULE IMPACT ATTENUATORS FOR THIS PROJECT.
- 4. THIS PROJECT WILL REQUIRE TEMPORARY RUMBLE STRIP.

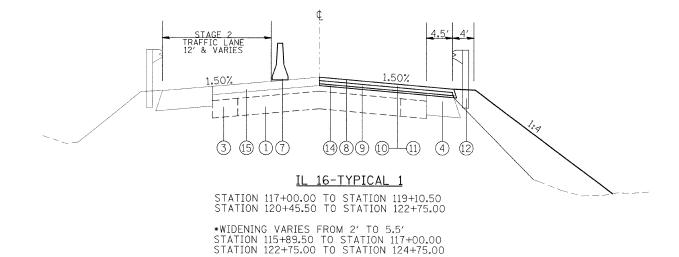

LEGEND

- (1) EXISITNG PCC PAVEMENT
- (2) EXISITNG HOT-MIX ASPHALT RESURFACING 3"
- (3) EXISITING HOT-MIX ASPHALT BASE COURSE WIDENING 8"
- (4) BASE COURSE WIDENING FROM STAGE 1A 10"
- (5) PROPOSED AGGREGATE FOR TEMPORARY ACCESS-9"
- (6) EXISTING LONE STAR (ROAD DEPTH) UNKNOWN-A1 SURFACE
- (7) TEMPORARY CONCRETE BARRIER
- (8) PROPOSED HMA SURFACE SOURSE-1 1/2"
- (9) PROPOSED HMA BINDER COURSE 1" AND VARIES
- (10) PROPOSED BITUMINOUS MATERIALS (PRIME COAT)
- (11) PROPOSED AGGREGATE PRIME COAT
- (12) PROPOSED SPBGR-TA
- (13) BASE COURSE WIDENING FROM PREVIOUS STAGE-10"
- (14) PROPOSED LEVELING BINDER (MACHINE METHOD) 3/4"
- (15) RESURFACING PLACED IN PREVIOUS STAGE

FILE NAME =	USER NAME = manntm	DESIGNED -	REVISED -			STAGE II CONSTRUCTION		F.A.P.	SECTION	COUNTY	TOTAL SHEET
o:\pw_work\pwidot\manntm\dms51935\pln02	806a.dgn	DRAWN -	REVISED -	STATE OF ILLINOIS		STAGE II CONSTRUCTION		325	3BP=2	JERSEY	90 33
	PLOT SCALE = 20.00000 '/ IN.	CHECKED -	REVISED -	DEPARTMENT OF TRANSPORTATION				1 323	CONTRACT NO. 76B01		
·	PLOT DATE = 12/11/2008	DATE ~	REVISED -		SCALE:	SHEET NO. 9 OF 12 SHEETS STA.	TO STA.	FED. ROAD D	IST. NO. 8 ILLINOIS FE	D. AID PROJECT	71 NO. 10BOI
