
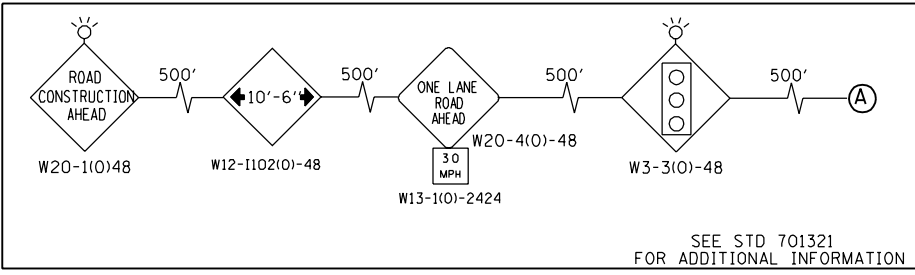


FILE NAME : F:\2010\VE\10010.PT\154-23.WHKS\CADD\Bases\264E08-SHT_5stage22_20.dgn
 USER : JLN
 MILLENNIA PROFESSIONAL SERVICES

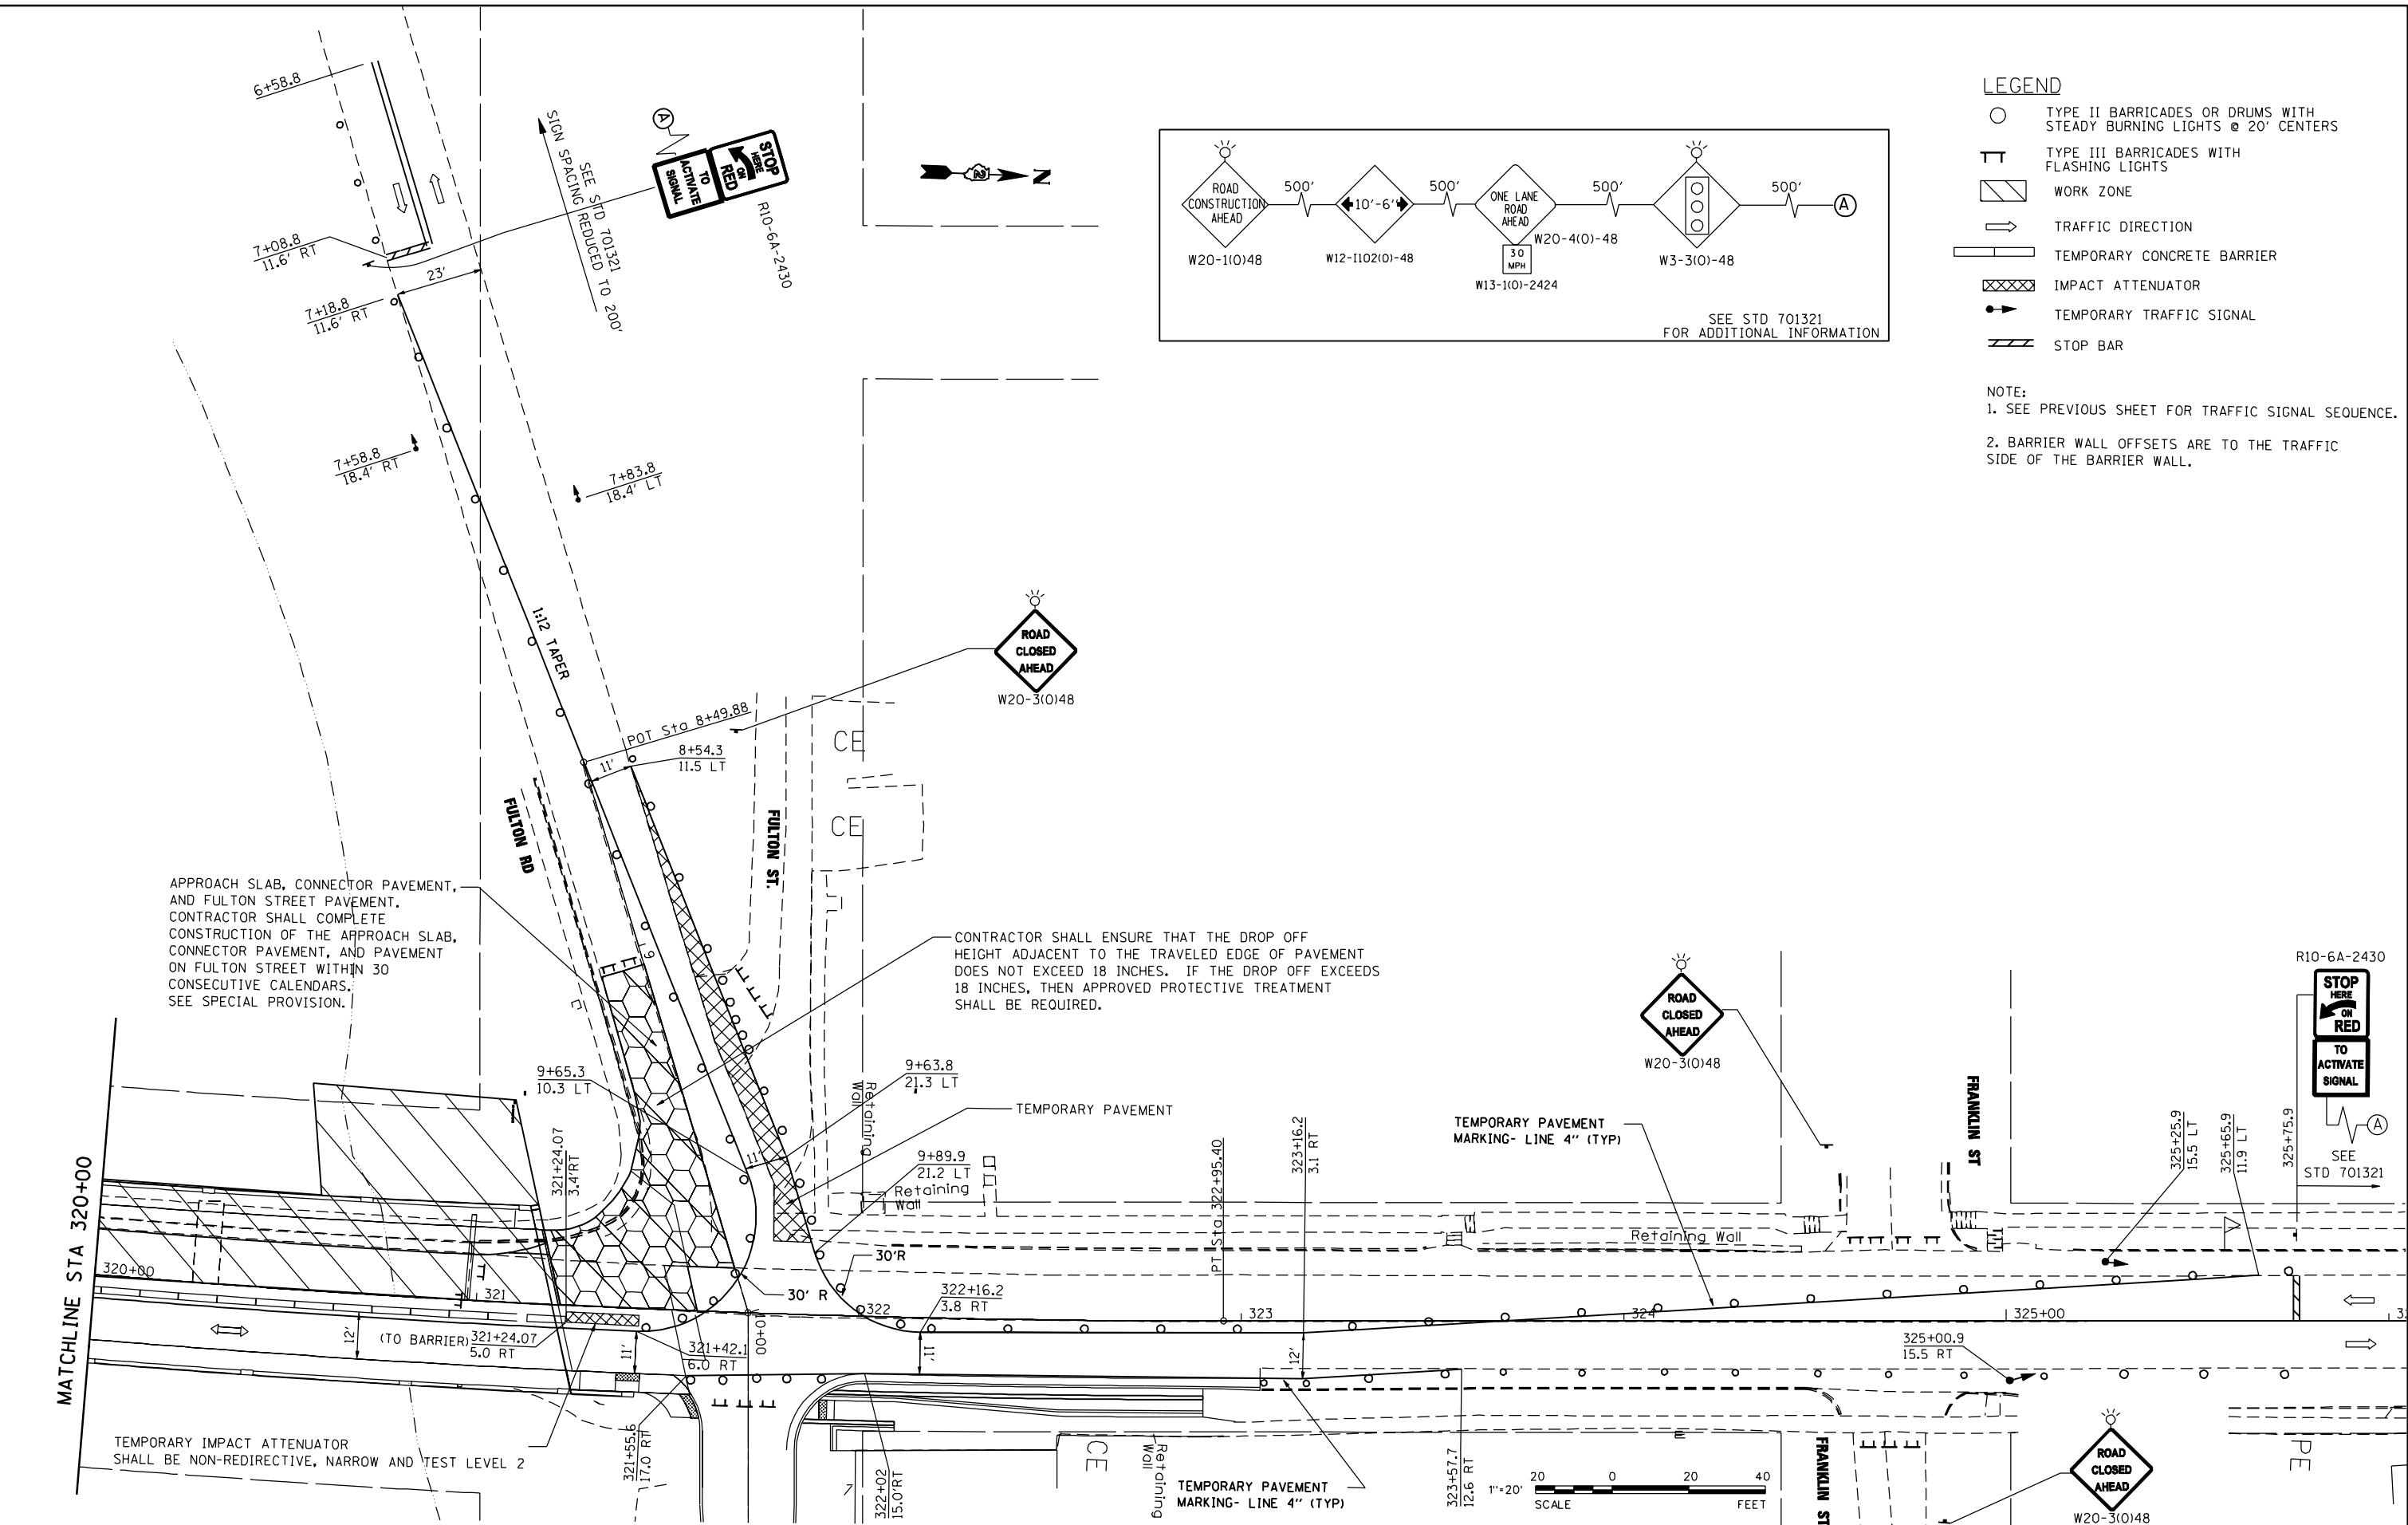

- LEGEND**
- TYPE II BARRICADES OR DRUMS WITH STEADY BURNING LIGHTS @ 20' CENTERS
 - ⊥ TYPE III BARRICADES WITH FLASHING LIGHTS
 - ▨ WORK ZONE
 - TRAFFIC DIRECTION
 - ▬ TEMPORARY CONCRETE BARRIER
 - ▩ IMPACT ATTENUATOR
 - ⬇ TEMPORARY TRAFFIC SIGNAL
 - ▬ STOP BAR
- NOTE:**
- SEE PREVIOUS SHEET FOR TRAFFIC SIGNAL SEQUENCE.
 - BARRIER WALL OFFSETS ARE TO THE TRAFFIC SIDE OF THE BARRIER WALL.

APPROACH SLAB, CONNECTOR PAVEMENT, AND FULTON STREET PAVEMENT. CONTRACTOR SHALL COMPLETE CONSTRUCTION OF THE APPROACH SLAB, CONNECTOR PAVEMENT, AND PAVEMENT ON FULTON STREET WITHIN 30 CONSECUTIVE CALENDARS. SEE SPECIAL PROVISION.

CONTRACTOR SHALL ENSURE THAT THE DROP OFF HEIGHT ADJACENT TO THE TRAVELED EDGE OF PAVEMENT DOES NOT EXCEED 18 INCHES. IF THE DROP OFF EXCEEDS 18 INCHES, THEN APPROVED PROTECTIVE TREATMENT SHALL BE REQUIRED.

TEMPORARY IMPACT ATTENUATOR SHALL BE NON-REDIRECTIVE, NARROW AND TEST LEVEL 2

MILLENNIA PROFESSIONAL SERVICES
 2600 Warrenville Road, Suite 203, Downers Grove, IL 60515-1761
 630.705.0110 voice, 630.839.3566 fax
 www.mps-il.com

DESIGNED - TVN	REVISED -
DRAWN - TVN/BB	REVISED -
CHECKED - MG	REVISED -
DATE - 8/2/2013	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**IL ROUTE 84
OVER APPLE RIVER**

**STAGES OF CONSTRUCTION
& TRAFFIC CONTROL
STAGE II**

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
308	103BR-4	JO DAVIESS	159	35
CONTRACT NO. 64E08				

SCALE: 1"=20' SHEET NO. OF SHEETS STA. TO STA.
