




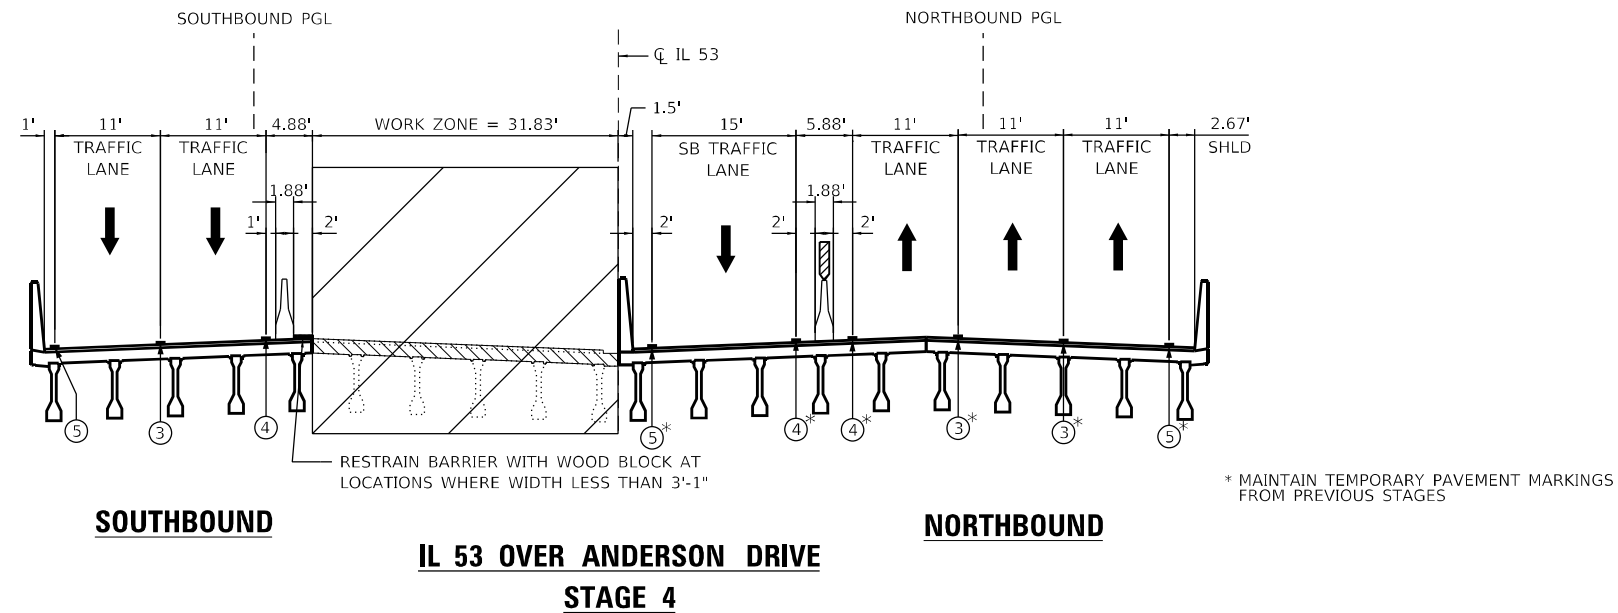

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
- (B) EXISTING PAVEMENT MARKING 4" WHITE
- (C) EXISTING PAVEMENT MARKING 5" WHITE DASH-SKIP
- (1) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- (2) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- (3) TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH - 30' SKIP

- (4) TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- (5) TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
- (6) PERMANENT PAVEMENT MARKINGS. SEE PAVEMENT MARKING PLAN
- (7) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- (8) TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE
- (9) TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED

- ↑ DIRECTION OF TRAFFIC FLOW
- TEMPORARY CONCRETE BARRIER
- TEMPORARY CONCRETE BARRIER - PINNED
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
- WORK ZONE
- MODULAR GLARE SCREEN SYSTEM, TEMPORARY

MODEL: Default
FILE: \\na11c6-001\wsp-cs-pw-bentley.com\usps4-cs-pw-illinois\Documents\Project: E2N9-IL 53 Bridge\CAD Sheets\163W38-01t-01g10-cv\cvt-21-IL 53W38.dgn





USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 20,0000 * / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL TYPICAL SECTION

SCALE: NTS SHEET 21 OF 33 SHEETS STA. TO STA.


F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	202
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				



	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL TYPICAL SECTION					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 20,0000' = 1 in.	DRAWN - MM	REVISED -							342	(531) BR 23	COOK	1211	203
	PLOT DATE = 9/25/2024	CHECKED - TC	REVISED -		CONTRACT NO. 62W38									
		DATE - 8/23/2024	REVISED -		SCALE: NTS	SHEET 22 OF 33 SHEETS	STA.	TO STA.	ILLINOIS	FED. AID PROJECT				



	DIRECTION OF TRAFFIC FLOW
	TEMPORARY CONCRETE BARRIER
	TEMPORARY CONCRETE BARRIER - PINNED
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
	WORK ZONE

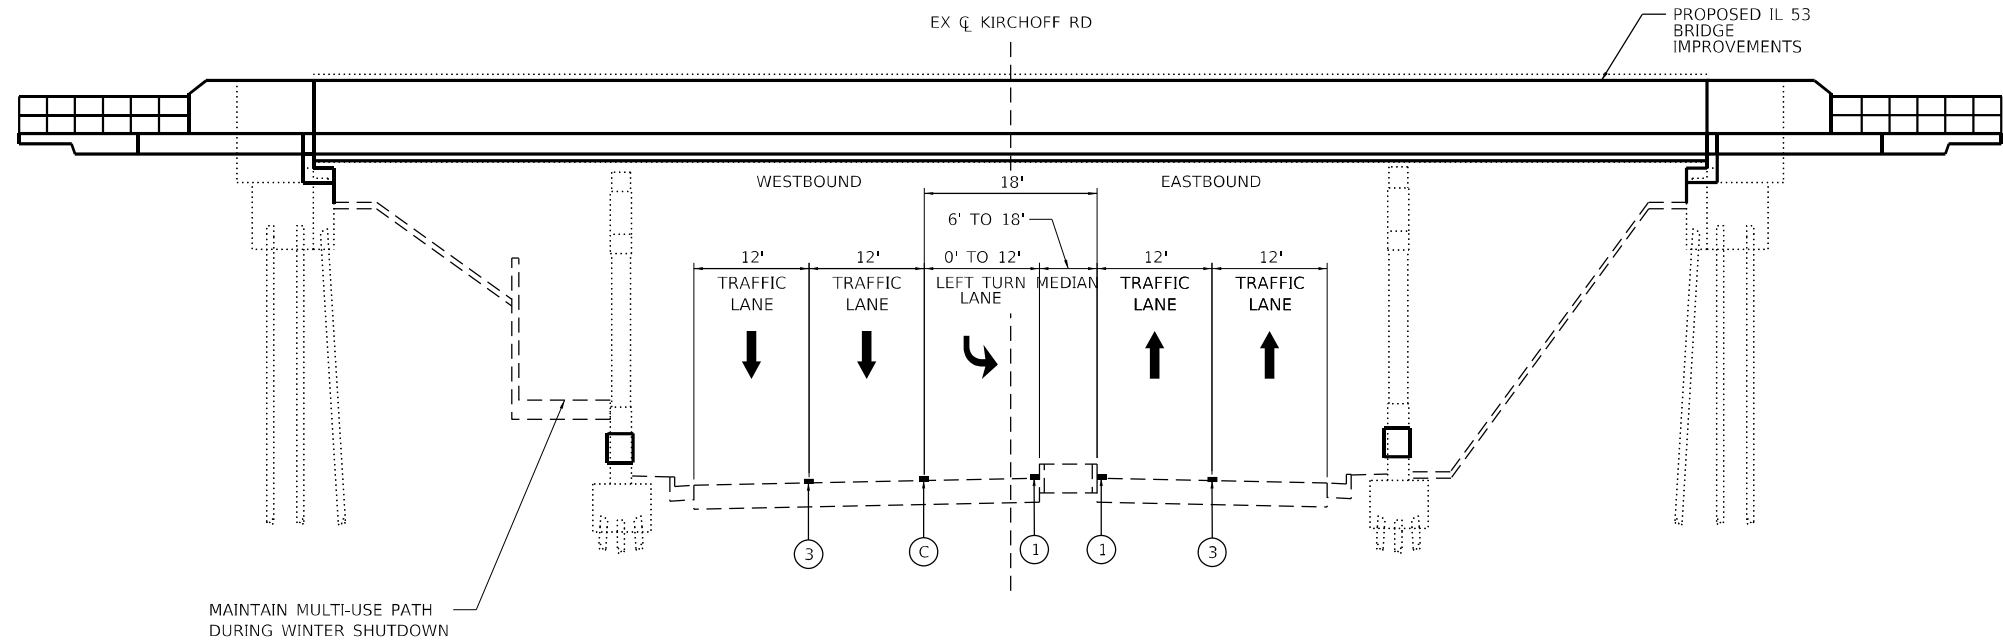

KIRCHOFF ROAD AT IL 53
WINTER SHUTDOWN
STA. 306+45.63 TO STA. 309+54.24

LEGEND

(A) EXISTING PAVEMENT MARKING 4" YELLOW

(B) EXISTING PAVEMENT MARKING 4" WHITE

(C) EXISITNG PAVEMENT MARKING 4", 2' DASH - 6' SKIP

(D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP

(E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP

(1) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW

(2) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE

(3) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 10' DASH - 30' SKIP

(4) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW (DOUBLE YELLOW)

(5) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 2' DASH - 6' SKIP

DIRECTION OF TRAFFIC FLOW

TEMPORARY CONCRETE BARRIER

TEMPORARY CONCRETE BARRIER - PINNED

TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT


WORK ZONE

MODEL: Default
FILE: N:\MISC - 2024\wsp-je-pw-bentley.com\usps4-je-pw-ill\Documents\Project_62W38-24\bridge-cad-sheet\162W38-24-bridge-cad-sheet-24-kirchoff-53.dgn

	USER NAME = USTC714594		DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	KIRCHOFF ROAD TRAFFIC CONTROL TYPICAL SECTION		F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
			DRAWN - MM	REVISED -				342	(531) BR 23	COOK	1211	205
	PLOT SCALE = 20,0000' = 1" / in.		CHECKED - TC	REVISED -				CONTRACT NO. 62W38				
	PLOT DATE = 9/25/2024		DATE - 8/23/2024	REVISED -		SCALE: NTS	SHEET 24 OF 33 SHEETS	STA.	TO STA.	ILLINOIS FED. AID PROJECT		



	DIRECTION OF TRAFFIC FLOW
	TEMPORARY CONCRETE BARRIER
	TEMPORARY CONCRETE BARRIER - PINNED
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
	WORK ZONE

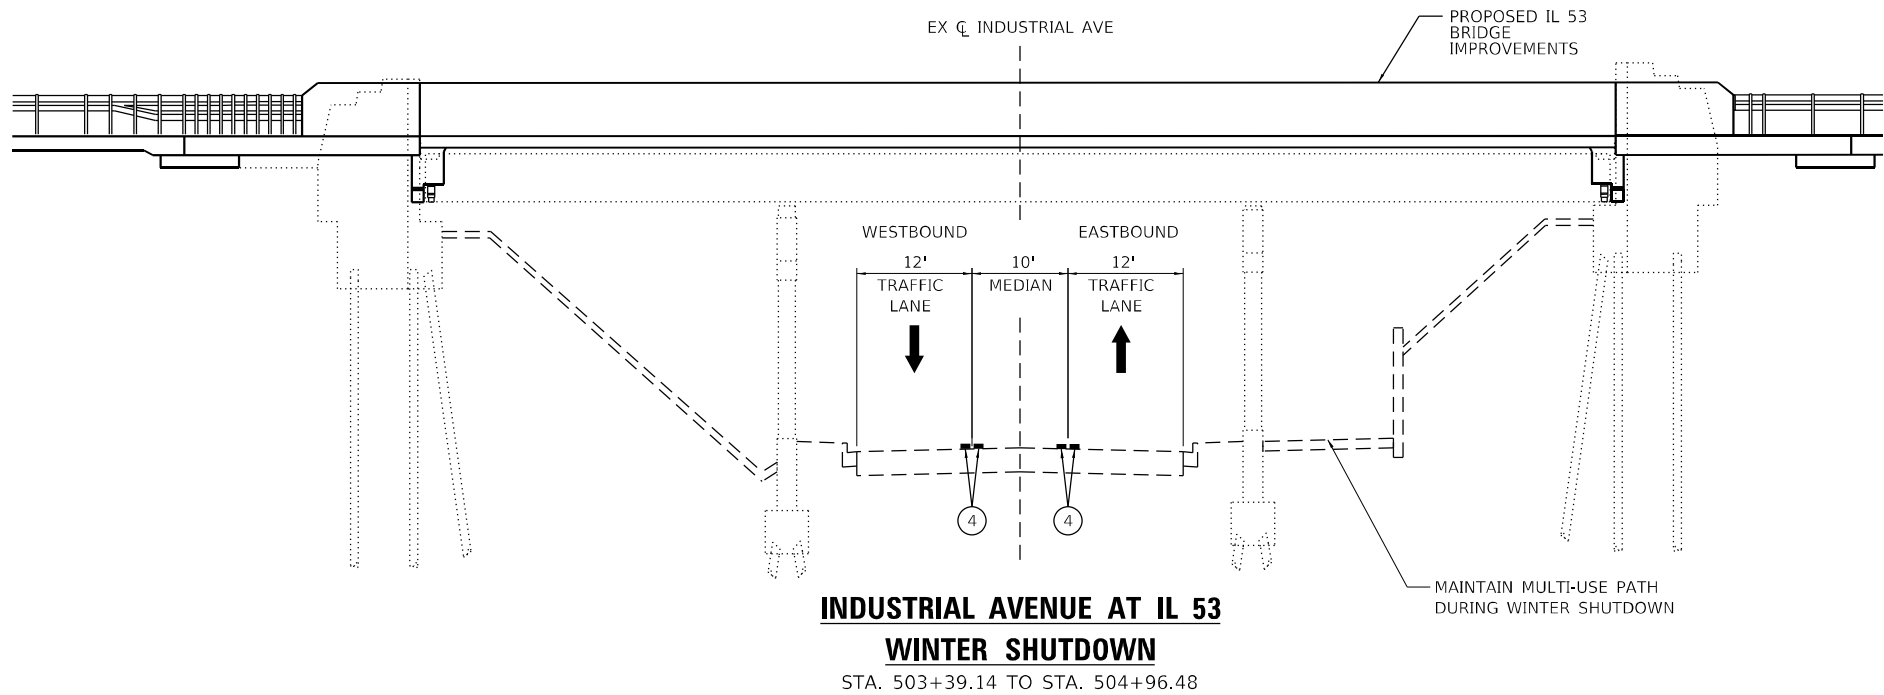

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
(B) EXISTING PAVEMENT MARKING 4" WHITE
(C) EXISITNG PAVEMENT MARKING 4", 2' DASH - 6' SKIP
(D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
(E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
(1) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
(2) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
(3) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 10' DASH - 30' SKIP
(4) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW (DOUBLE YELLOW)
(5) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 2' DASH - 6' SKIP



DIRECTION OF TRAFFIC FLOW




TEMPORARY CONCRETE BARRIER



TEMPORARY CONCRETE BARRIER - PINNED



TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT



WORK ZONE

MODEL: Default
FILE: \\wsp-cs-pw-bentley.com\wsp-cs-pw-ill\Documents\Project: 62W38-26-Industrial\WSP.dgn



USER NAME	= USTC714594
PLOT SCALE	= 20,0000 * / in.
PLOT DATE	= 9/25/2024

DESIGNED -	MM
DRAWN -	MM
CHECKED -	TC
DATE -	8/23/2024

REVISED -	
REVISED -	
REVISED -	
REVISED -	


STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

INDUSTRIAL AVENUE
TRAFFIC CONTROL TYPICAL SECTION

SCALE: NTS SHEET 26 OF 33 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	207
CONTRACT NO. 62W38				
		ILLINOIS	FED. AID PROJECT	

MODEL: Default
FILE NAME: g:\wsp\cpepw\benley.com\uspc4-e-pw-ill\Documents\Project E2N91-IL 53 Bridge\CAD_Sheets\163W38-ohr-rtb\trfco-typical-27-NW Hwy-53.dgn

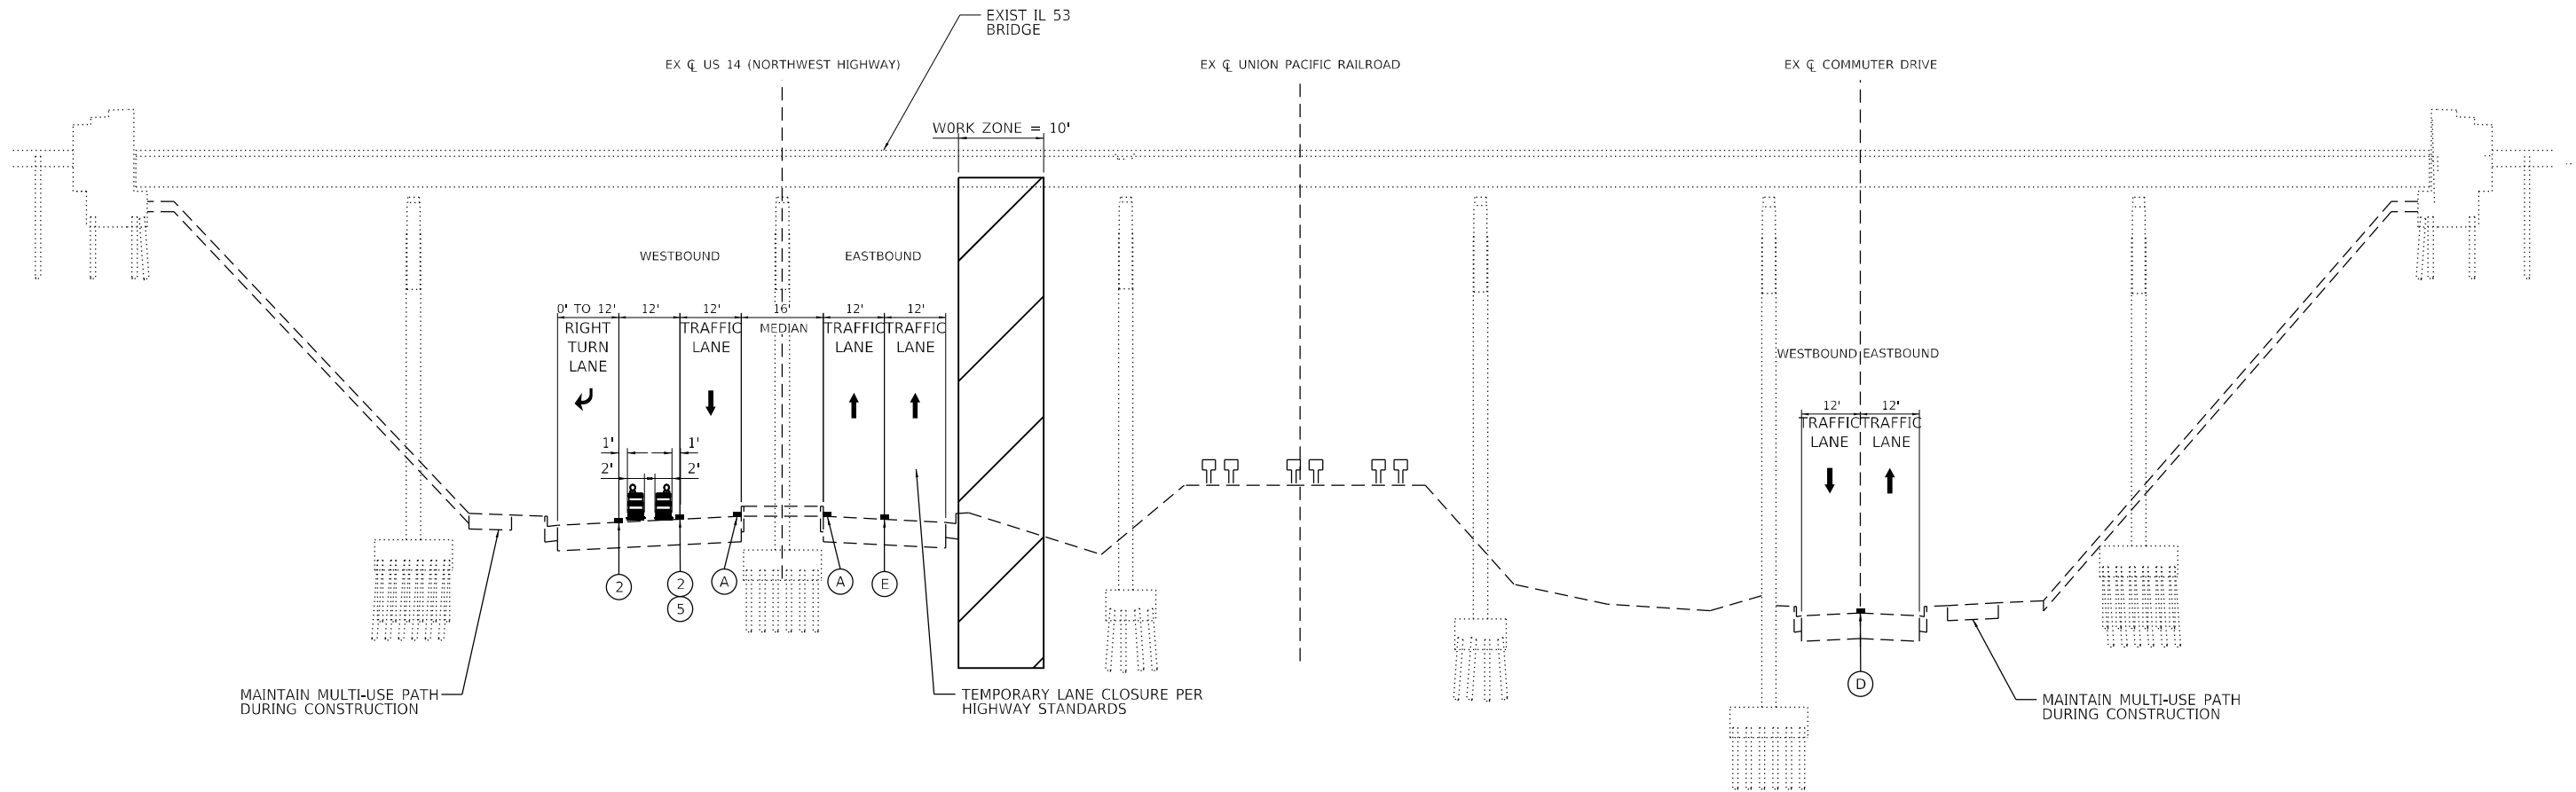

**US 14 (NORTHWEST HIGHWAY), COMMUTER DRIVE,
& UNION PACIFIC RAILROAD AT IL 53
STAGE 1**

US 14 (NORTHWEST HIGHWAY) STA. 608+76.64 TO STA. 611+22.66
COMMUTER DRIVE STA. 921+44.87 TO STA. 923+34.48

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
- (B) EXISTING PAVEMENT MARKING 4" WHITE
- (C) EXISTING PAVEMENT MARKING 4", 2' DASH - 6' SKIP
- (D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
- (E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
- (1) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- (2) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- (3) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, 10' DASH - 30' SKIP
- (4) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW (DOUBLE YELLOW)

-  DIRECTION OF TRAFFIC FLOW
-  TEMPORARY CONCRETE BARRIER
-  TEMPORARY CONCRETE BARRIER - PINNED
-  TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
-  WORK ZONE



USER NAME = USTC714594
PLOT SCALE = 20,0000 * / in.
PLOT DATE = 9/25/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024

REVISED -
REVISED -
REVISED -
REVISED -


**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**US 14 (NW HIGHWAY), COMMUTER DRIVE, & UNION PACIFIC RR
TRAFFIC CONTROL TYPICAL SECTION**

SCALE: NTS SHEET 27 OF 33 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	208
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

MODEL: Default
FILE: \\nslc-pw-wsp-cs-pw-bentley.com\usps4-cs-pw-ill\Documents\Project: 62W38-01-01\Drawings\Typical-29-NW Hwy-15SP.dgn

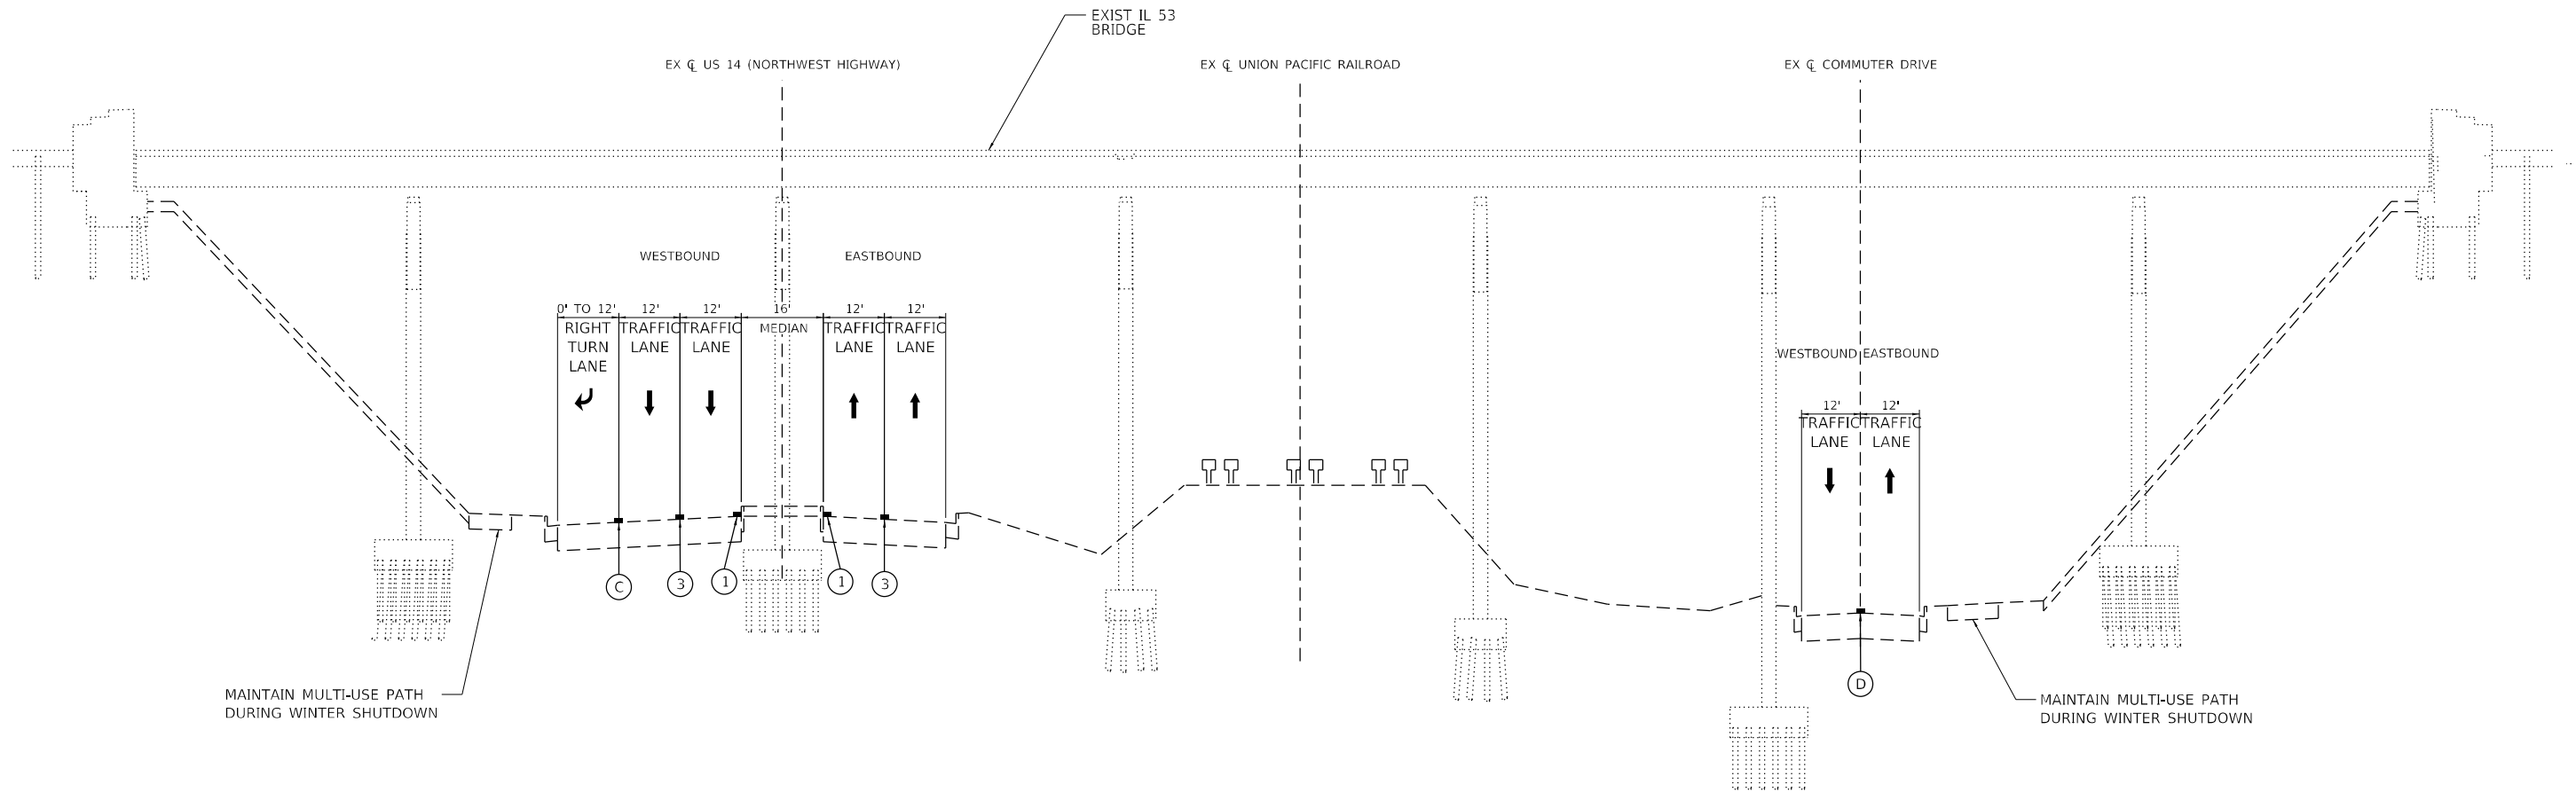

**US 14 (NORTHWEST HIGHWAY), COMMUTER DRIVE,
& UNION PACIFIC RAILROAD AT IL 53
WINTER SHUTDOWN**

US 14 (NORTHWEST HIGHWAY) STA. 608+76.64 TO STA. 611+22.66
COMMUTER DRIVE STA. 921+44.87 TO STA. 923+34.48

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
- (B) EXISTING PAVEMENT MARKING 4" WHITE
- (C) EXISTING PAVEMENT MARKING 4", 2' DASH - 6' SKIP
- (D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
- (E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
- (1) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
- (2) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
- (3) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 10' DASH - 30' SKIP
- (4) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW (DOUBLE YELLOW)
- (5) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 2' DASH - 6' SKIP

-  DIRECTION OF TRAFFIC FLOW
-  TEMPORARY CONCRETE BARRIER
-  TEMPORARY CONCRETE BARRIER - PINNED
-  TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
-  WORK ZONE



USER NAME = USTC714594
PLOT SCALE = 20,0000 * / in.
PLOT DATE = 9/23/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024

REVISED -
REVISED -
REVISED -
REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**


**US 14 (NW HIGHWAY), COMMUTER DRIVE, & UNION PACIFIC RR
TRAFFIC CONTROL TYPICAL SECTION**

SCALE: NTS SHEET 29 OF 33 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	210
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				



	DIRECTION OF TRAFFIC FLOW
	TEMPORARY CONCRETE BARRIER
	TEMPORARY CONCRETE BARRIER - PINNED
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
	WORK ZONE

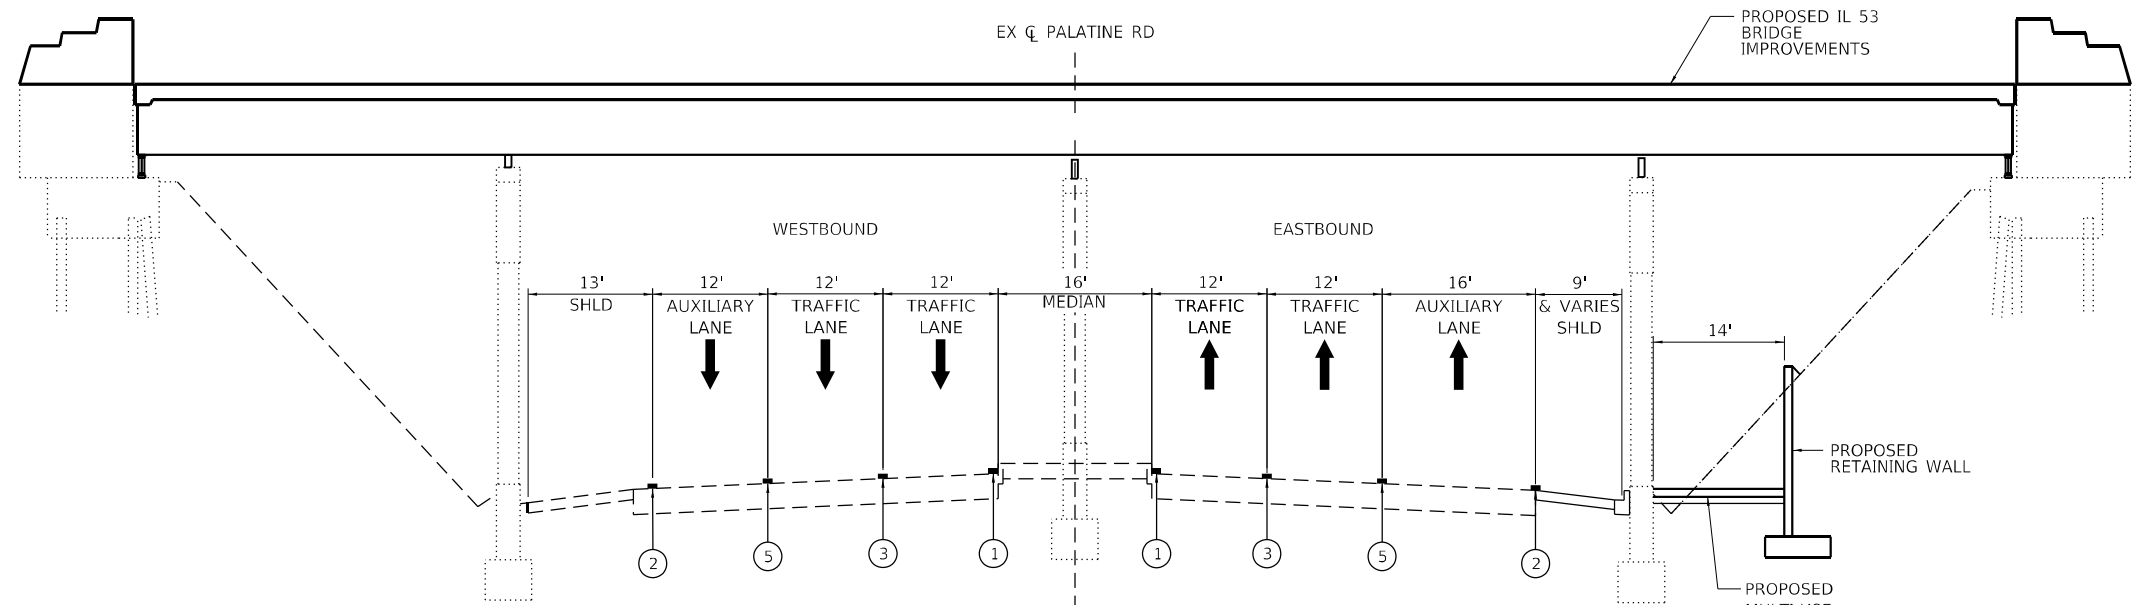

PALATINE ROAD AT IL 53
WINTER SHUTDOWN
STA. 818+06.10 TO STA. 819+92.74

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
- (B) EXISTING PAVEMENT MARKING 4" WHITE
- (C) EXISTING PAVEMENT MARKING 4", 2' DASH - 6' SKIP
- (D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
- (E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
- (1) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
- (2) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
- (3) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 10' DASH - 30' SKIP
- (4) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW (DOUBLE YELLOW)
- (5) TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 2' DASH - 6' SKIP

- DIRECTION OF TRAFFIC FLOW
- TEMPORARY CONCRETE BARRIER
- TEMPORARY CONCRETE BARRIER - PINNED
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
- WORK ZONE

MODEL: Default
FILE: \\wsp-cs-pw-bentley.com\wsp-cs-pw-ill\Documents\Project_62W38-01\Drawings\Typical-31-Palatine-WSP.dgn



USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 20,0000 * / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -


STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

PALATINE ROAD
TRAFFIC CONTROL TYPICAL SECTION

SCALE: NTS SHEET 31 OF 33 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	212
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				


MODEL: Default
FILE: \\nautilus-prod-wsp-cs-pw-bentley.com\usps4-cs-pw-ill\Documents\Project_62W38-01r-01\typical-32-Anderson-W38.dgn

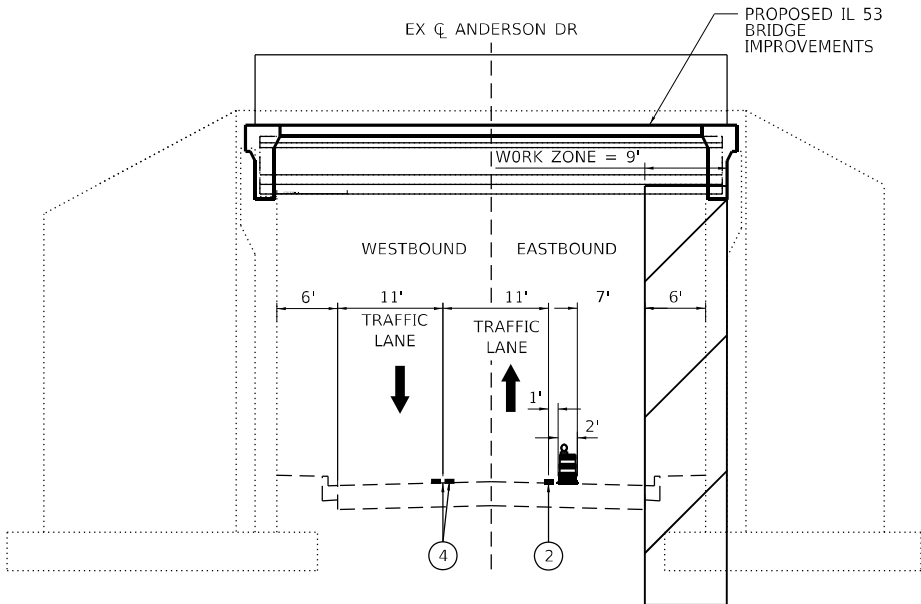

ANDERSON DRIVE AT IL 53

STAGE 1

STA. 902+43.15 TO STA. 903+64.44

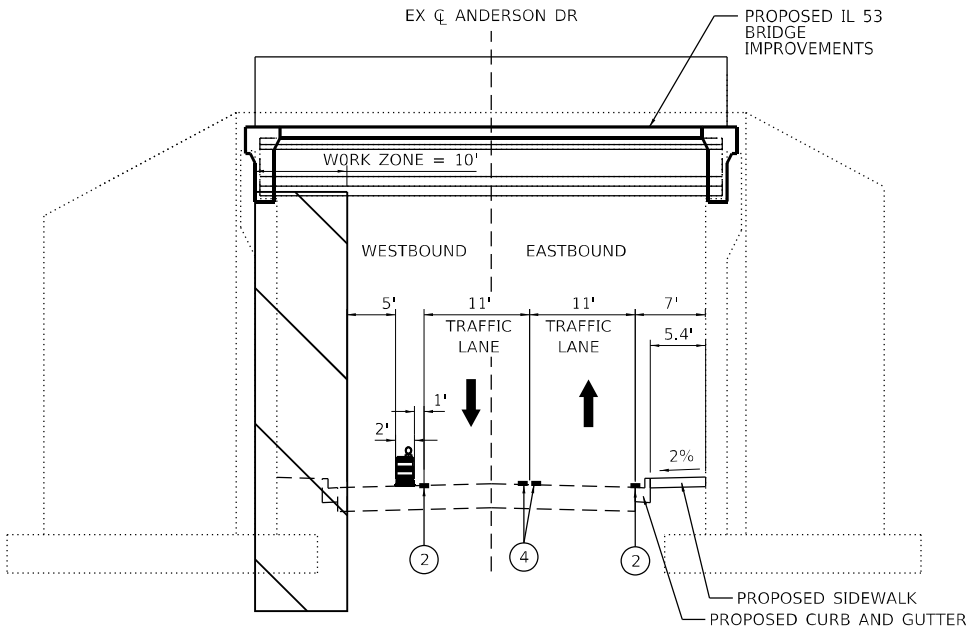

ANDERSON DRIVE AT IL 53

STAGE 2

STA. 902+35.99 TO STA. 903+57.06

LEGEND

- (A) EXISTING PAVEMENT MARKING 4" YELLOW
- (B) EXISTING PAVEMENT MARKING 4" WHITE
- (C) EXISTING PAVEMENT MARKING 4", 2' DASH - 6' SKIP
- (D) EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
- (E) EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
- (1) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- (2) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- (3) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, 10' DASH - 30' SKIP
- (4) TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW (DOUBLE YELLOW)

- DIRECTION OF TRAFFIC FLOW
- TEMPORARY CONCRETE BARRIER
- TEMPORARY CONCRETE BARRIER - PINNED
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT
- WORK ZONE



USER NAME = USTC714594
DRAWN - MM
PLOT SCALE = 20,0000 * / in.
PLOT DATE = 9/25/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024

REVISED -
REVISED -
REVISED -
REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**


**ANDERSON DRIVE
TRAFFIC CONTROL TYPICAL SECTION**

SCALE: NTS SHEET 32 OF 33 SHEETS STA. TO STA.


F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	213
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				



(A)	EXISTING PAVEMENT MARKING 4" YELLOW
(B)	EXISTING PAVEMENT MARKING 4" WHITE
(C)	EXISTING PAVEMENT MARKING 4", 2' DASH - 6' SKIP
(D)	EXISTING PAVEMENT MARKING 4" YELLOW DASH-SKIP
(E)	EXISTING PAVEMENT MARKING 4" WHITE DASH-SKIP
(1)	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
(2)	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
(3)	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 10' DASH - 30' SKIP
(4)	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW (DOUBLE YELLOW)
(5)	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, 2' DASH - 6' SKIP

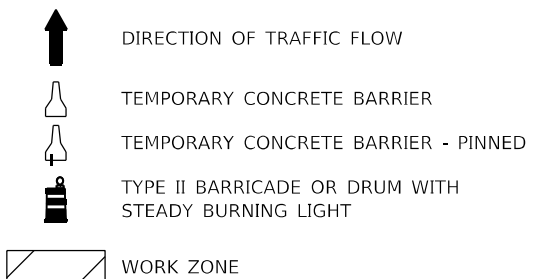



	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	ANDERSON DRIVE TRAFFIC CONTROL TYPICAL SECTION				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	214
	PLOT SCALE = 20,0000' = 1".	CHECKED - TC	REVISED -		CONTRACT NO. 62W38								
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: NTS	SHEET 33 OF 33 SHEETS	STA.	TO STA.		ILLINOIS	FED. AID PROJECT		





- NOTES**
1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

 FILE NAME: 0000	USER NAME = U5TC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE A				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,000' / in.	DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	215
	PLOT DATE = 9/25/2024	CHECKED - TC	REVISED -		CONTRACT NO. 62W38								
	DATE - 8/23/2024	REVISED -	ILLINOIS FED. AID PROJECT										
	SCALE: 1" = 50'				SHEET 1 OF 16 SHEETS	STA. 1186+00.00 TO STA. 1199+00.00							

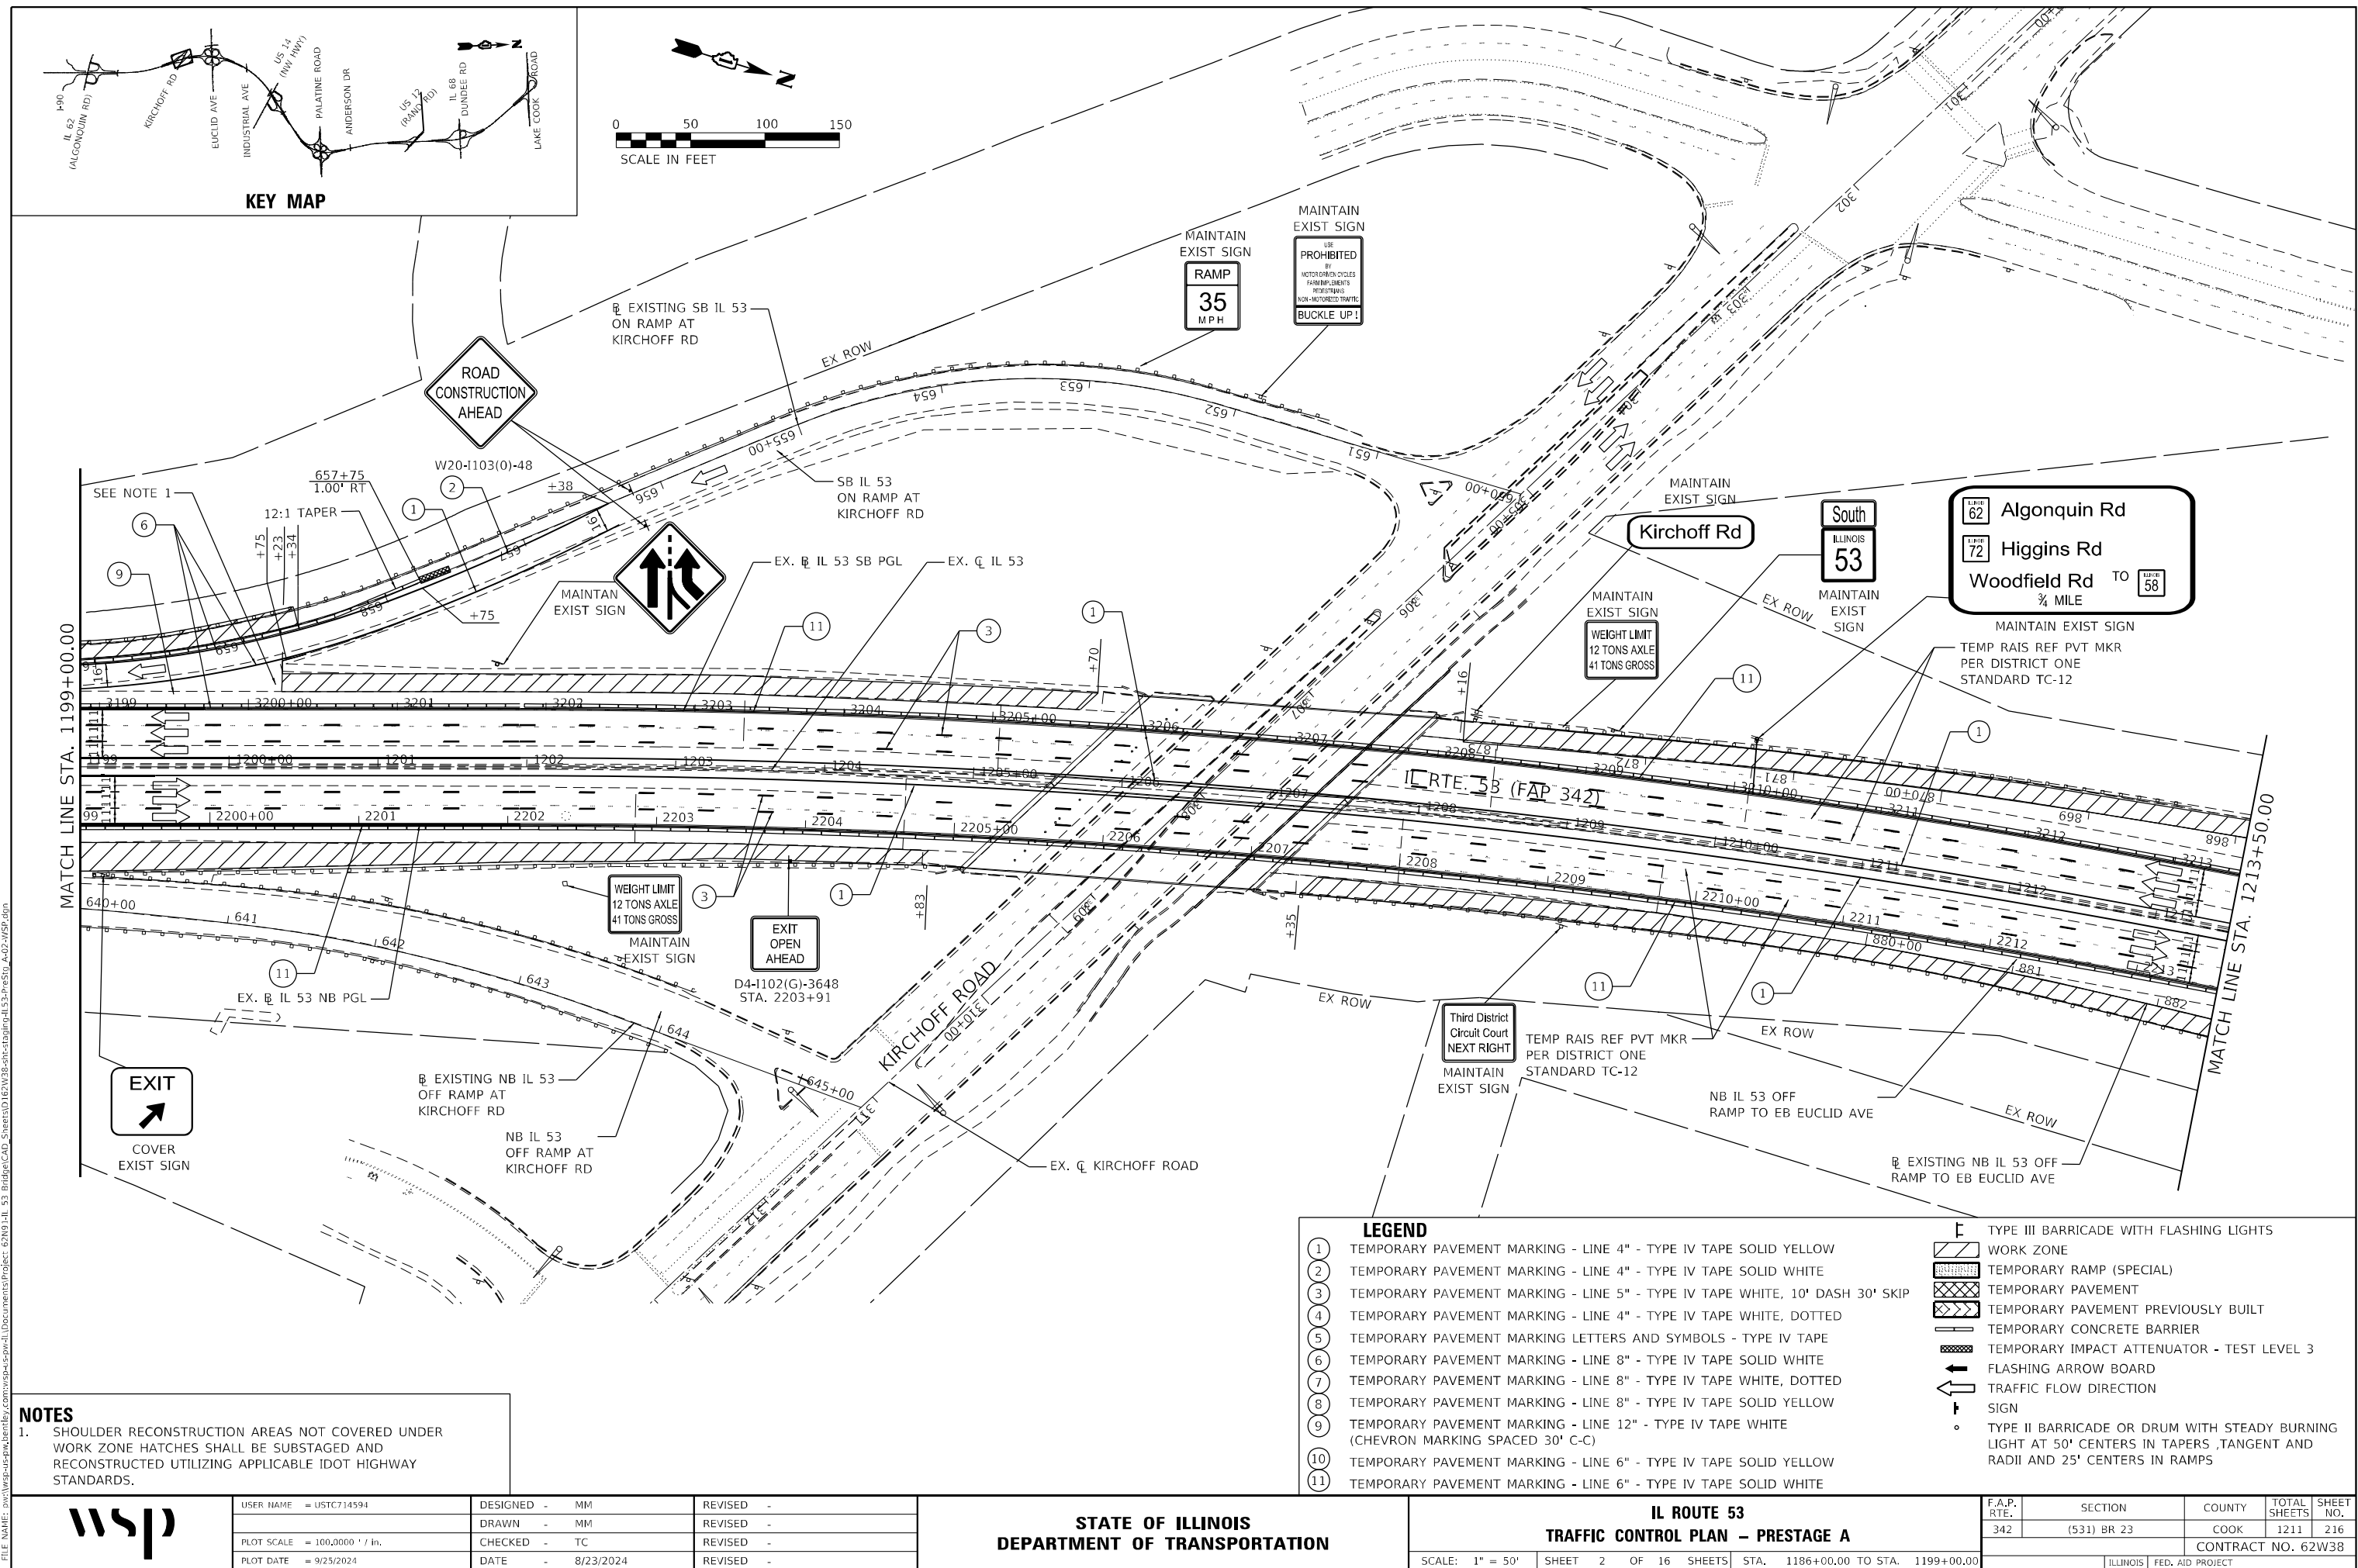




KEY MAP

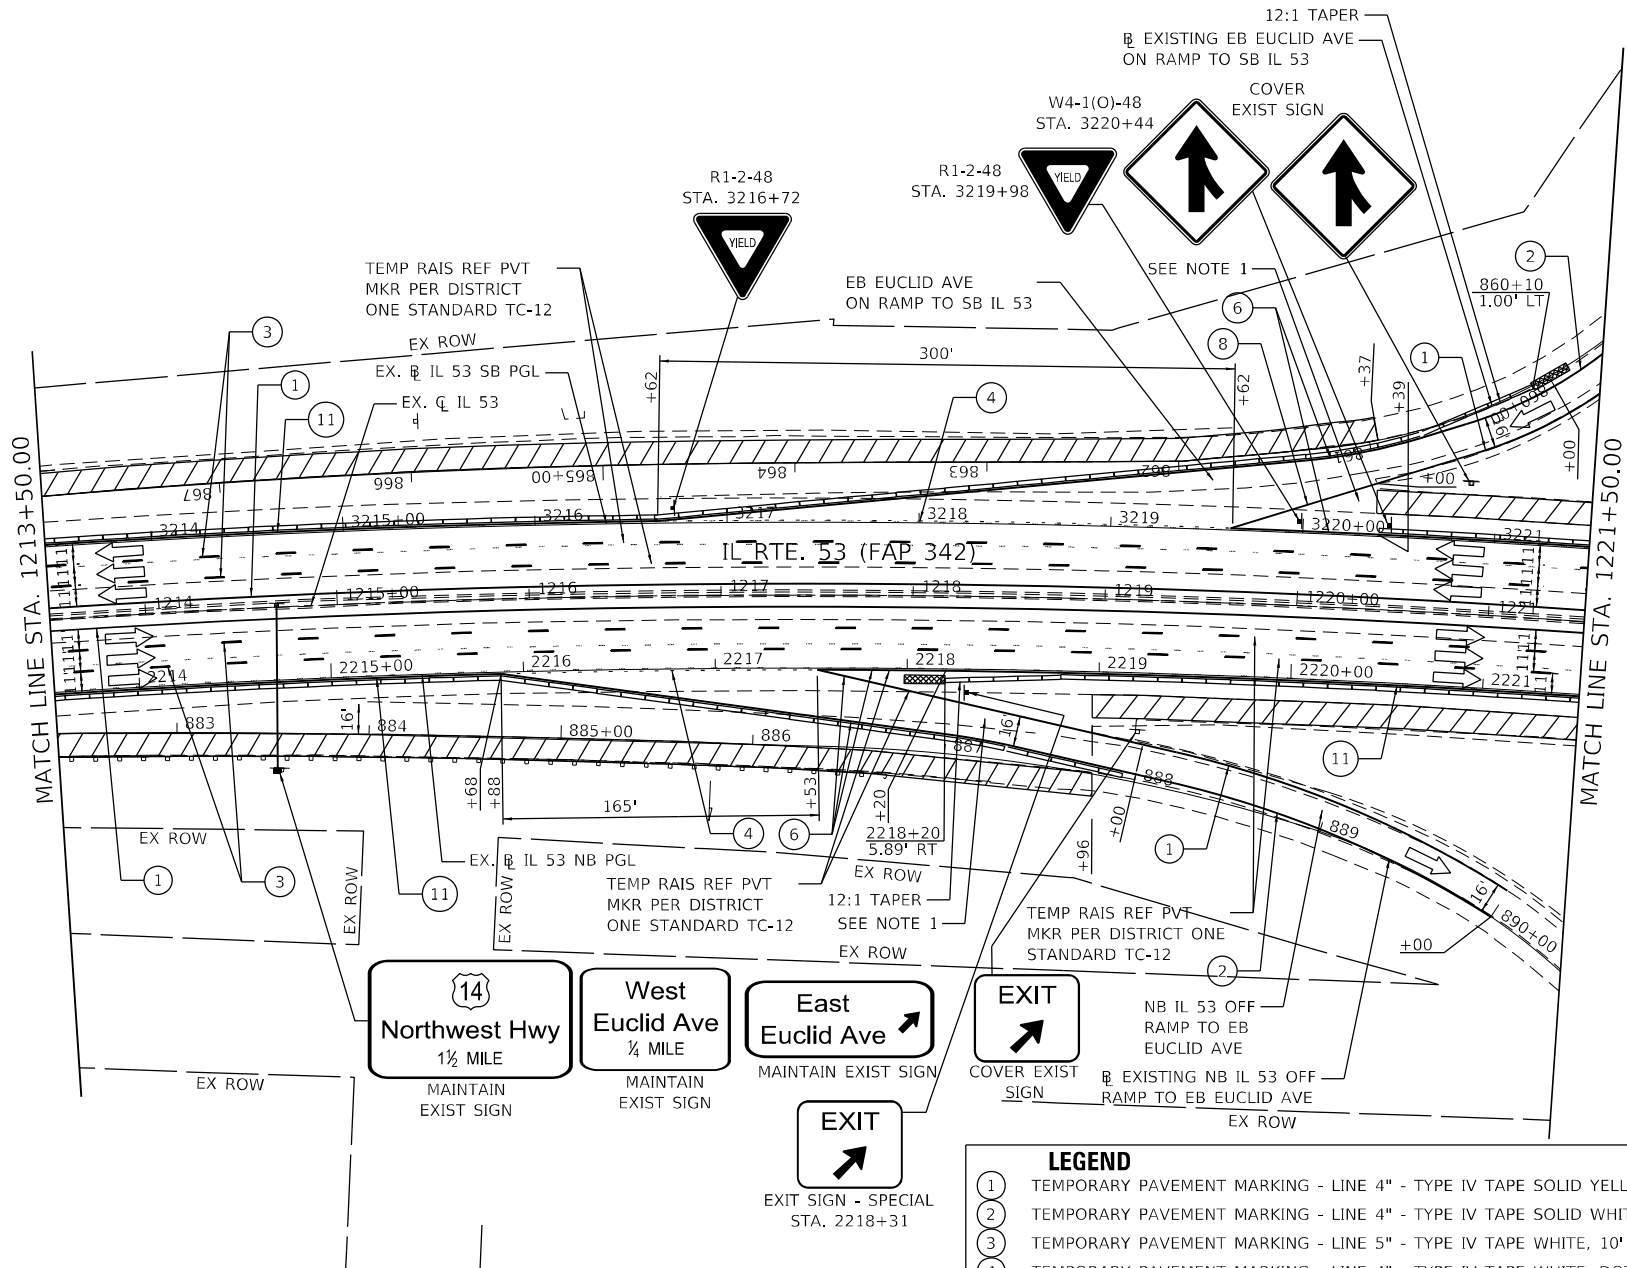



- NOTES**
- SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

- LEGEND**
- | | | |
|----|---|--|
| 1 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW | TYPE III BARRICADE WITH FLASHING LIGHTS |
| 2 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE | WORK ZONE |
| 3 | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP | TEMPORARY RAMP (SPECIAL) |
| 4 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED | TEMPORARY PAVEMENT |
| 5 | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
| 6 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE | TEMPORARY CONCRETE BARRIER |
| 7 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
| 8 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW | FLASHING ARROW BOARD |
| 9 | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C) | TRAFFIC FLOW DIRECTION SIGN |
| 10 | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |
| 11 | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE | |

	USER NAME = USTC714594		DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - PRESTAGE A		F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	DRAWN - MM		REVIS	REVISED -		SCALE: 1" = 50'		342	(531) BR 23	COOK	1211	217
	PLOT SCALE = 100,0000 ' / in.		CHECKED - TC	REVISED -		SHEET 3 OF 16 SHEETS		CONTRACT NO. 62W38				
	PLOT DATE = 9/23/2024		DATE - 8/23/2024	REVISED -		STA. 1213+50.00 TO STA. 1221+50.00		ILLINOIS FED. AID PROJECT				

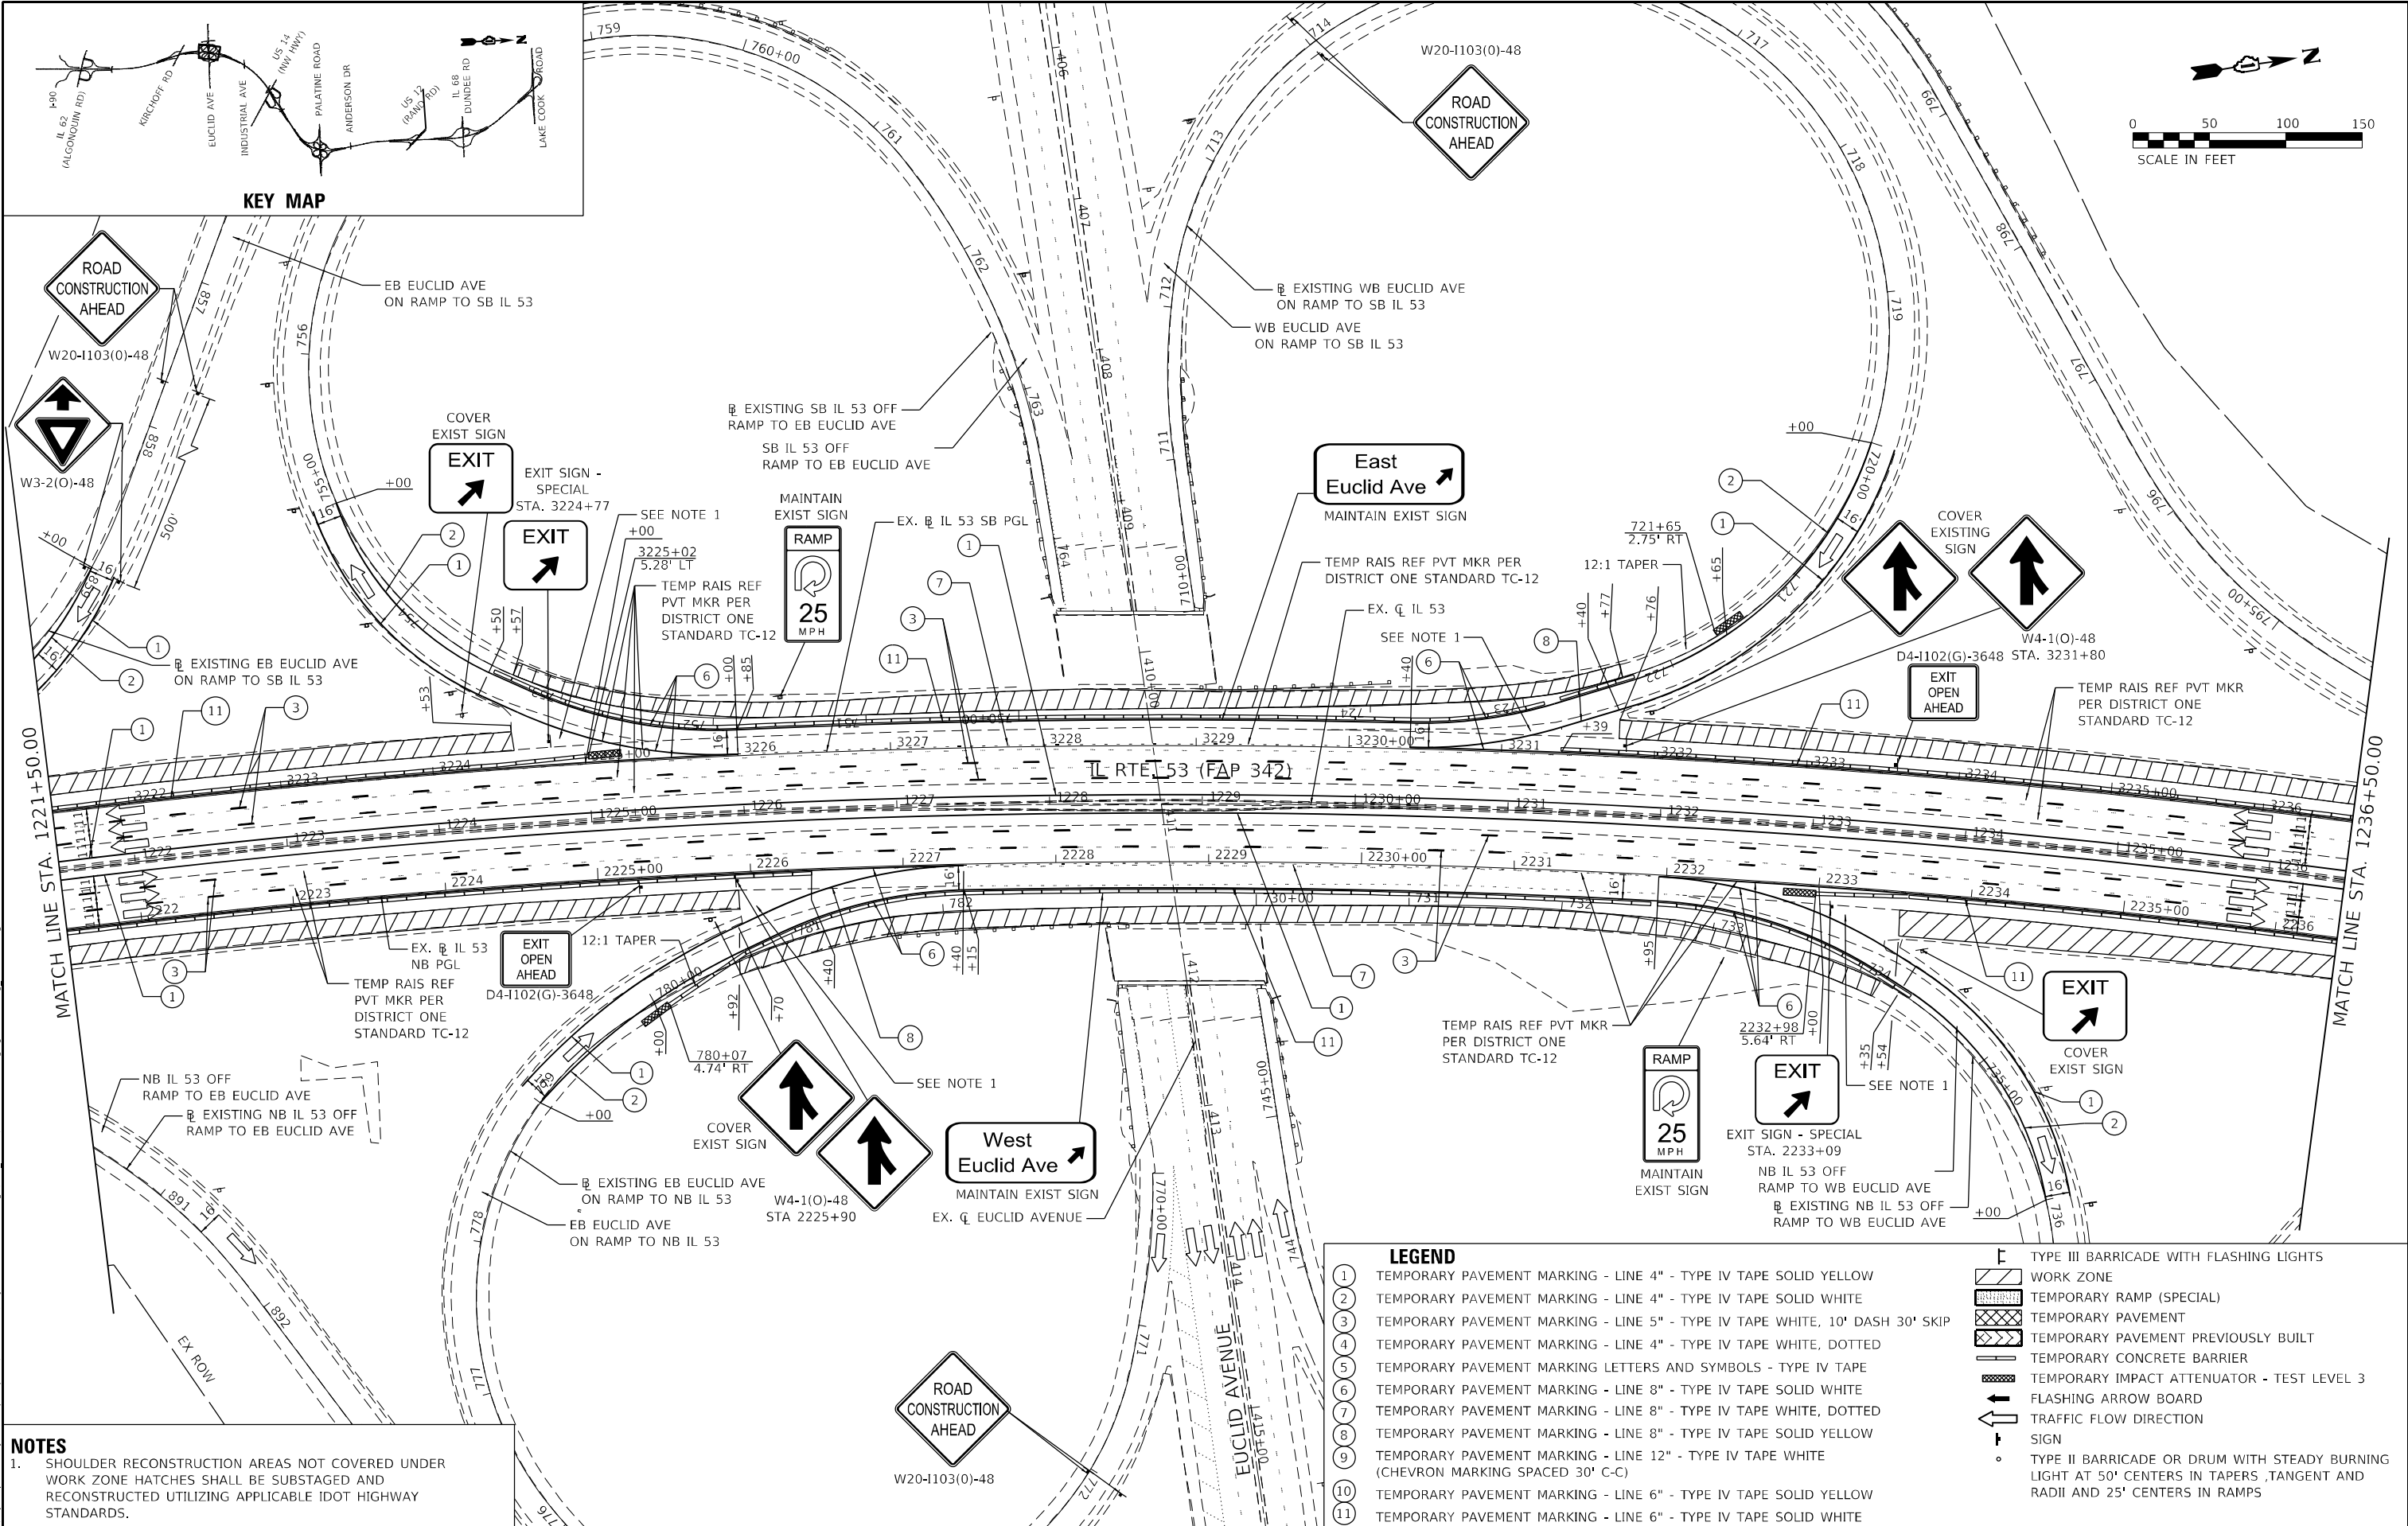

KEY MAP



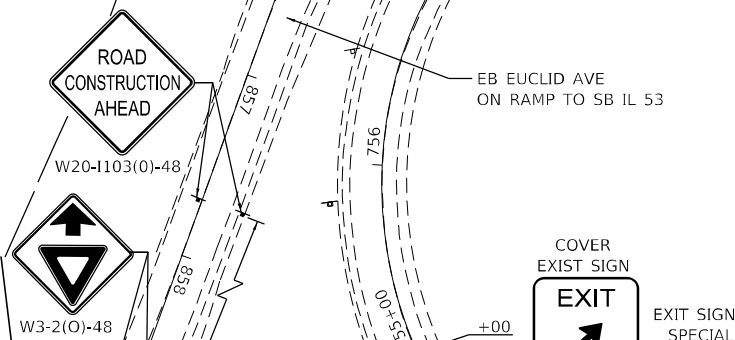


NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	TYPE III BARRICADE WITH FLASHING LIGHTS
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE	WORK ZONE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP	TEMPORARY RAMP (SPECIAL)
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY PAVEMENT
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE	TEMPORARY PAVEMENT PREVIOUSLY BUILT
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE	TEMPORARY CONCRETE BARRIER
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW	FLASHING ARROW BOARD
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)	TRAFFIC FLOW DIRECTION SIGN
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE	

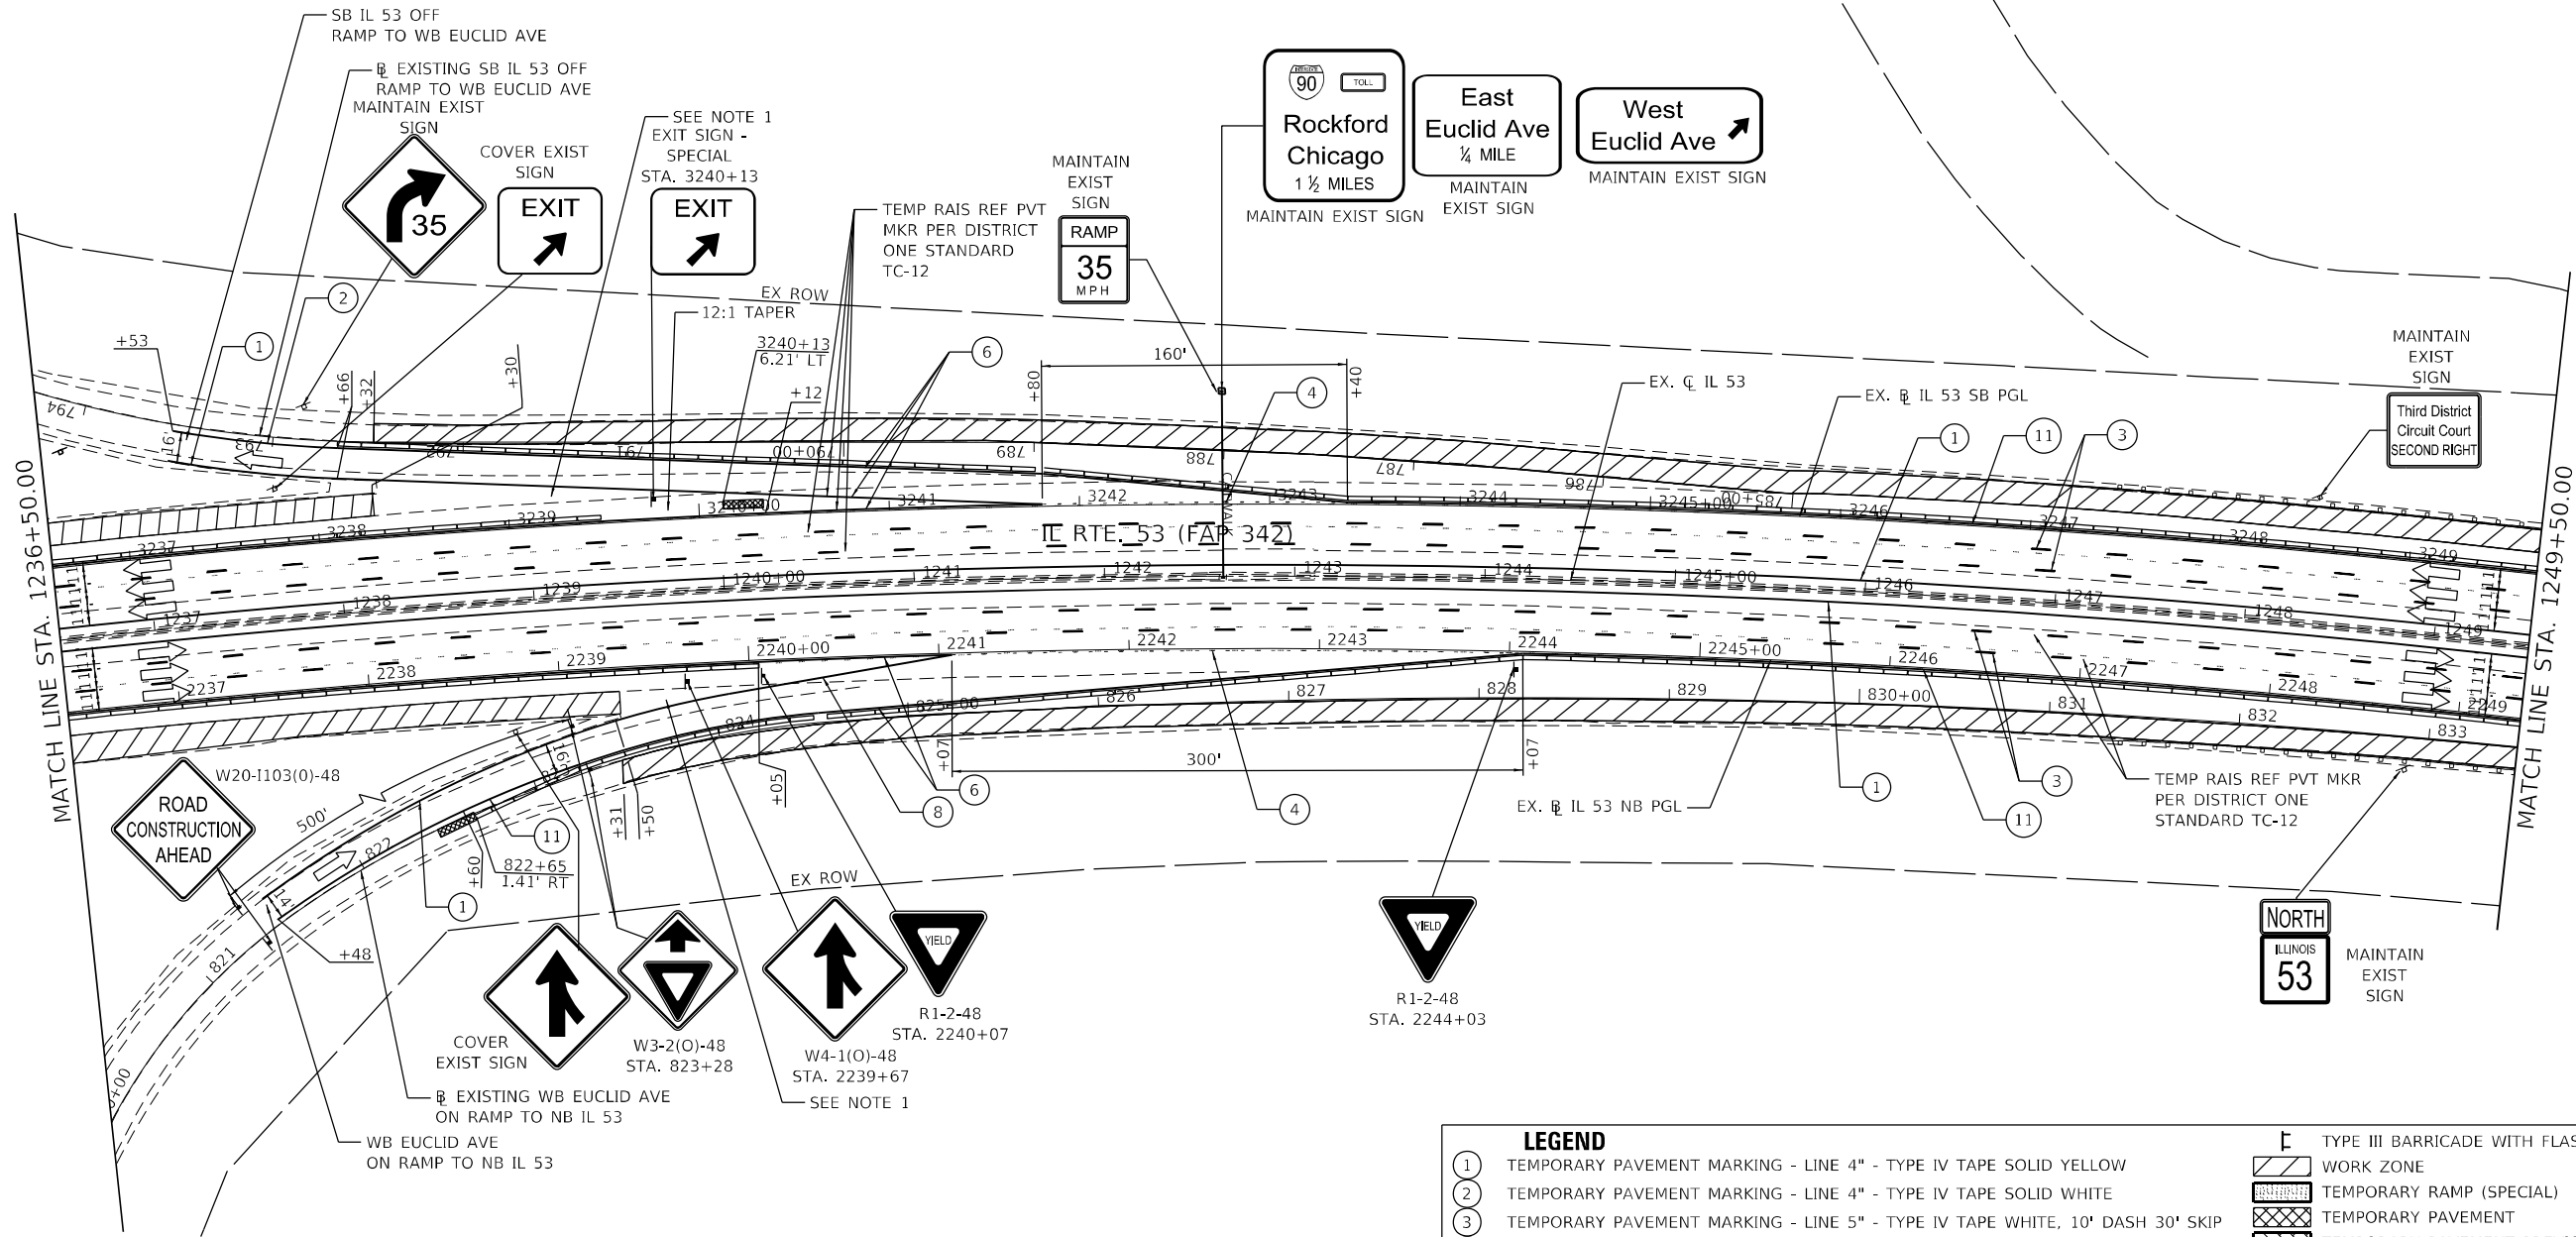

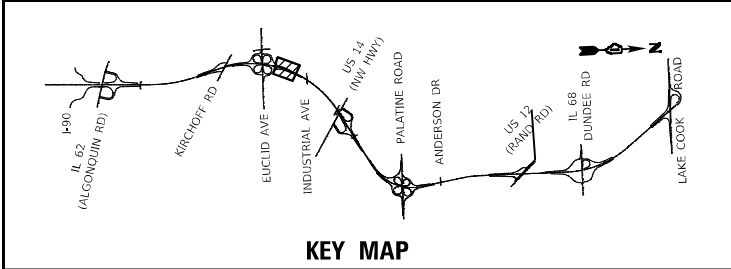


NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.



LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE A				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000' / in.	DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	219
	PLOT DATE = 9/25/2024	CHECKED - TC	REVISED -						CONTRACT NO. 62W38				
					SCALE: 1" = 50'	SHEET 5 OF 16 SHEETS	STA. 1236+50.00 TO STA. 1249+50.00	ILLINOIS FED. AID PROJECT					

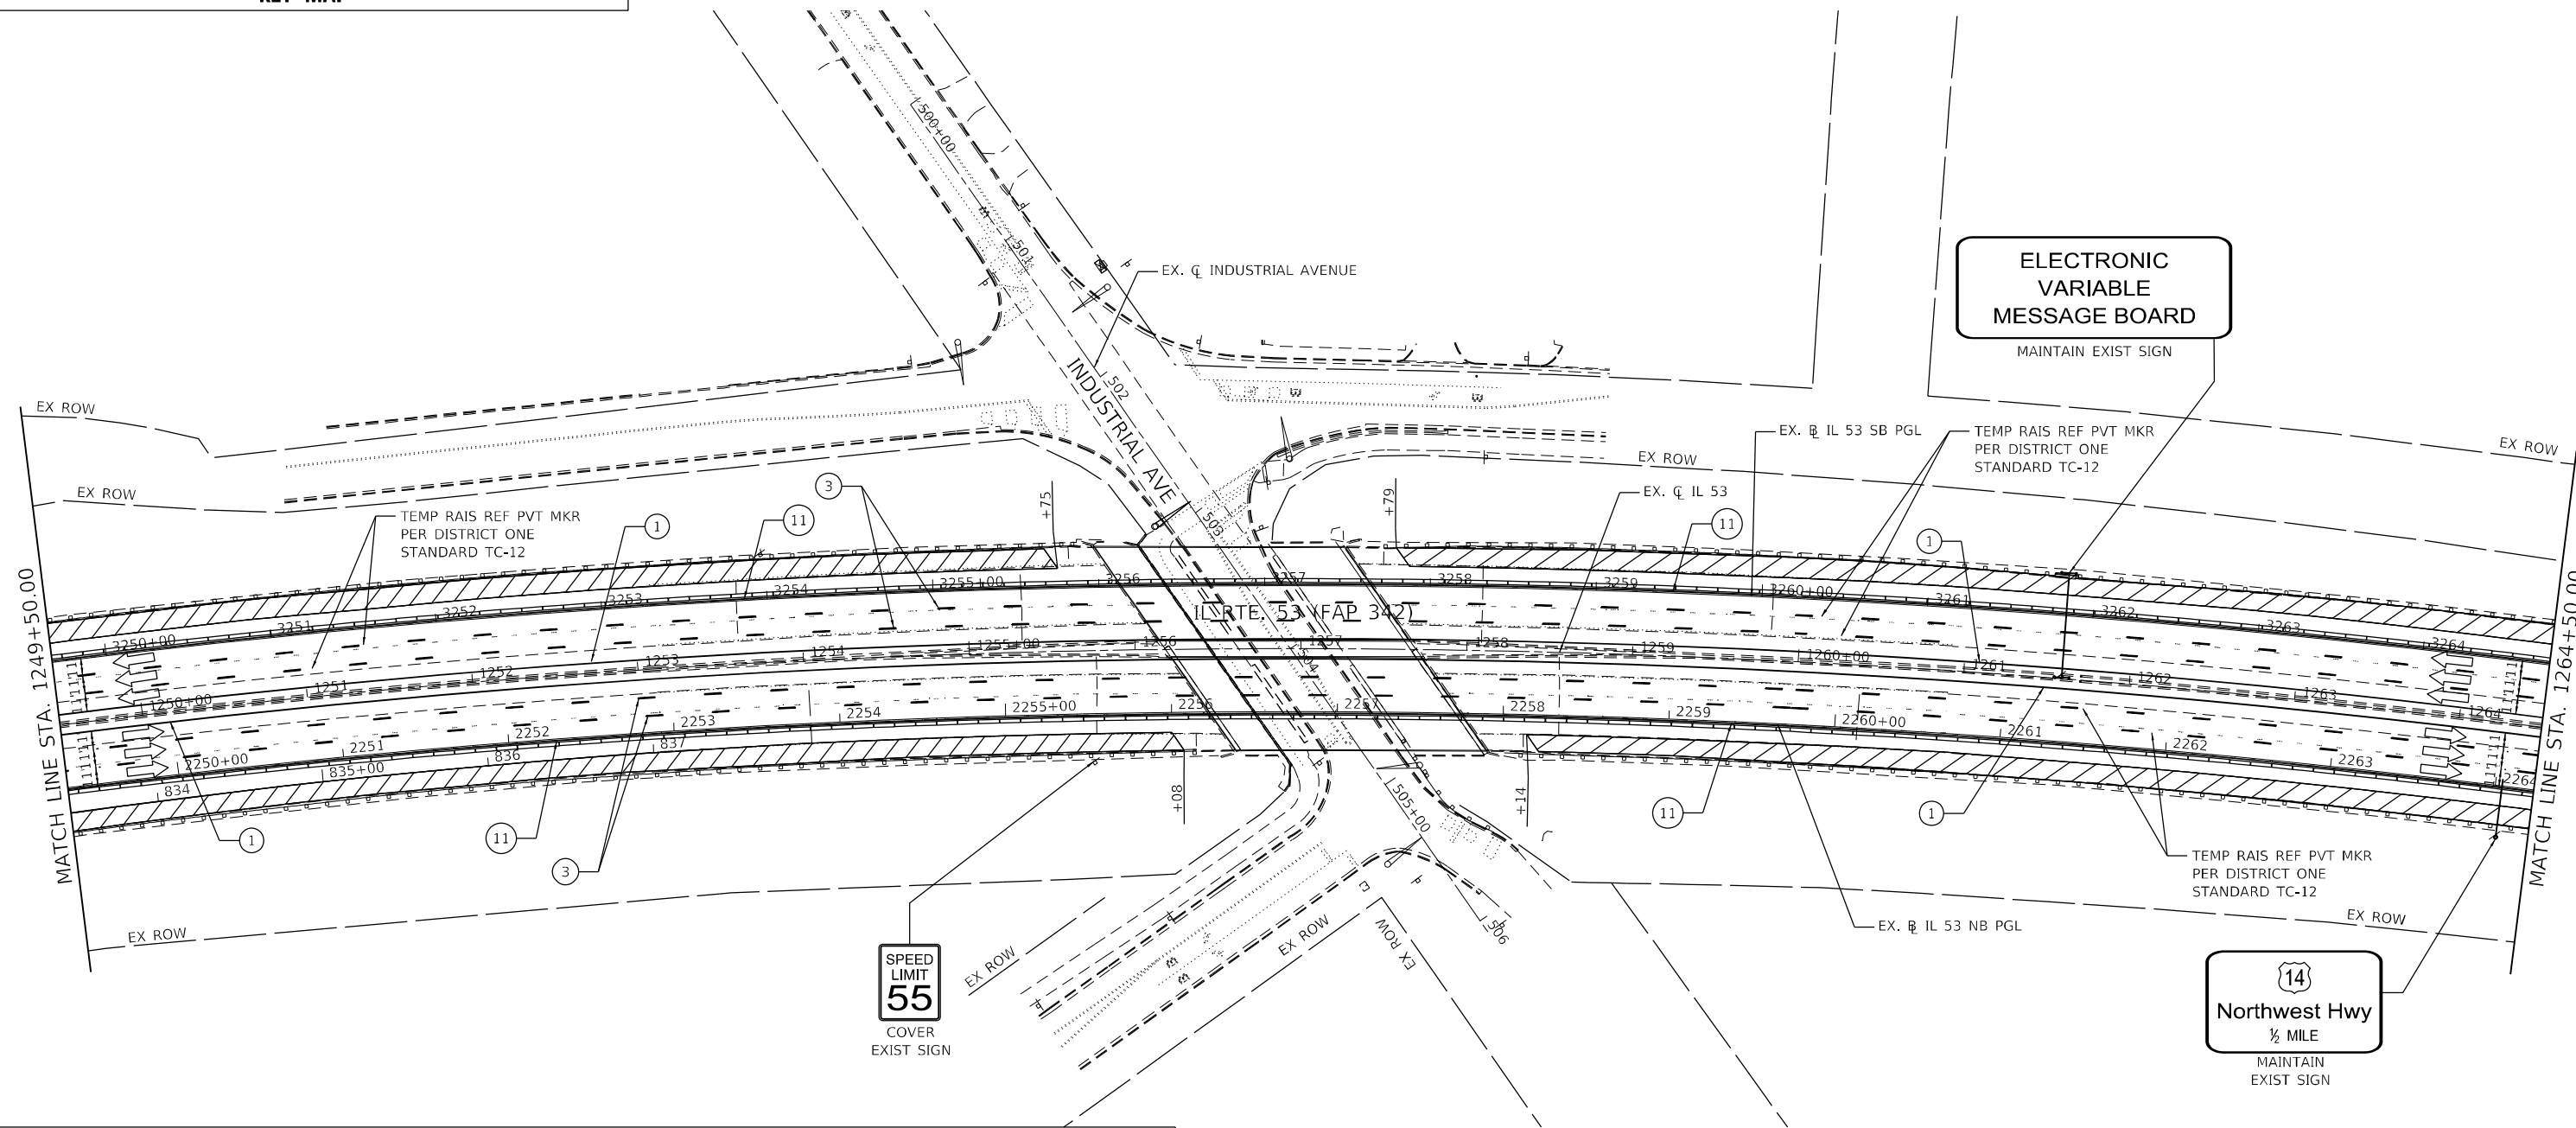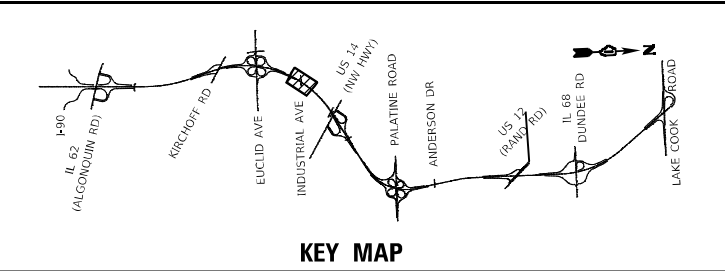

LEGEND	
1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
12	TYPE III BARRICADE WITH FLASHING LIGHTS
13	WORK ZONE
14	TEMPORARY RAMP (SPECIAL)
15	TEMPORARY PAVEMENT
16	TEMPORARY PAVEMENT PREVIOUSLY BUILT
17	TEMPORARY CONCRETE BARRIER
18	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
19	FLASHING ARROW BOARD
20	TRAFFIC FLOW DIRECTION
21	SIGN
22	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADIUS AND 25' CENTERS IN RAMP

	USER NAME = USTC714594		DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - PRESTAGE A		F.A.P. RTE. 342	SECTION (531) BR 23	COUNTY COOK	TOTAL SHEETS 1211	SHEET NO. 220
	PLOT SCALE = 100,000' / in.		DRAWN - MM	REVISED -		SCALE: 1" = 50'		SHEET 6 OF 16 SHEETS		CONTRACT NO. 62W38		
	PLOT DATE = 9/23/2024		CHECKED - TC	REVISED -		STA. 1249+50.00 TO STA. 1264+50.00		ILLINOIS		FED. AID PROJECT		
			DATE - 8/23/2024	REVISED -								

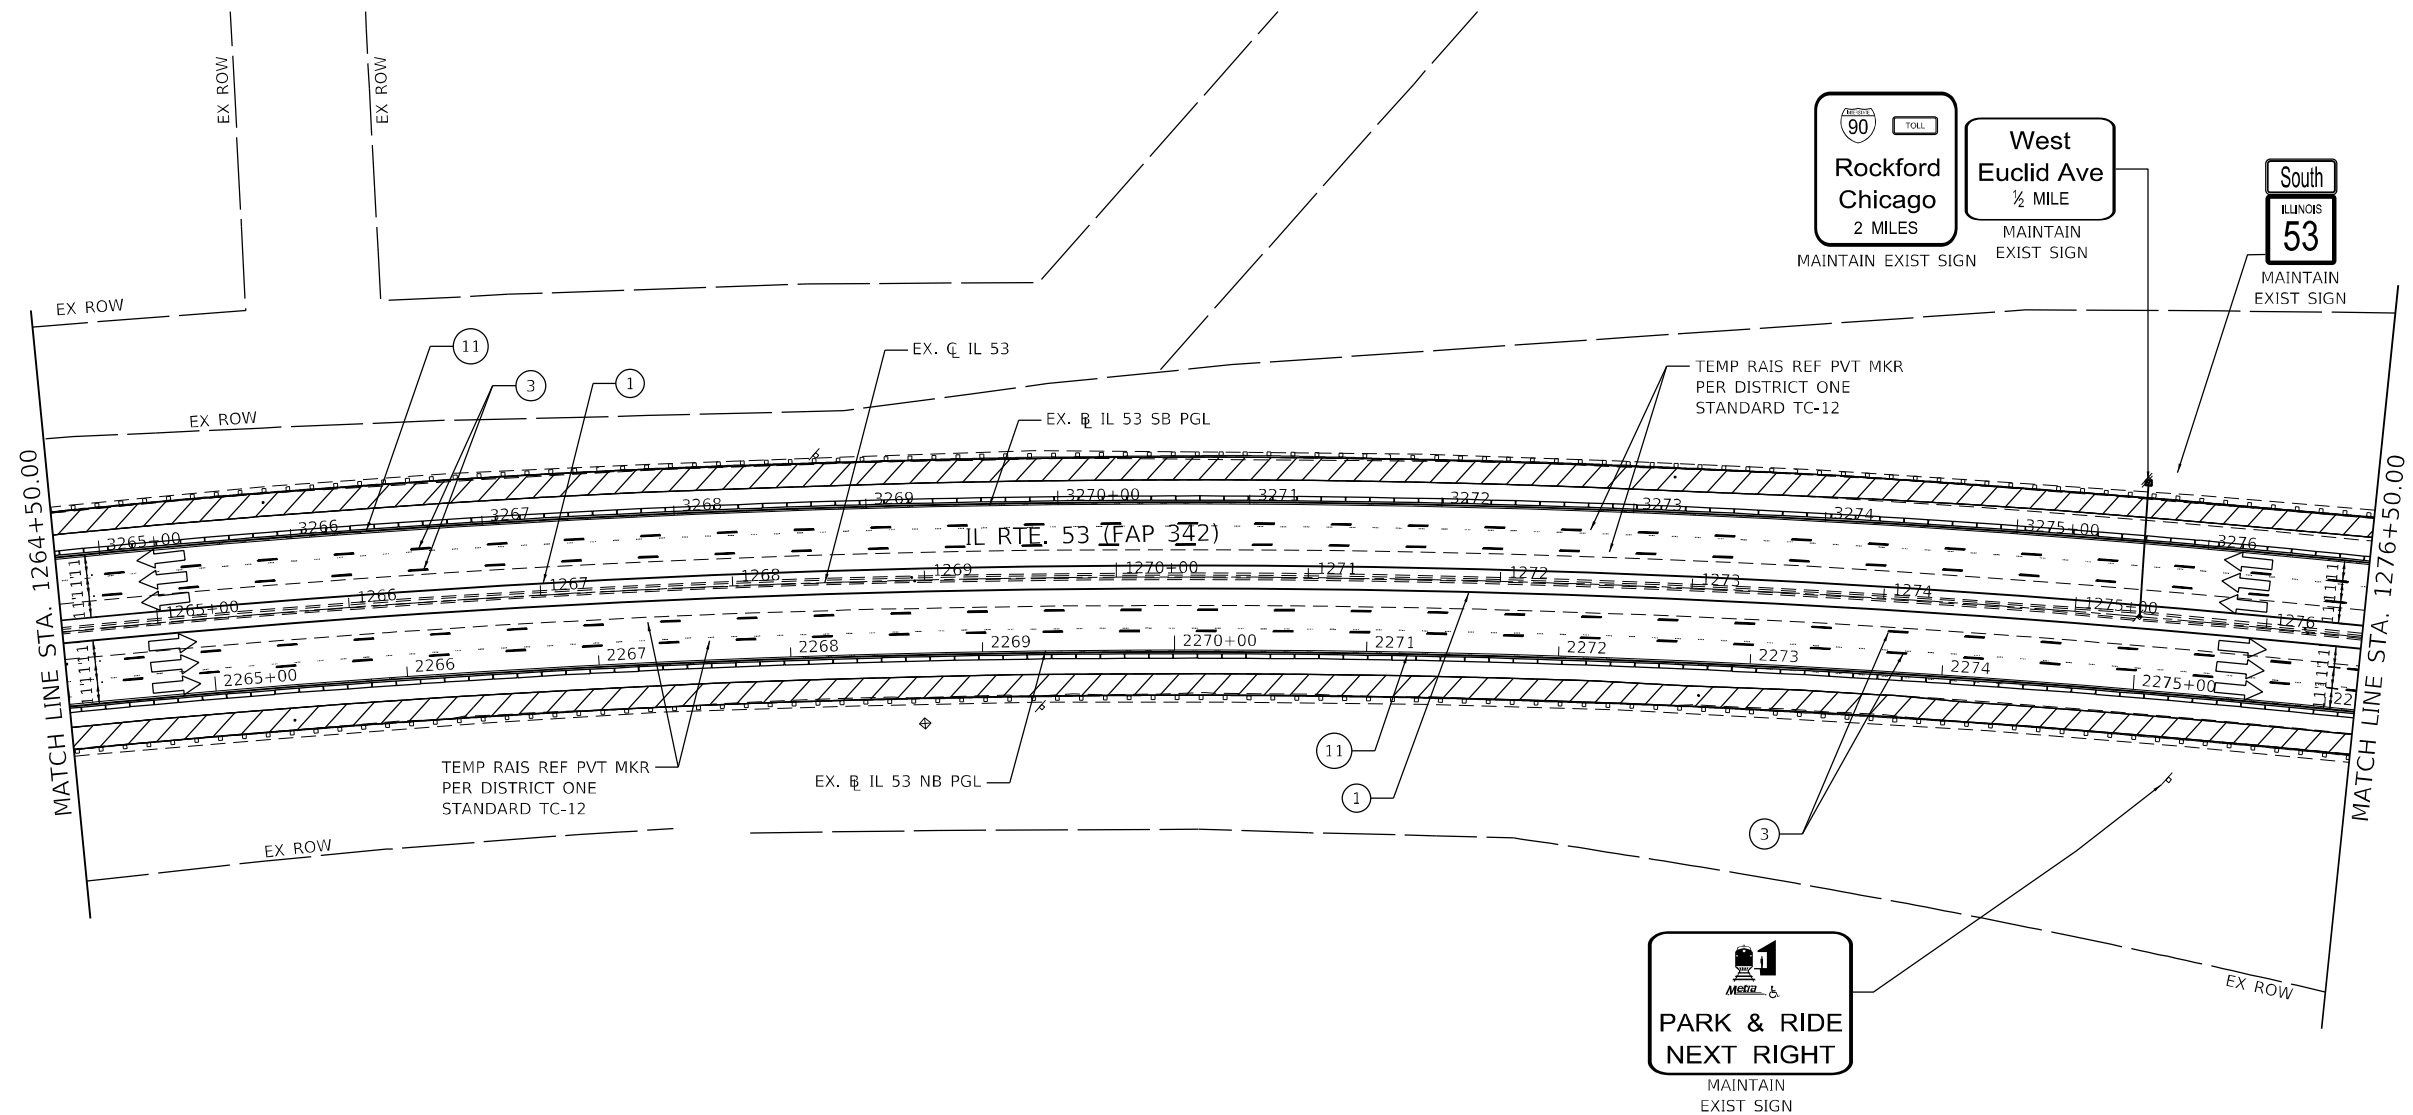

- | LEGEND | |
|--------|--|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE
(CHEVRON MARKING SPACED 30' C-C) |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE |

- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |

USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -




**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

IL ROUTE 53
TRAFFIC CONTROL PLAN – PRESTAGE A

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	221
		CONTRACT NO. 62W38		

MODEL: Default
FILE NAME: c:\wsp-us-pw-bentley.com\wsp-us-pw-ll\Documents\Project: 62N91-I-1: 53 Bridge\CAD Sheets\162\38-shr-stairing-IL53-PreSta A-07-WSP.dgn

MODEL: Default
FILE: I:\Users\pawelpawel\OneDrive\Documents\Project_62W38-IL_53_Bridge\CAD_Sheets\IL53-PreStag-A-08-VIS.dgn

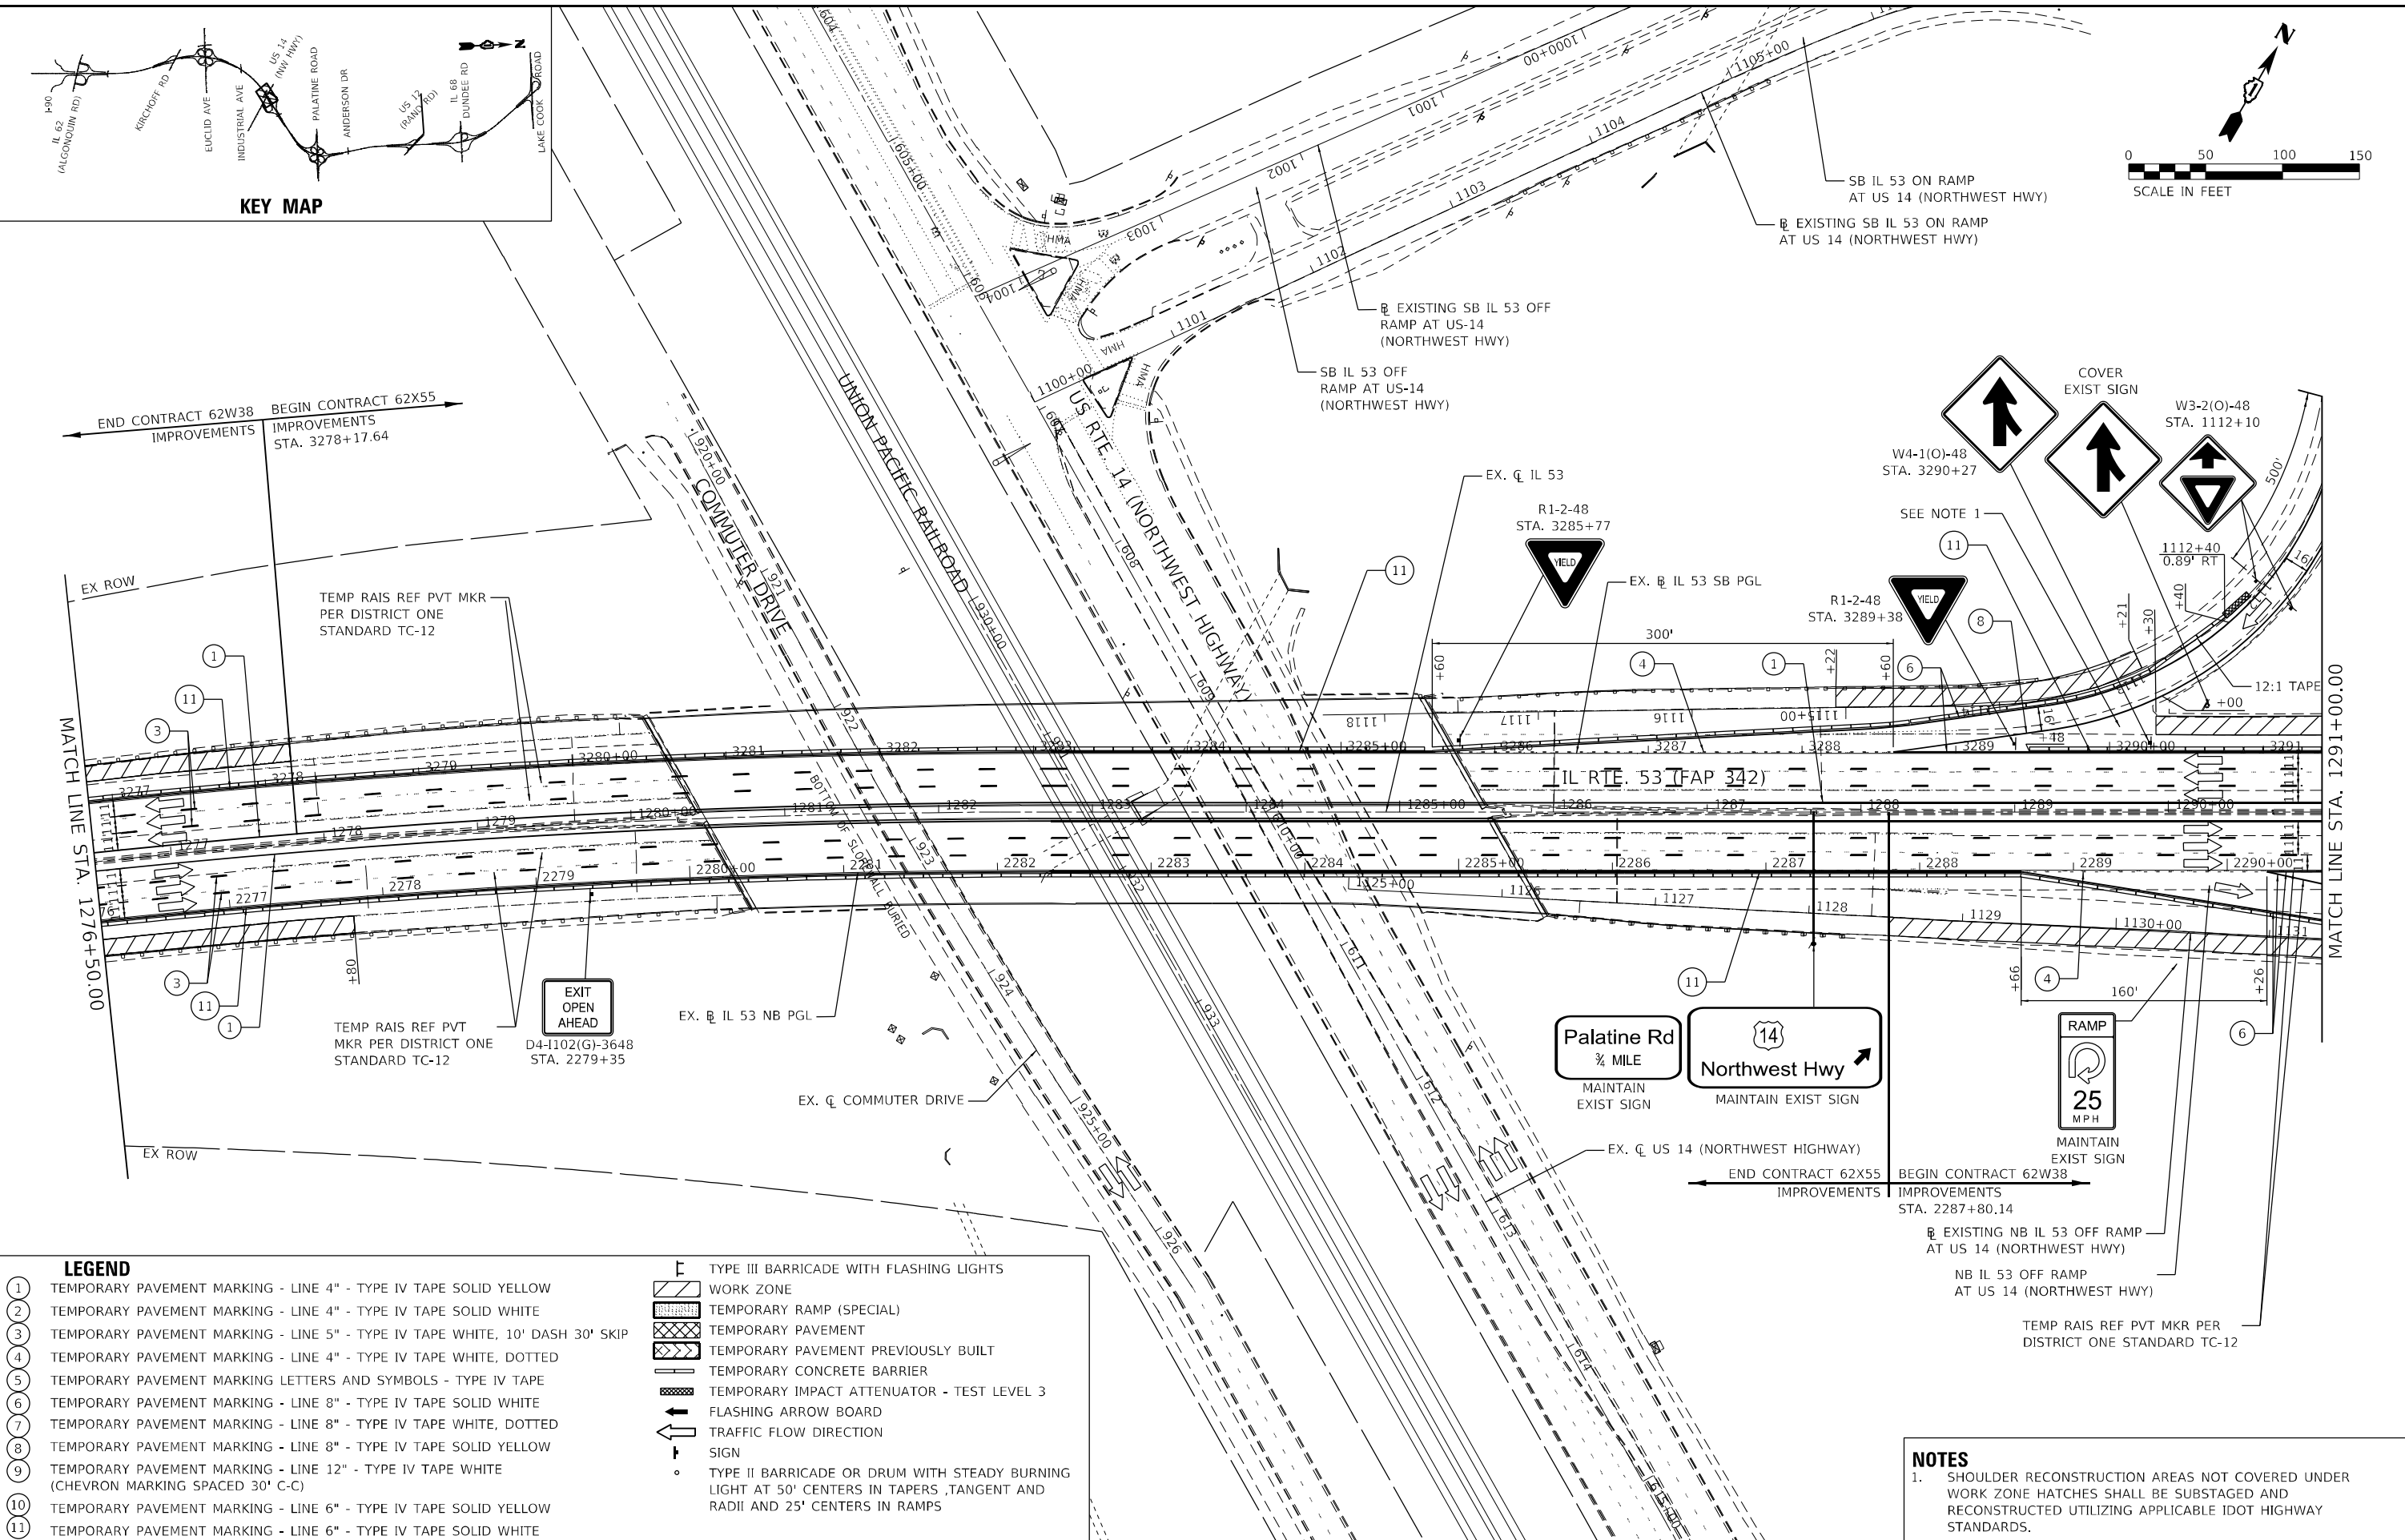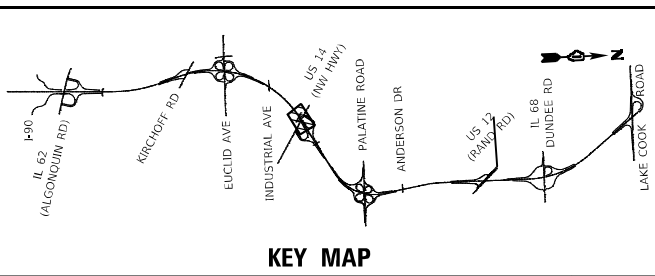

LEGEND

1

2

3

4

5

6

7

8

9

10

11

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

TYPE III BARRICADE WITH FLASHING LIGHTS

WORK ZONE

TEMPORARY RAMP (SPECIAL)

TEMPORARY PAVEMENT

TEMPORARY PAVEMENT PREVIOUSLY BUILT

TEMPORARY CONCRETE BARRIER

TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3

FLASHING ARROW BOARD

TRAFFIC FLOW DIRECTION SIGN

TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMP

	USER NAME = USTC714594	DESIGNED - MM	REVISED -
		DRAWN - MM	REVISED -
	PLOT SCALE = 100,000 ' / in.	CHECKED - TC	REVISED -
	PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -



STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53 TRAFFIC CONTROL PLAN - PRESTAGE A			
SCALE: 1" = 50'	SHEET 1 OF 1 SHEETS	STA. 1276+50.00 TO STA. 1291+00.00	




F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	222
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.



	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE A					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000 ' / in.	DRAWN - MM	REVISED -							342	(531) BR 23	COOK	1211	223
	PLOT DATE = 9/25/2024	CHECKED - TC	REVISED -							CONTRACT NO. 62W38				
		DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 9 OF 16 SHEETS	STA. 1291+00.00 TO STA. 1306+00.00	ILLINOIS FED. AID PROJECT						

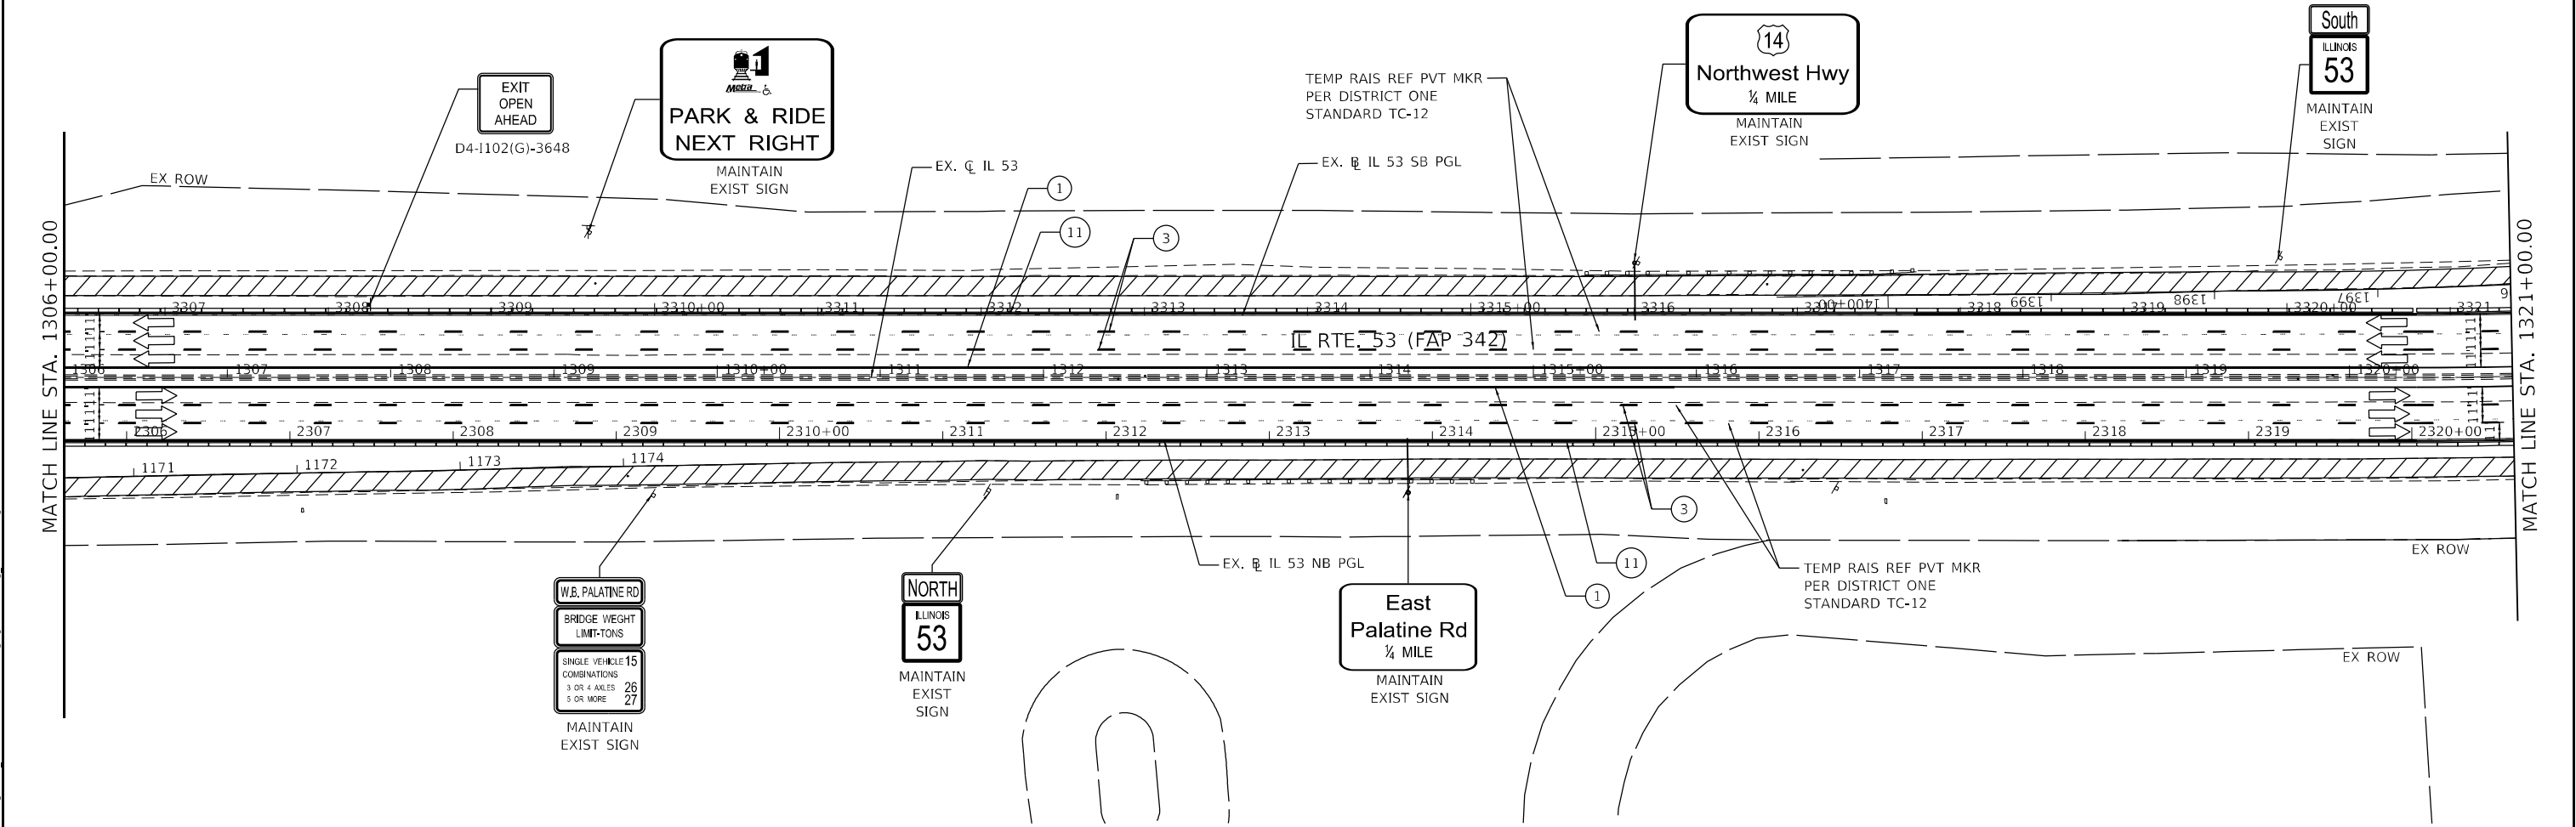
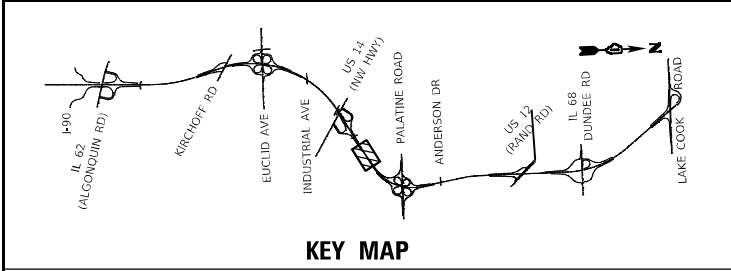


LEGEND

- ① TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- ② TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- ③ TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- ④ TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- ⑤ TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- ⑥ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- ⑦ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- ⑧ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- ⑨ TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- ⑩ TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- ⑪ TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

MODEL: Default
FILE: A:\Users\pawel.bentley.com\userpawel.bentley.com\workspace\pawel.bentley.com\workspace\Documents\Project: 62W38-23-24\Drawings\IL53-PreStag A-10-10\TSP.dgn

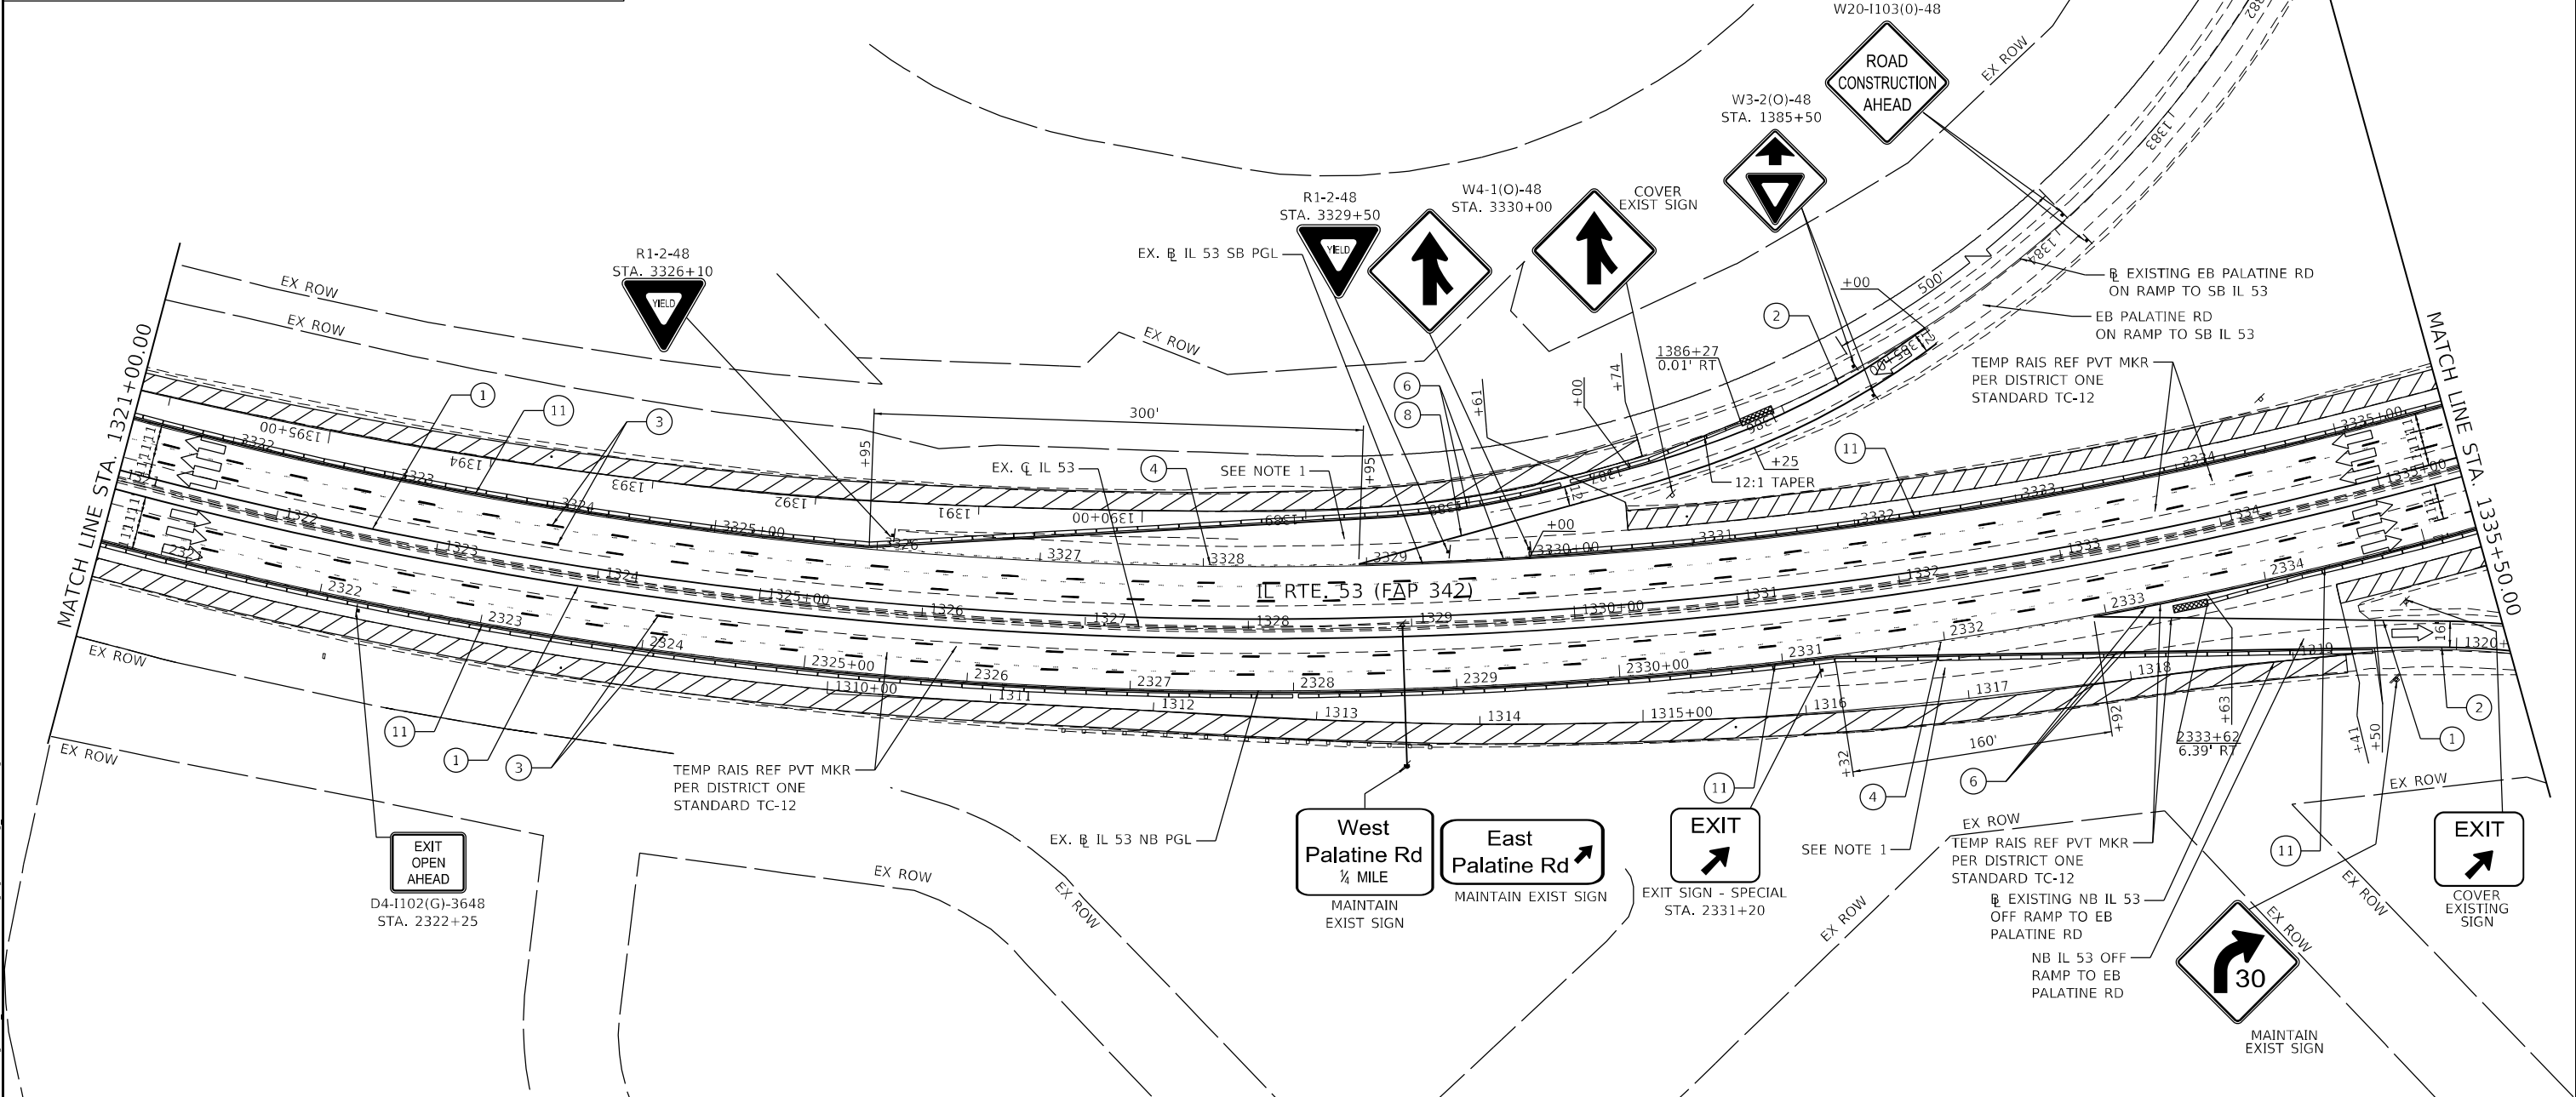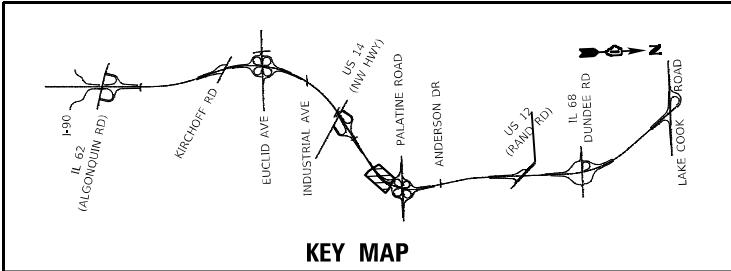


NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	TYPE III BARRICADE WITH FLASHING LIGHTS
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE	WORK ZONE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP	TEMPORARY RAMP (SPECIAL)
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY PAVEMENT
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE	TEMPORARY PAVEMENT PREVIOUSLY BUILT
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE	TEMPORARY CONCRETE BARRIER
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW	FLASHING ARROW BOARD
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)	TRAFFIC FLOW DIRECTION SIGN
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE	

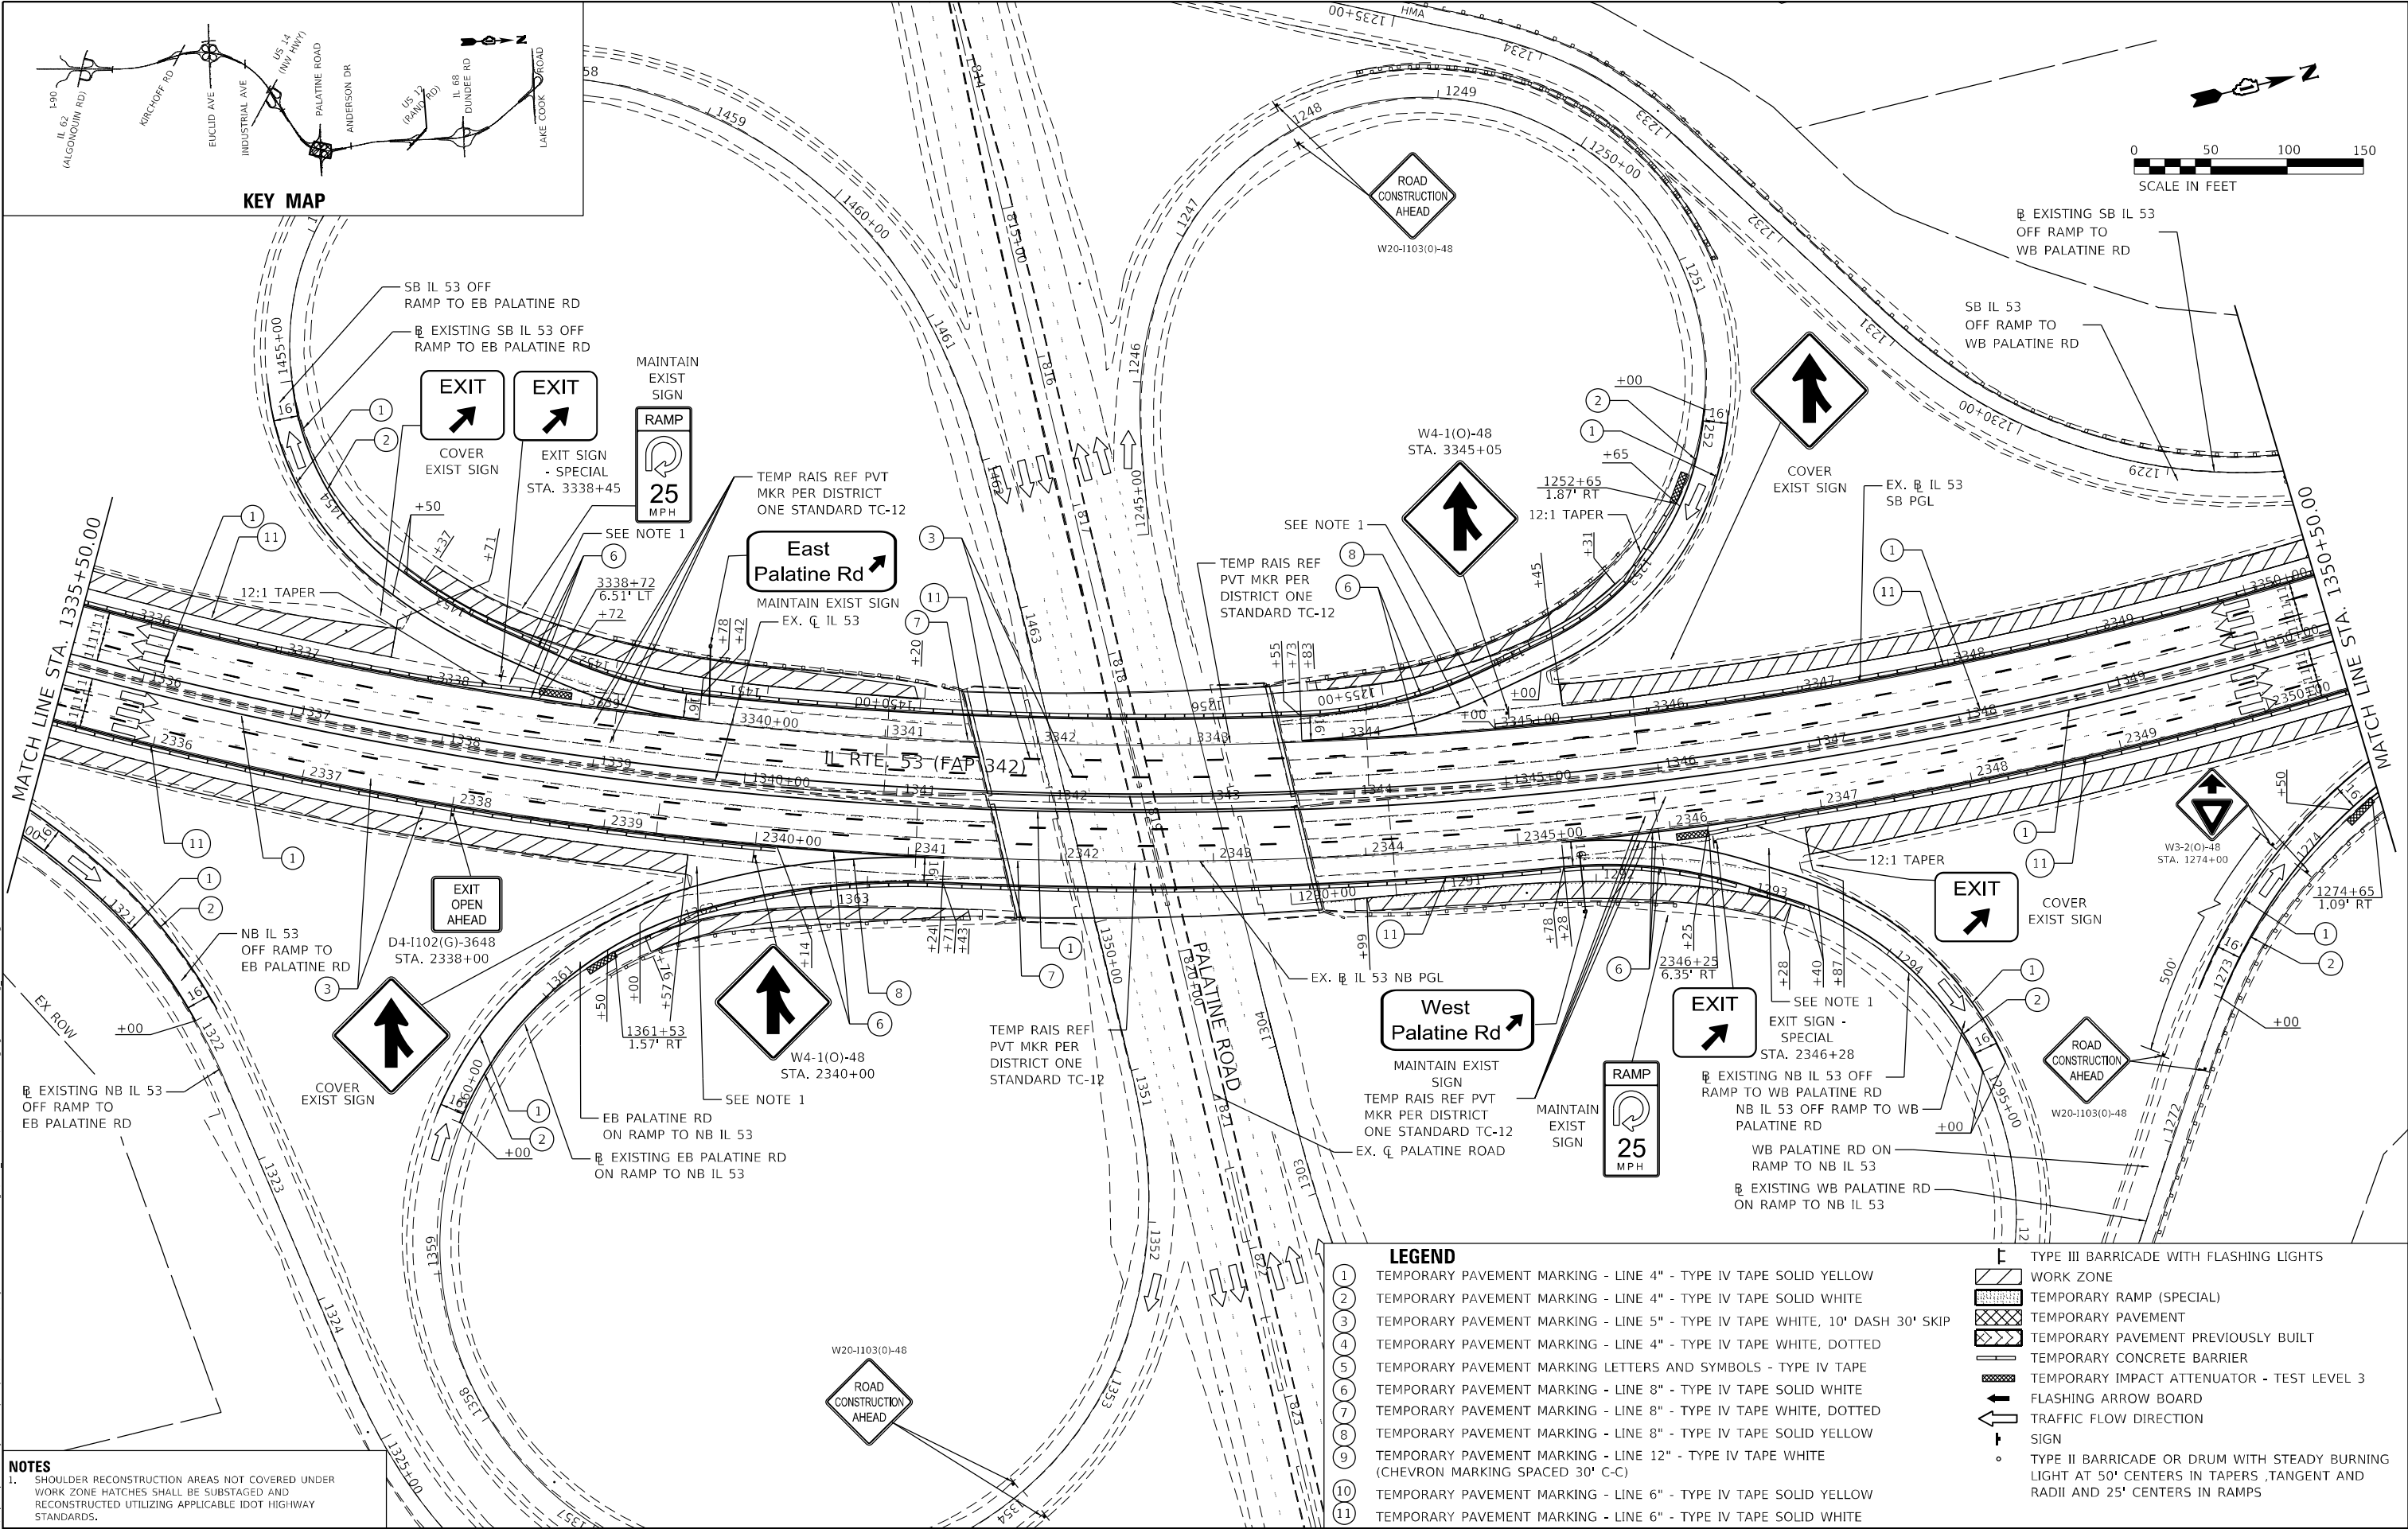

KEY MAP






NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMP

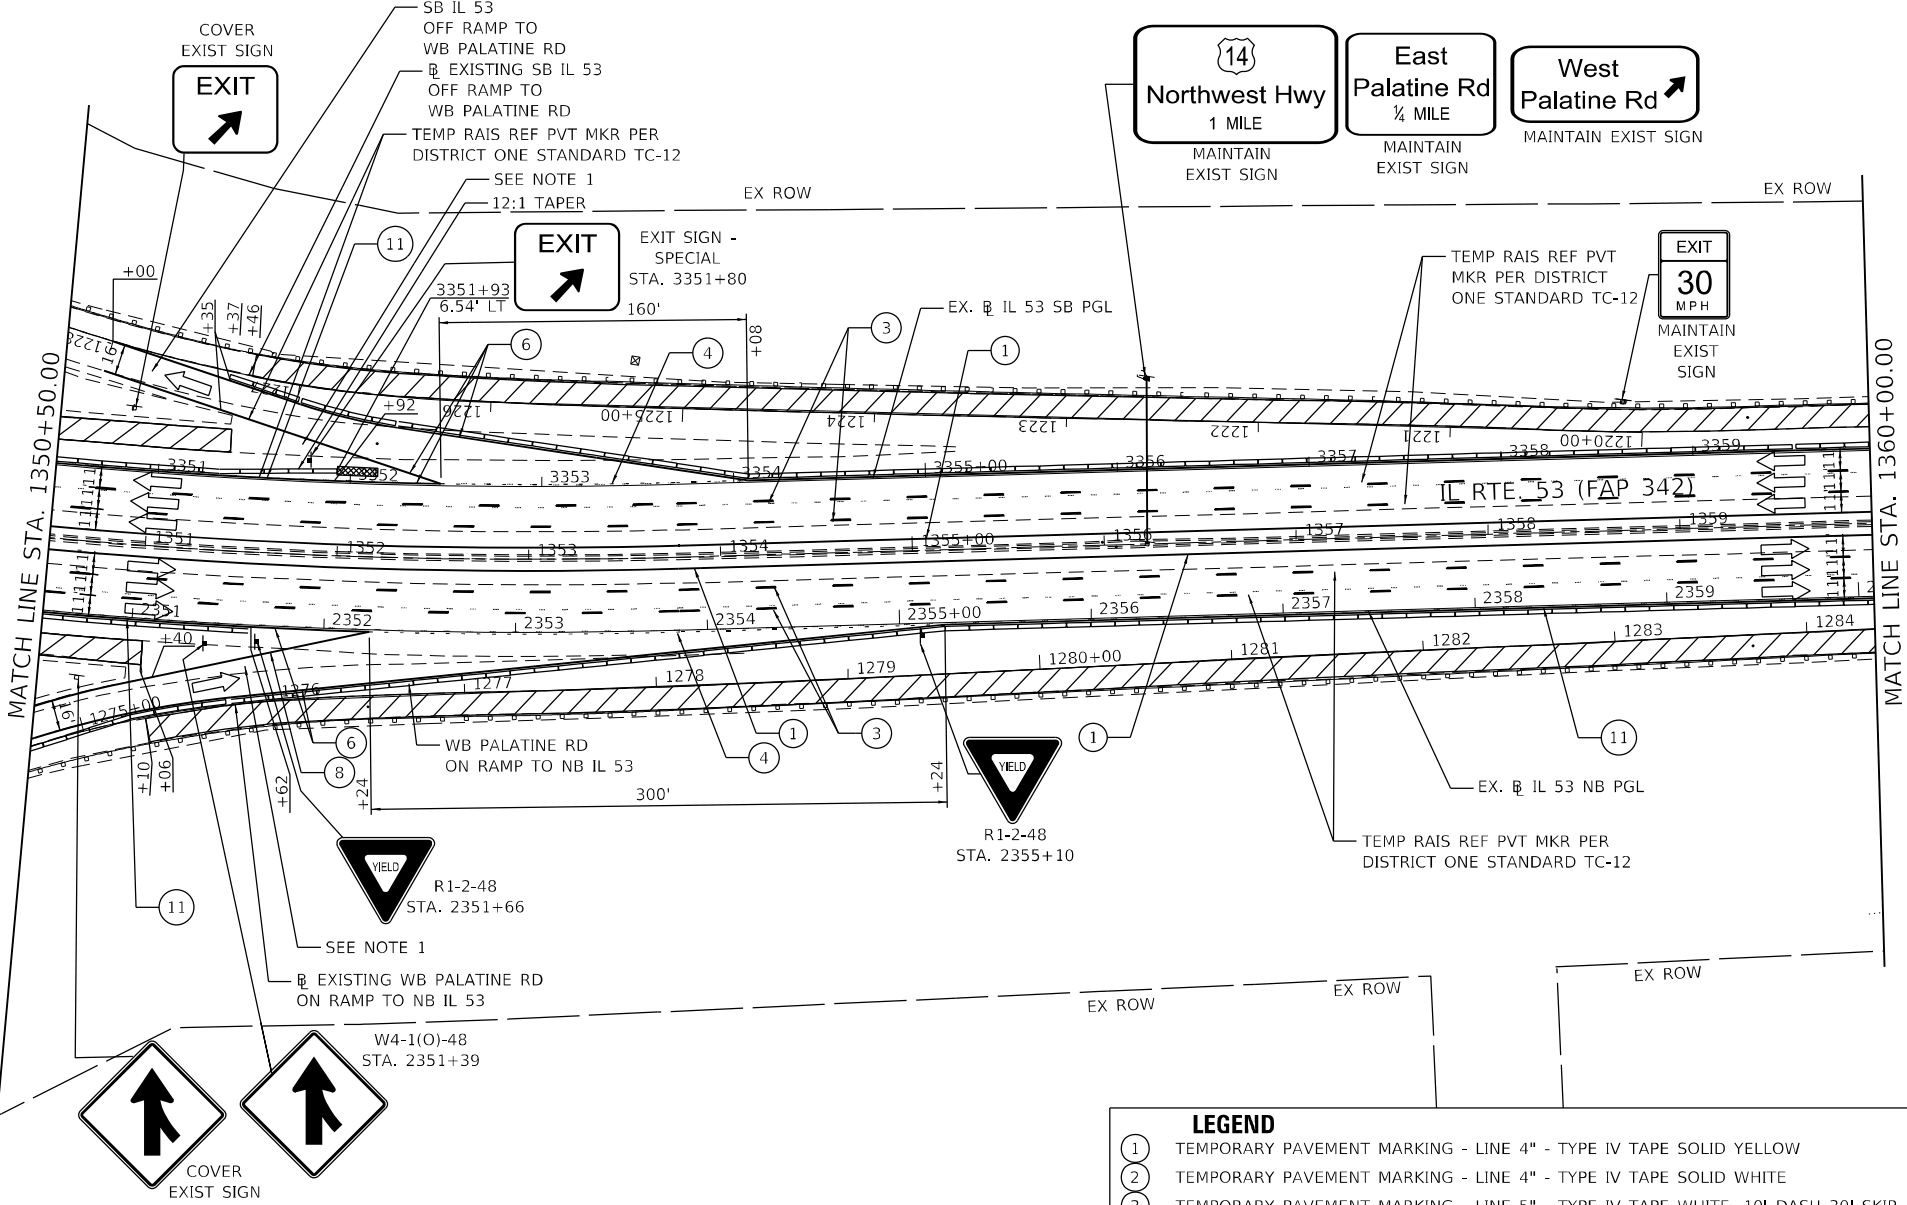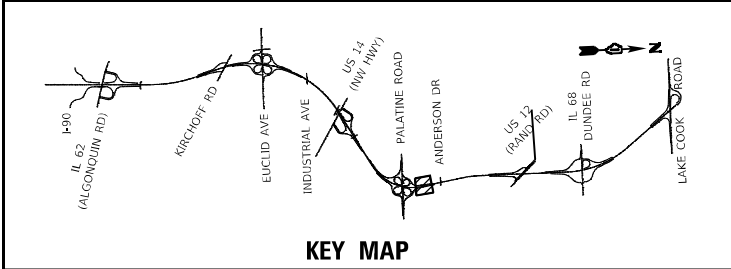

NOTES




1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING APPLICABLE IDOT HIGHWAY STANDARDS.

LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE A					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -							342	(531) BR 23	COOK	1211	227
	PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -		CONTRACT NO. 62W38									
	SCALE: 1" = 50'				SHEET 13 OF 16 SHEETS	STA. 1350+50.00 TO STA. 1360+00.00	ILLINOIS FED. AID PROJECT							

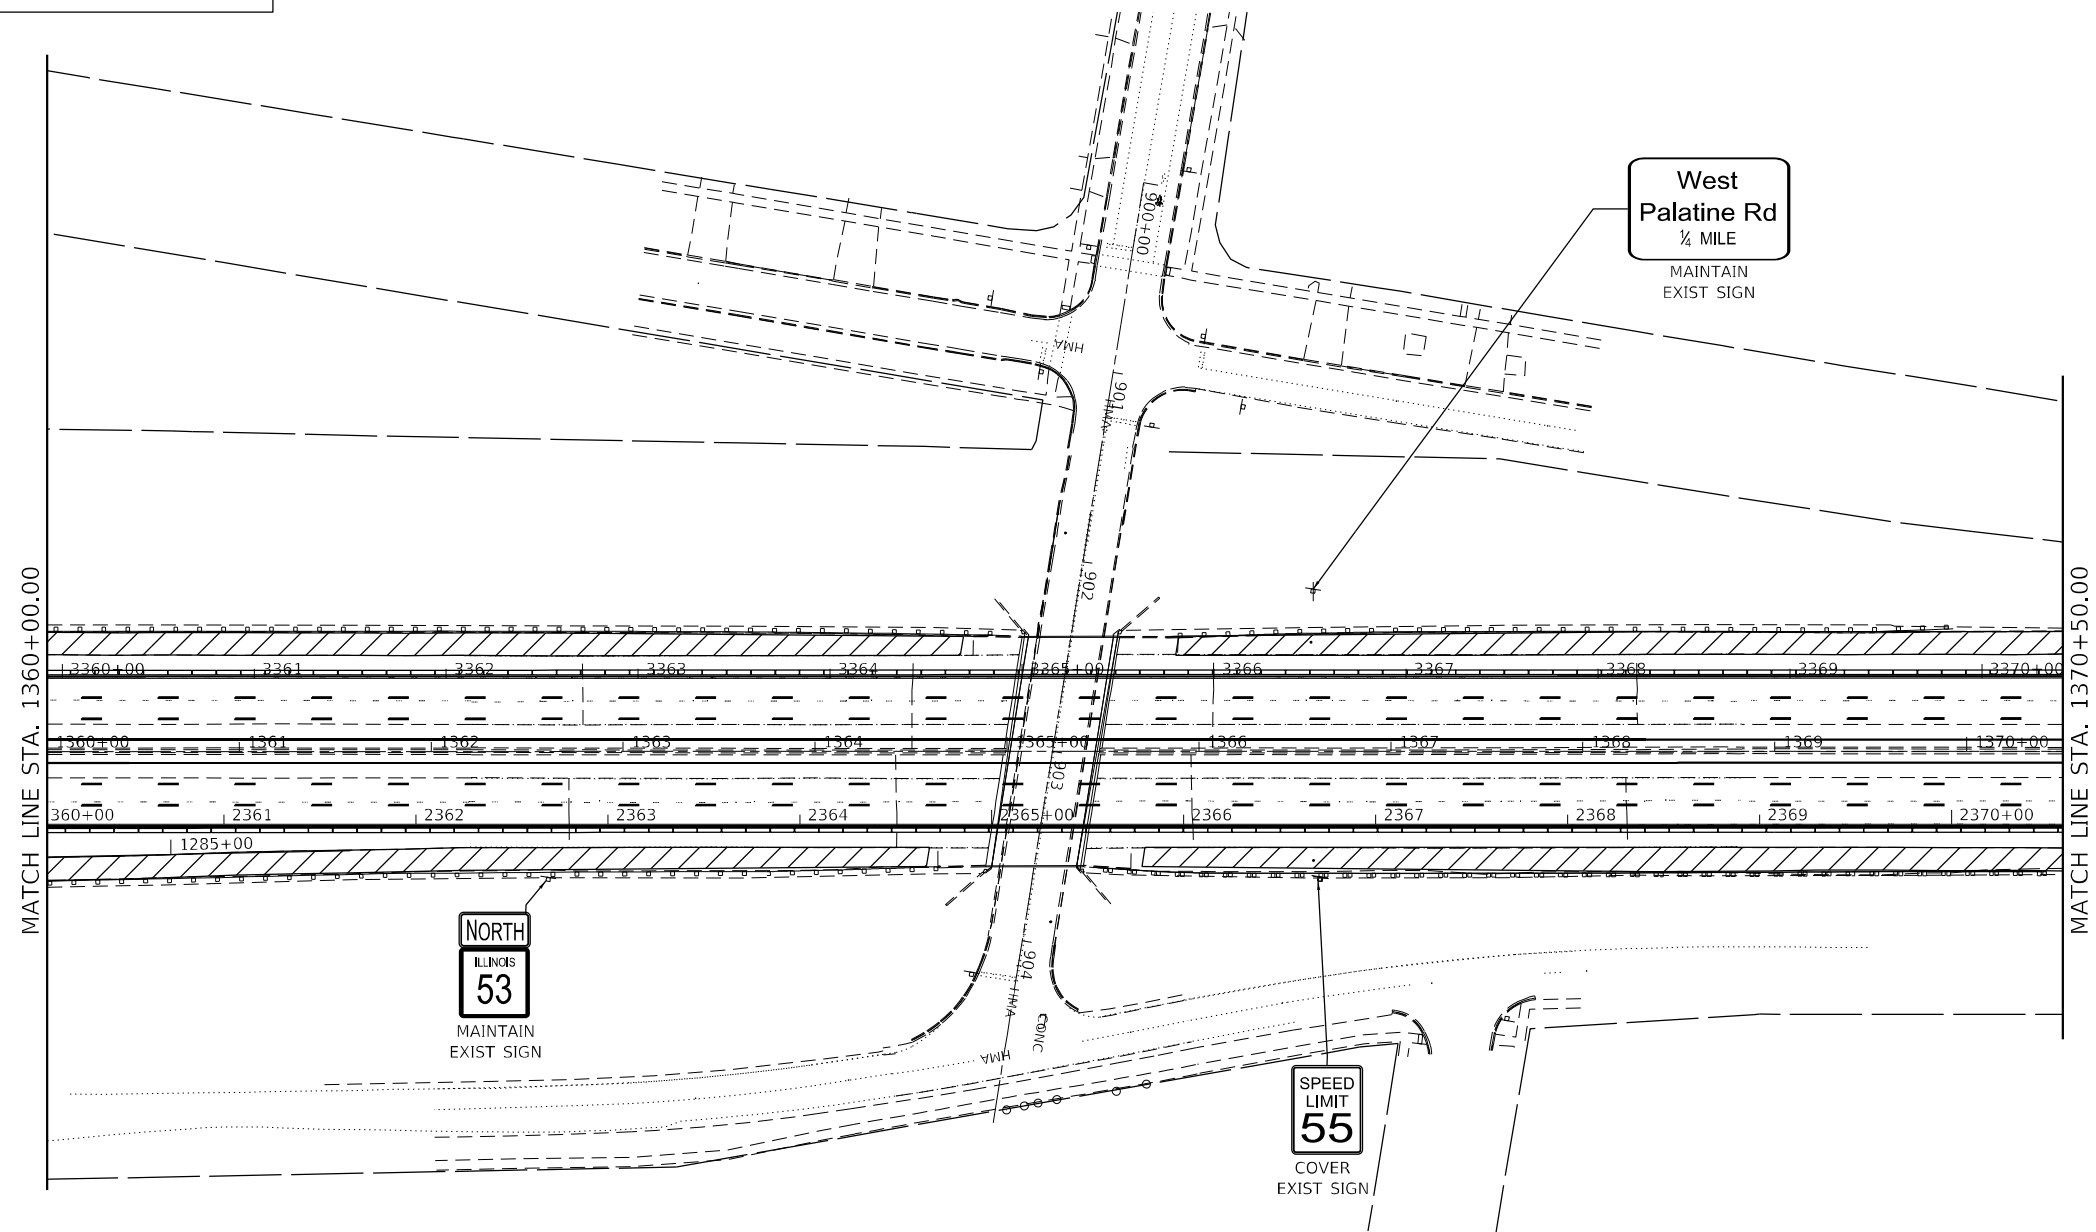

LEGEND

- | LEGEND | |
|--------|--|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE
(CHEVRON MARKING SPACED 30' C-C) |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE |

- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION SIGN |
| o | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |



USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

IL ROUTE 53


TRAFFIC CONTROL PLAN – PRESTAGE A

SCALE: 1" = 50'	SHEET 14 OF 16 SHEETS	STA. 1360+00.00 TO STA. 1370+00.00
-----------------	-----------------------	------------------------------------



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	228
		CONTRACT NO. 62W38		

MODEL: Default
FILE NAME: d:\wsp-us-pw-ll\Documents\Project: 62N9-1JL 53 Bridge\CAD Sheets\0162N38-shr-staging-IL53-PreStg_A-14-WSP.dgn

MODEL: Default
FILE NAME: p:\wsp\p4\p4\benfley.com\uspa4\p4\il\Documents\Project: 62W38-2\tr-ctg\p4-IL53-PreStgA.dgn
A-15-VISPR.dgn



KEY MAP

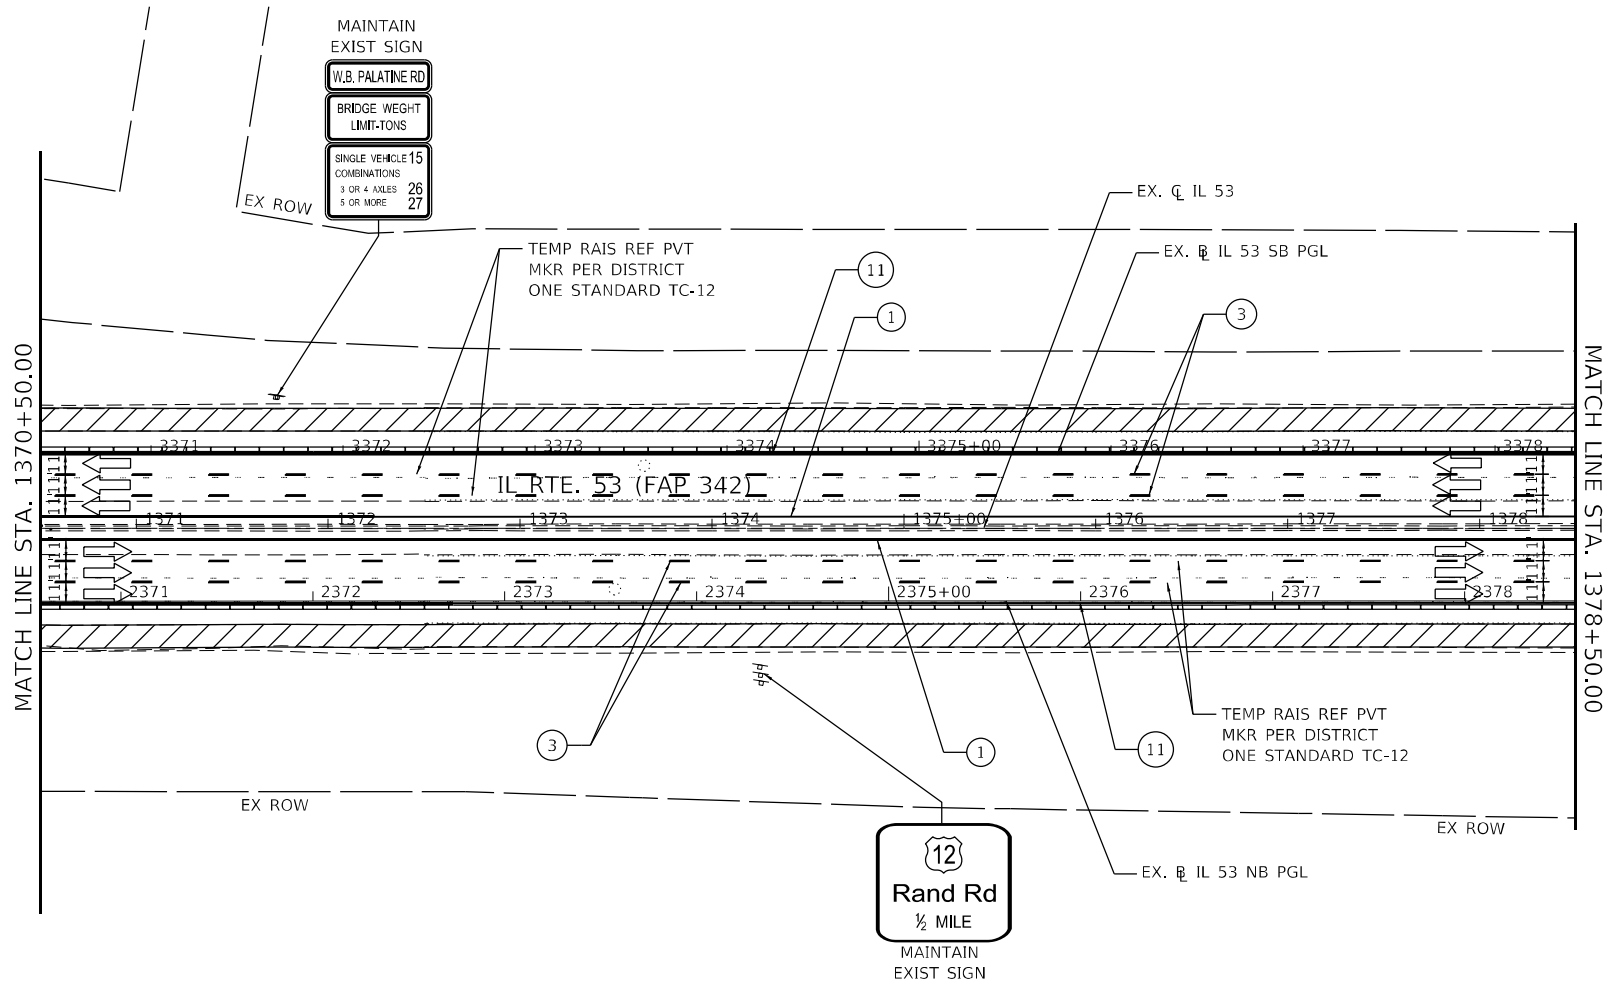

LEGEND


- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS


	USER NAME = USTC714594		DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - PRESTAGE A		F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	DRAWN - MM		CHECKED - TC	REVISED -		SCALE: 1" = 50'		342	(531) BR 23	COOK	1211	229
	PLOT SCALE = 100,0000 ' / in.		DATE - 8/23/2024	REVISED -		SHEET 15 OF 16 SHEETS		CONTRACT NO. 62W38				
	PLOT DATE = 9/23/2024					STA. 1370+50.00 TO STA. 1378+50.00		ILLINOIS FED. AID PROJECT				

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE B AND C				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000 ' / in.	DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	231
	PLOT DATE = 9/25/2024	CHECKED - TC	REVISED -		CONTRACT NO. 62W3E								
		DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 1 OF 16 SHEETS	STA. 1186+00.00 TO STA. 1199+00.00		ILLINOIS	FED. AID PROJECT			



MODEL: Default
FILE: \\wsp-04-pw-bentley.com\usps4-pw-ill\Documents\Project: 62W38-01-01\Drawings\IL53-PreStg-B_003-WSP.dgn



KEY MAP

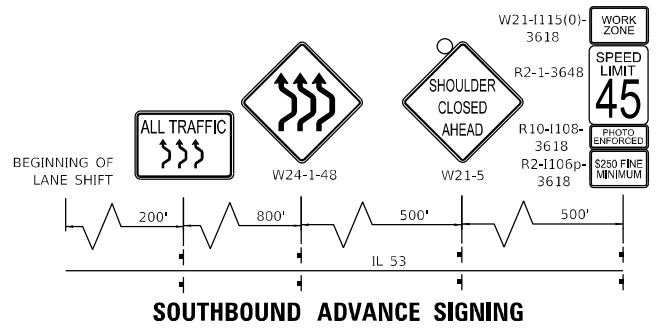

SOUTHBOUND ADVANCE SIGNING

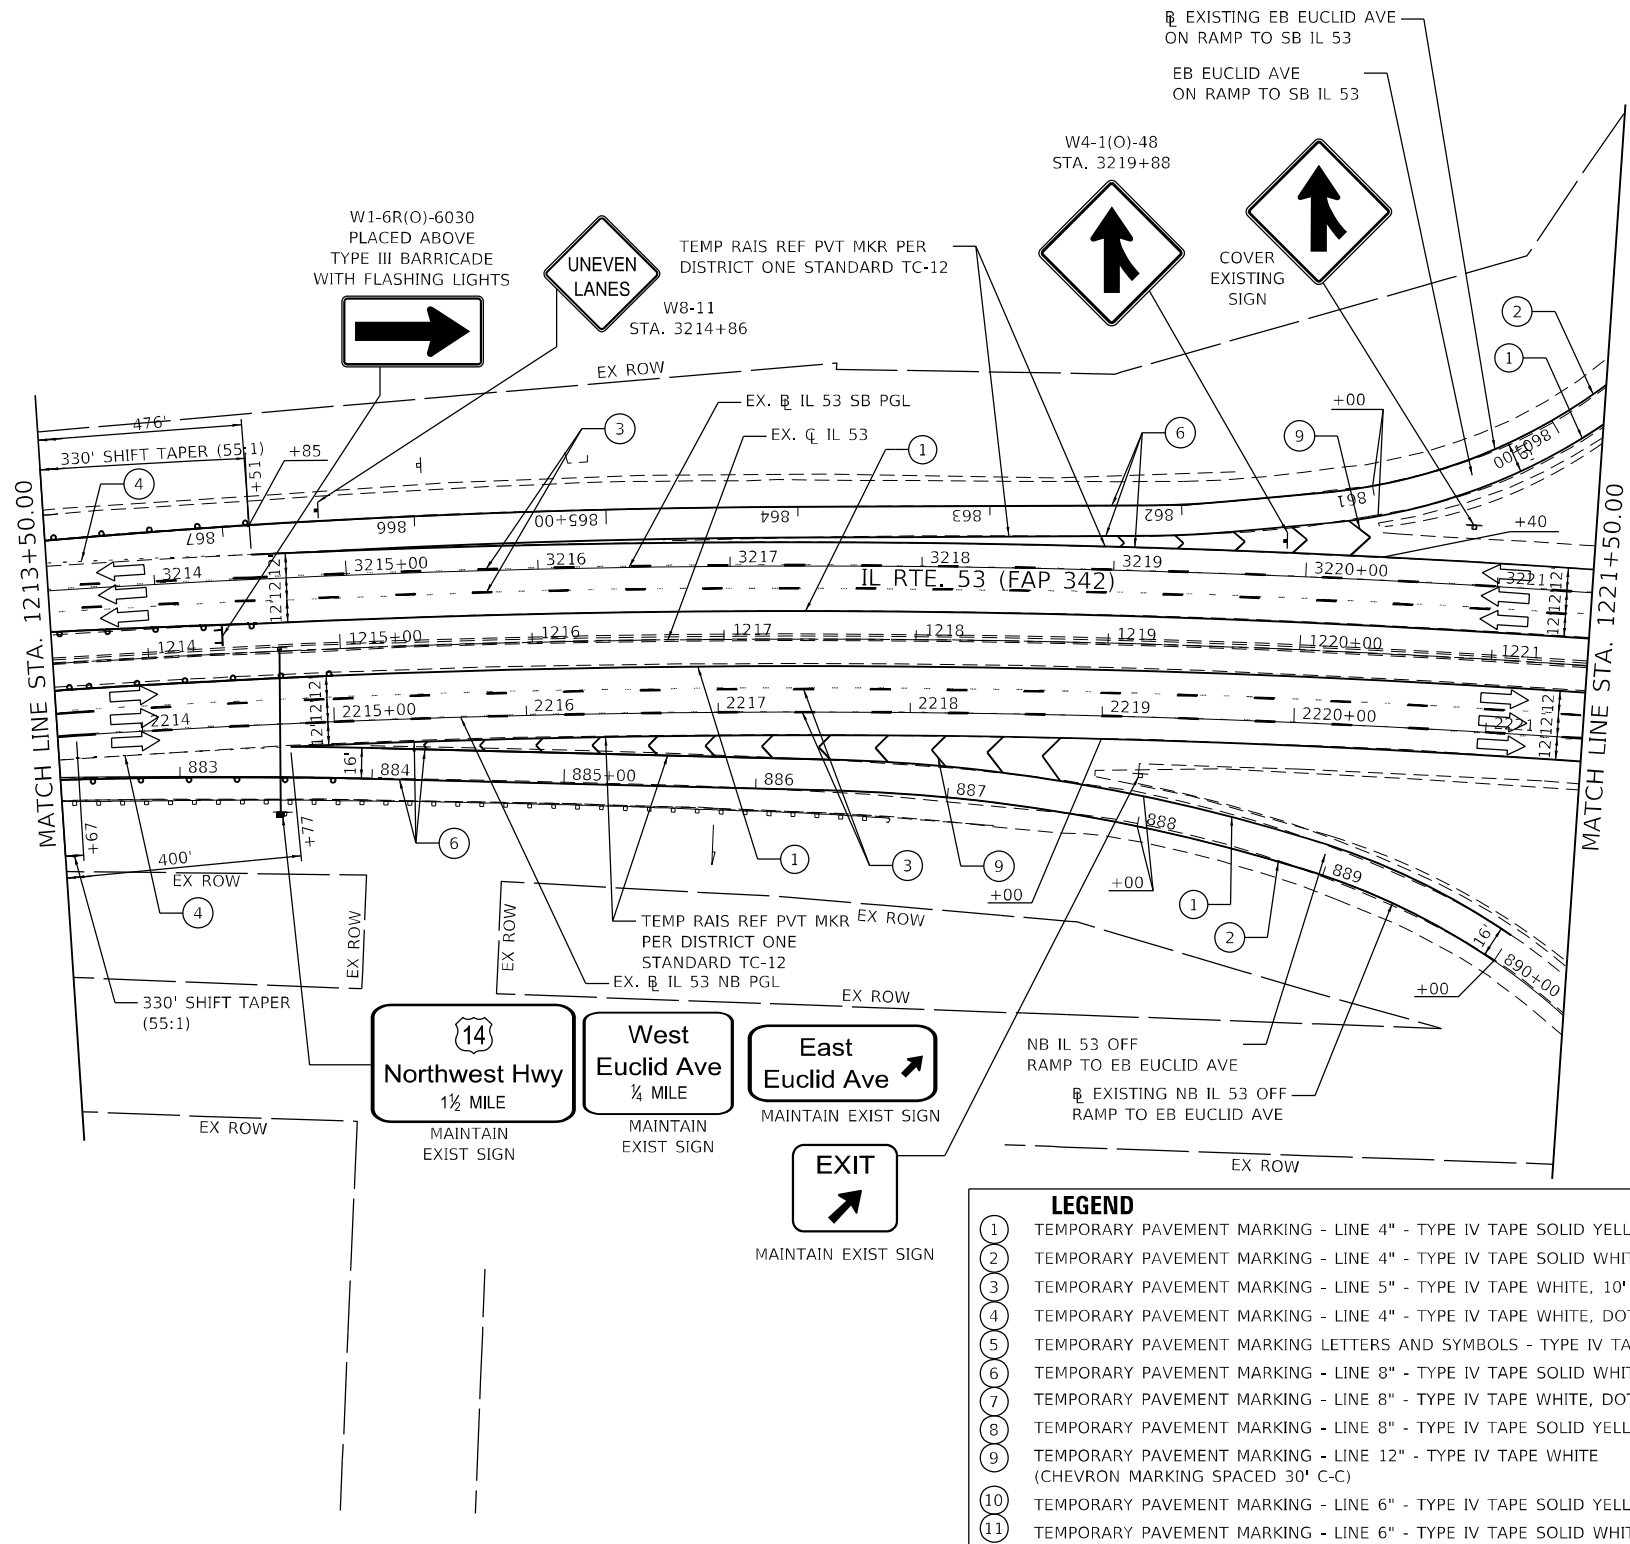

- LEGEND**
- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
 - 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
 - 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
 - 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
 - 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
 - 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
 - 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
 - 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
 - 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
 - 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
 - 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
- TYPE III BARRICADE WITH FLASHING LIGHTS
 - WORK ZONE
 - TEMPORARY RAMP (SPECIAL)
 - TEMPORARY PAVEMENT
 - TEMPORARY PAVEMENT PREVIOUSLY BUILT
 - TEMPORARY CONCRETE BARRIER
 - TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
 - FLASHING ARROW BOARD
 - TRAFFIC FLOW DIRECTION
 - SIGN
 - TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS




USER NAME = USTC714594	DESIGNED - MM	REVISED -
DRAWN - MM	REVISED -	
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN - PRESTAGE B AND C

SCALE: 1" = 50' SHEET 3 OF 16 SHEETS STA. 1213+50.00 TO STA. 1221+50.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	233
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

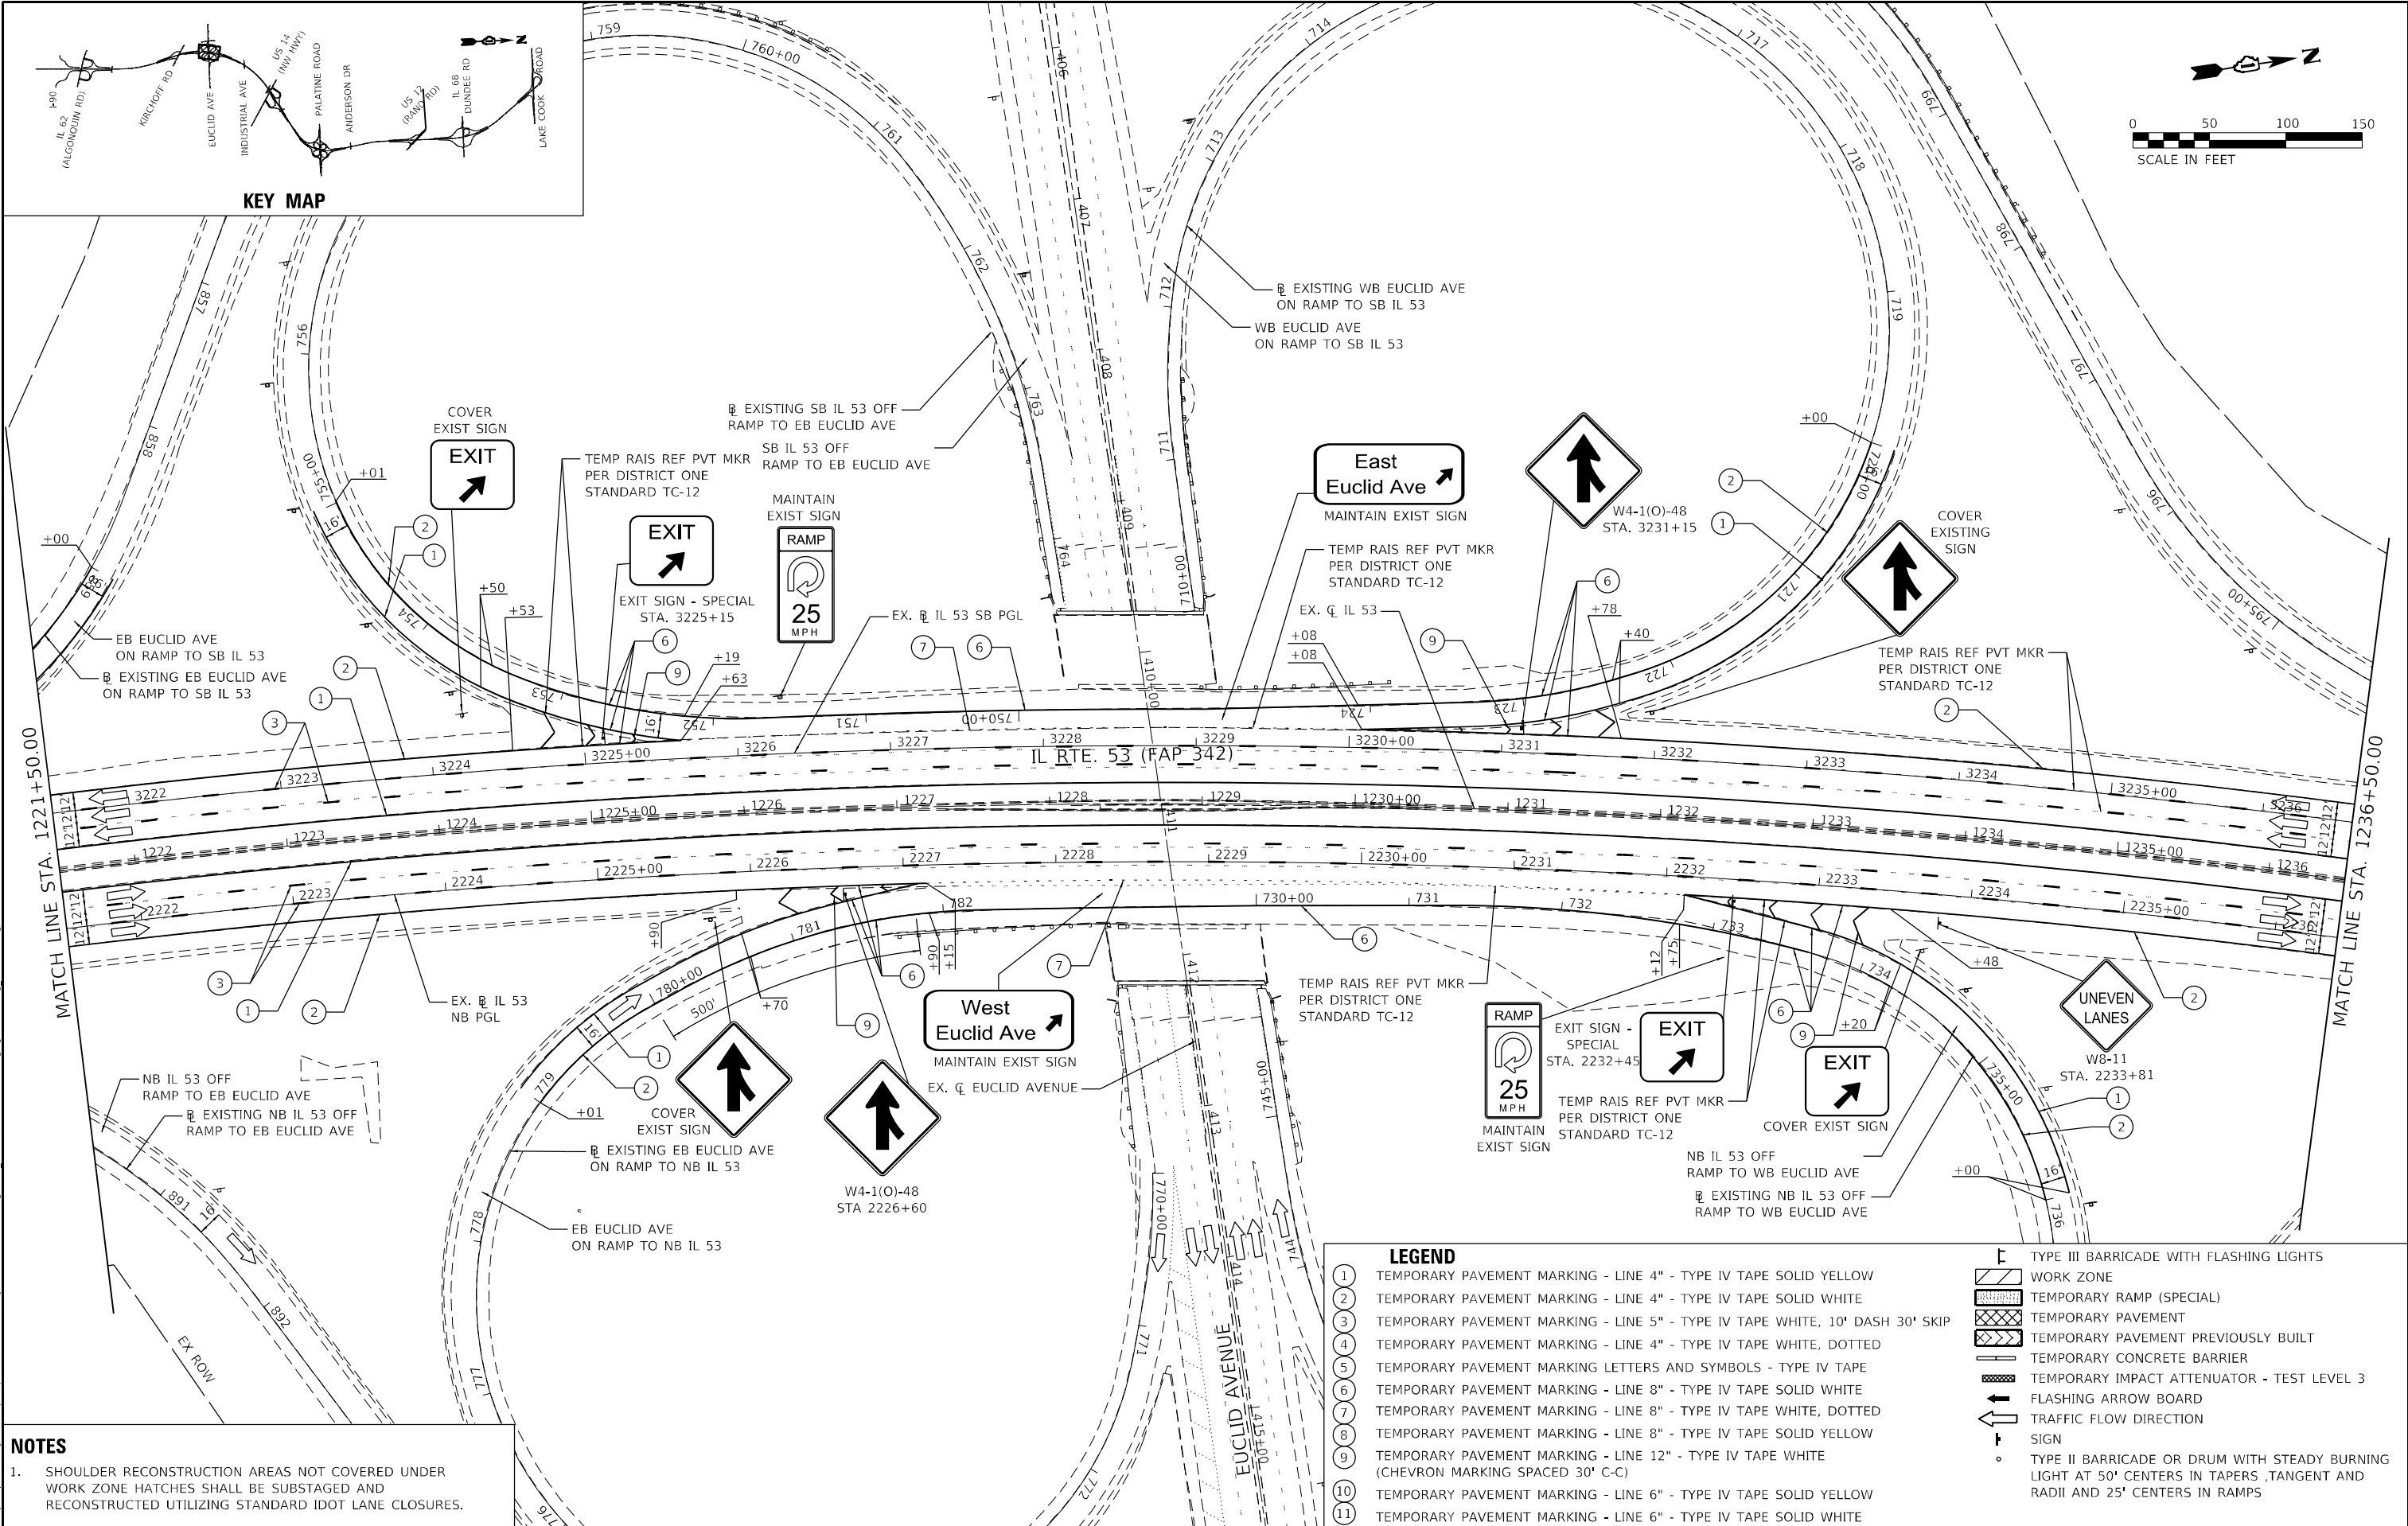

NOTES

1. SHOULDER RECONSTRUCTION AREAS NOT COVERED UNDER WORK ZONE HATCHES SHALL BE SUBSTAGED AND RECONSTRUCTED UTILIZING STANDARD IDOT LANE CLOSURES.

LEGEND

1

2

3

4

5

6

7

8

9

10

11

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

TYPE III BARRICADE WITH FLASHING LIGHTS

WORK ZONE

TEMPORARY RAMP (SPECIAL)

TEMPORARY PAVEMENT

TEMPORARY PAVEMENT PREVIOUSLY BUILT





TEMPORARY CONCRETE BARRIER

TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3

FLASHING ARROW BOARD

TRAFFIC FLOW DIRECTION SIGN


TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

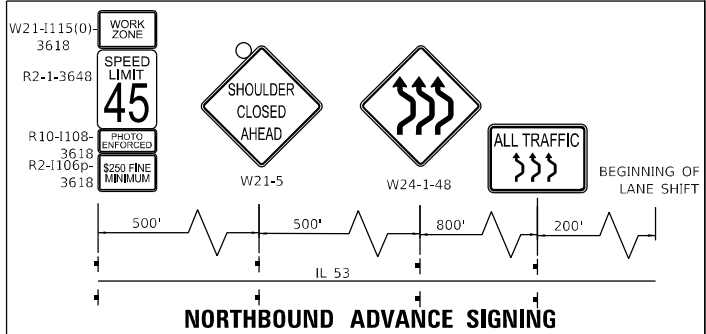
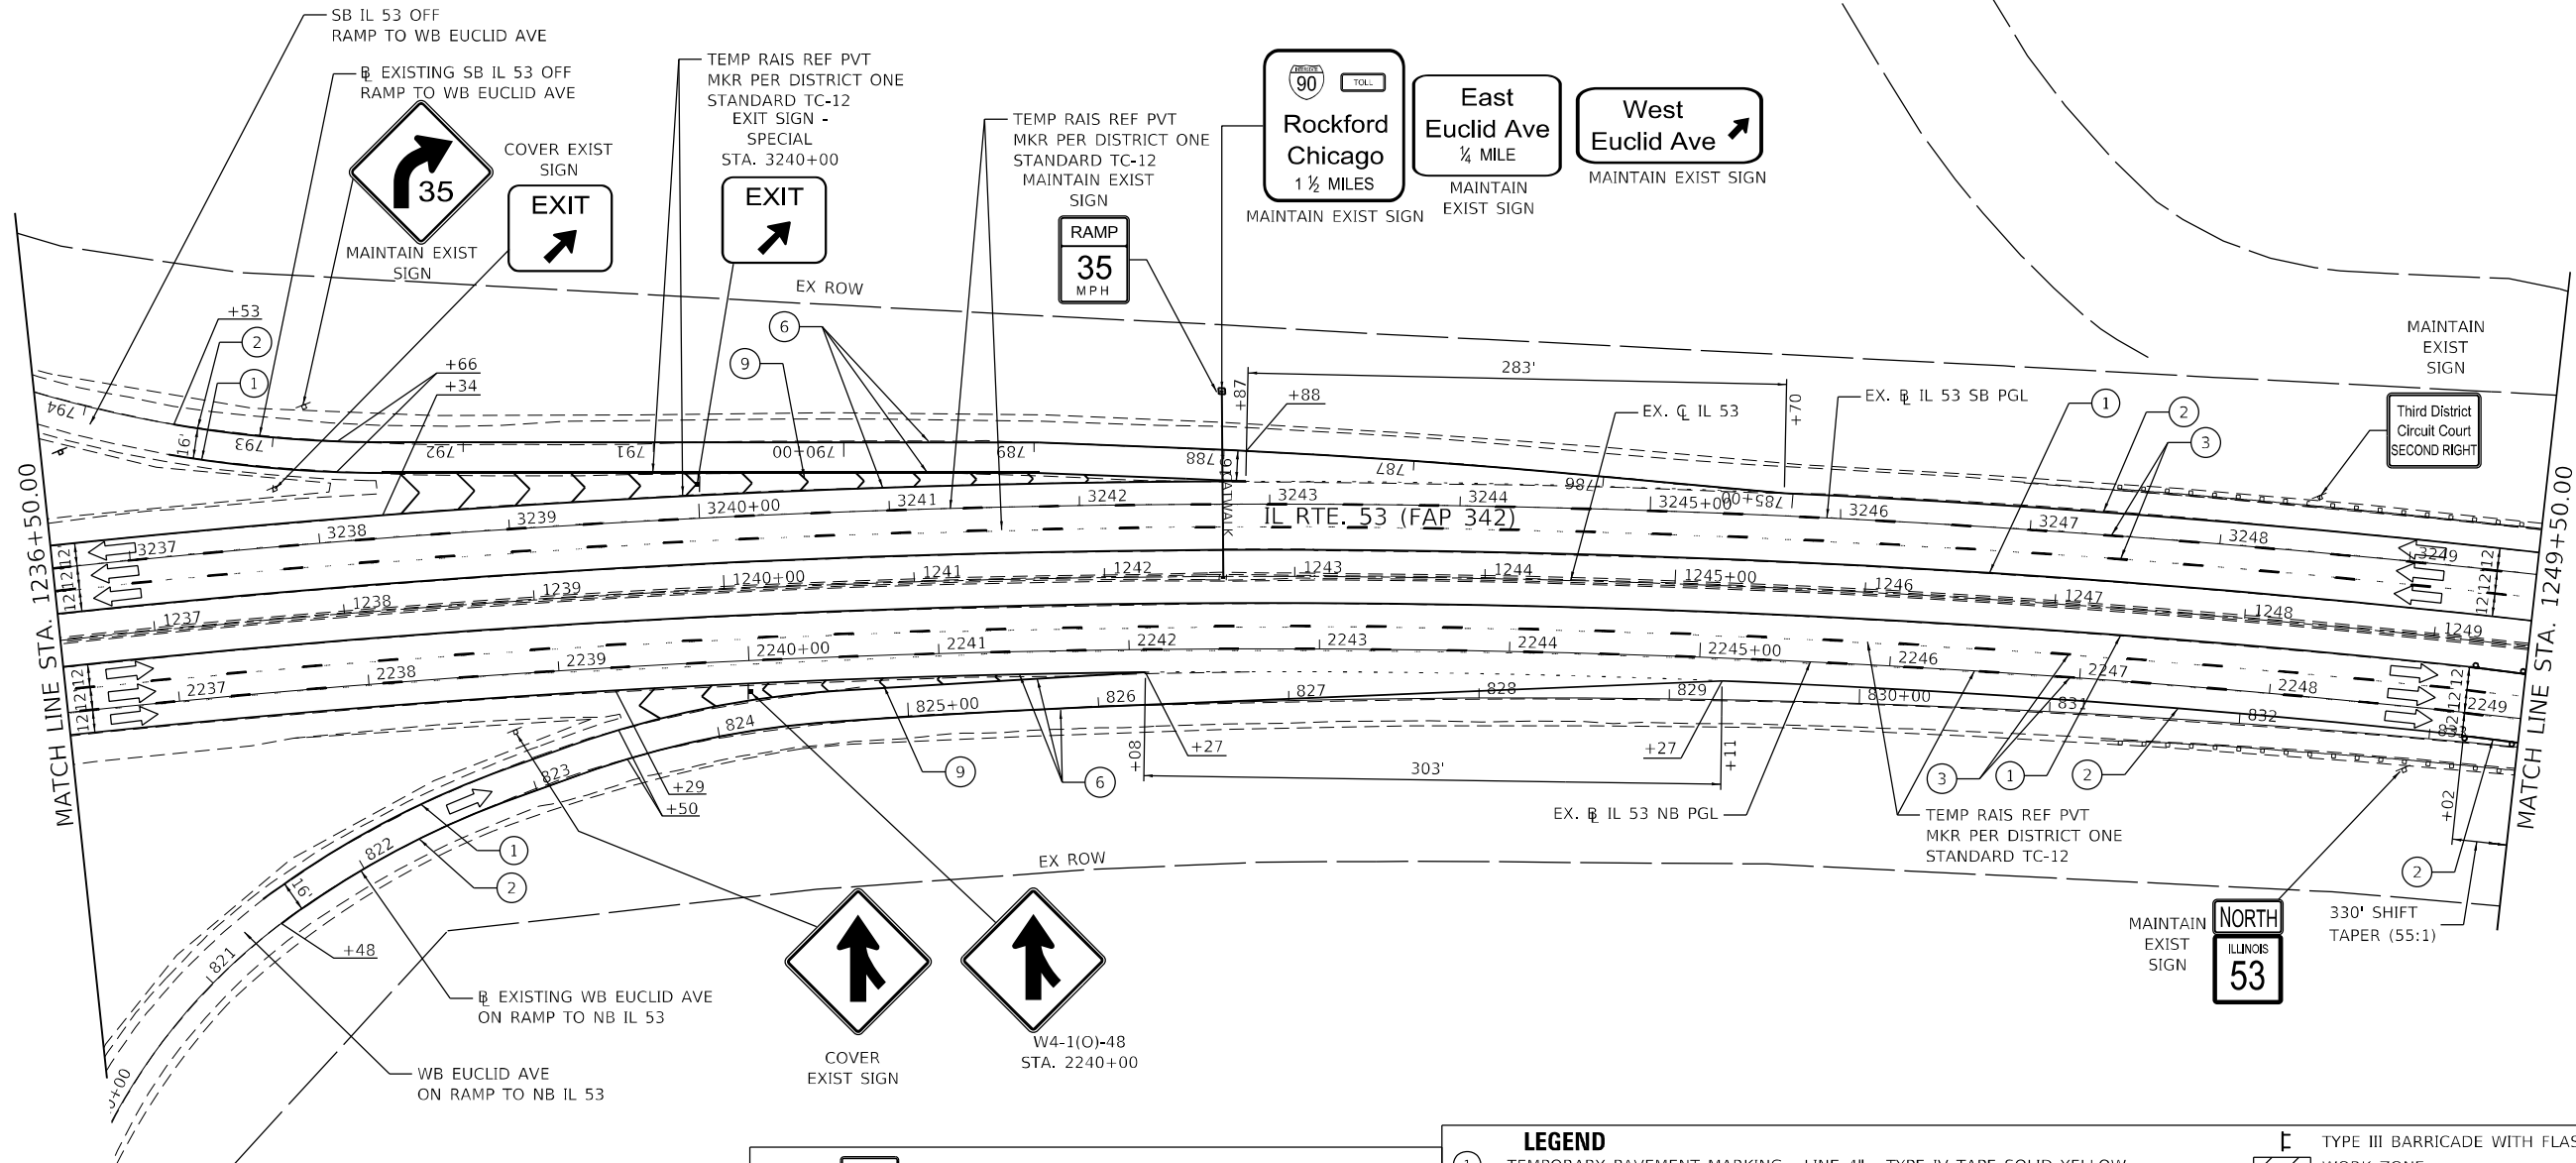

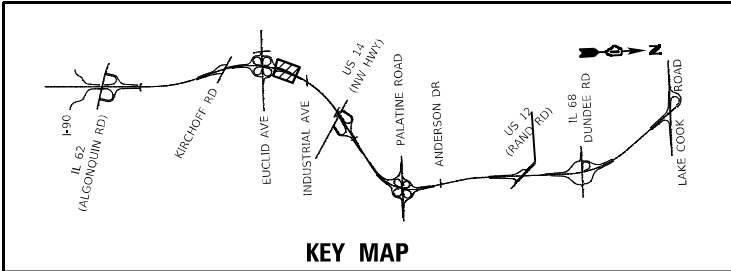


LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE		
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP		
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED		
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE		
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE		
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED		
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW		
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)		
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW		
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE		

11	TYPE III BARRICADE WITH FLASHING LIGHTS
12	WORK ZONE
13	TEMPORARY RAMP (SPECIAL)
14	TEMPORARY PAVEMENT
15	TEMPORARY PAVEMENT PREVIOUSLY BUILT
16	TEMPORARY CONCRETE BARRIER
17	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
18	FLASHING ARROW BOARD
19	TRAFFIC FLOW DIRECTION SIGN
20	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

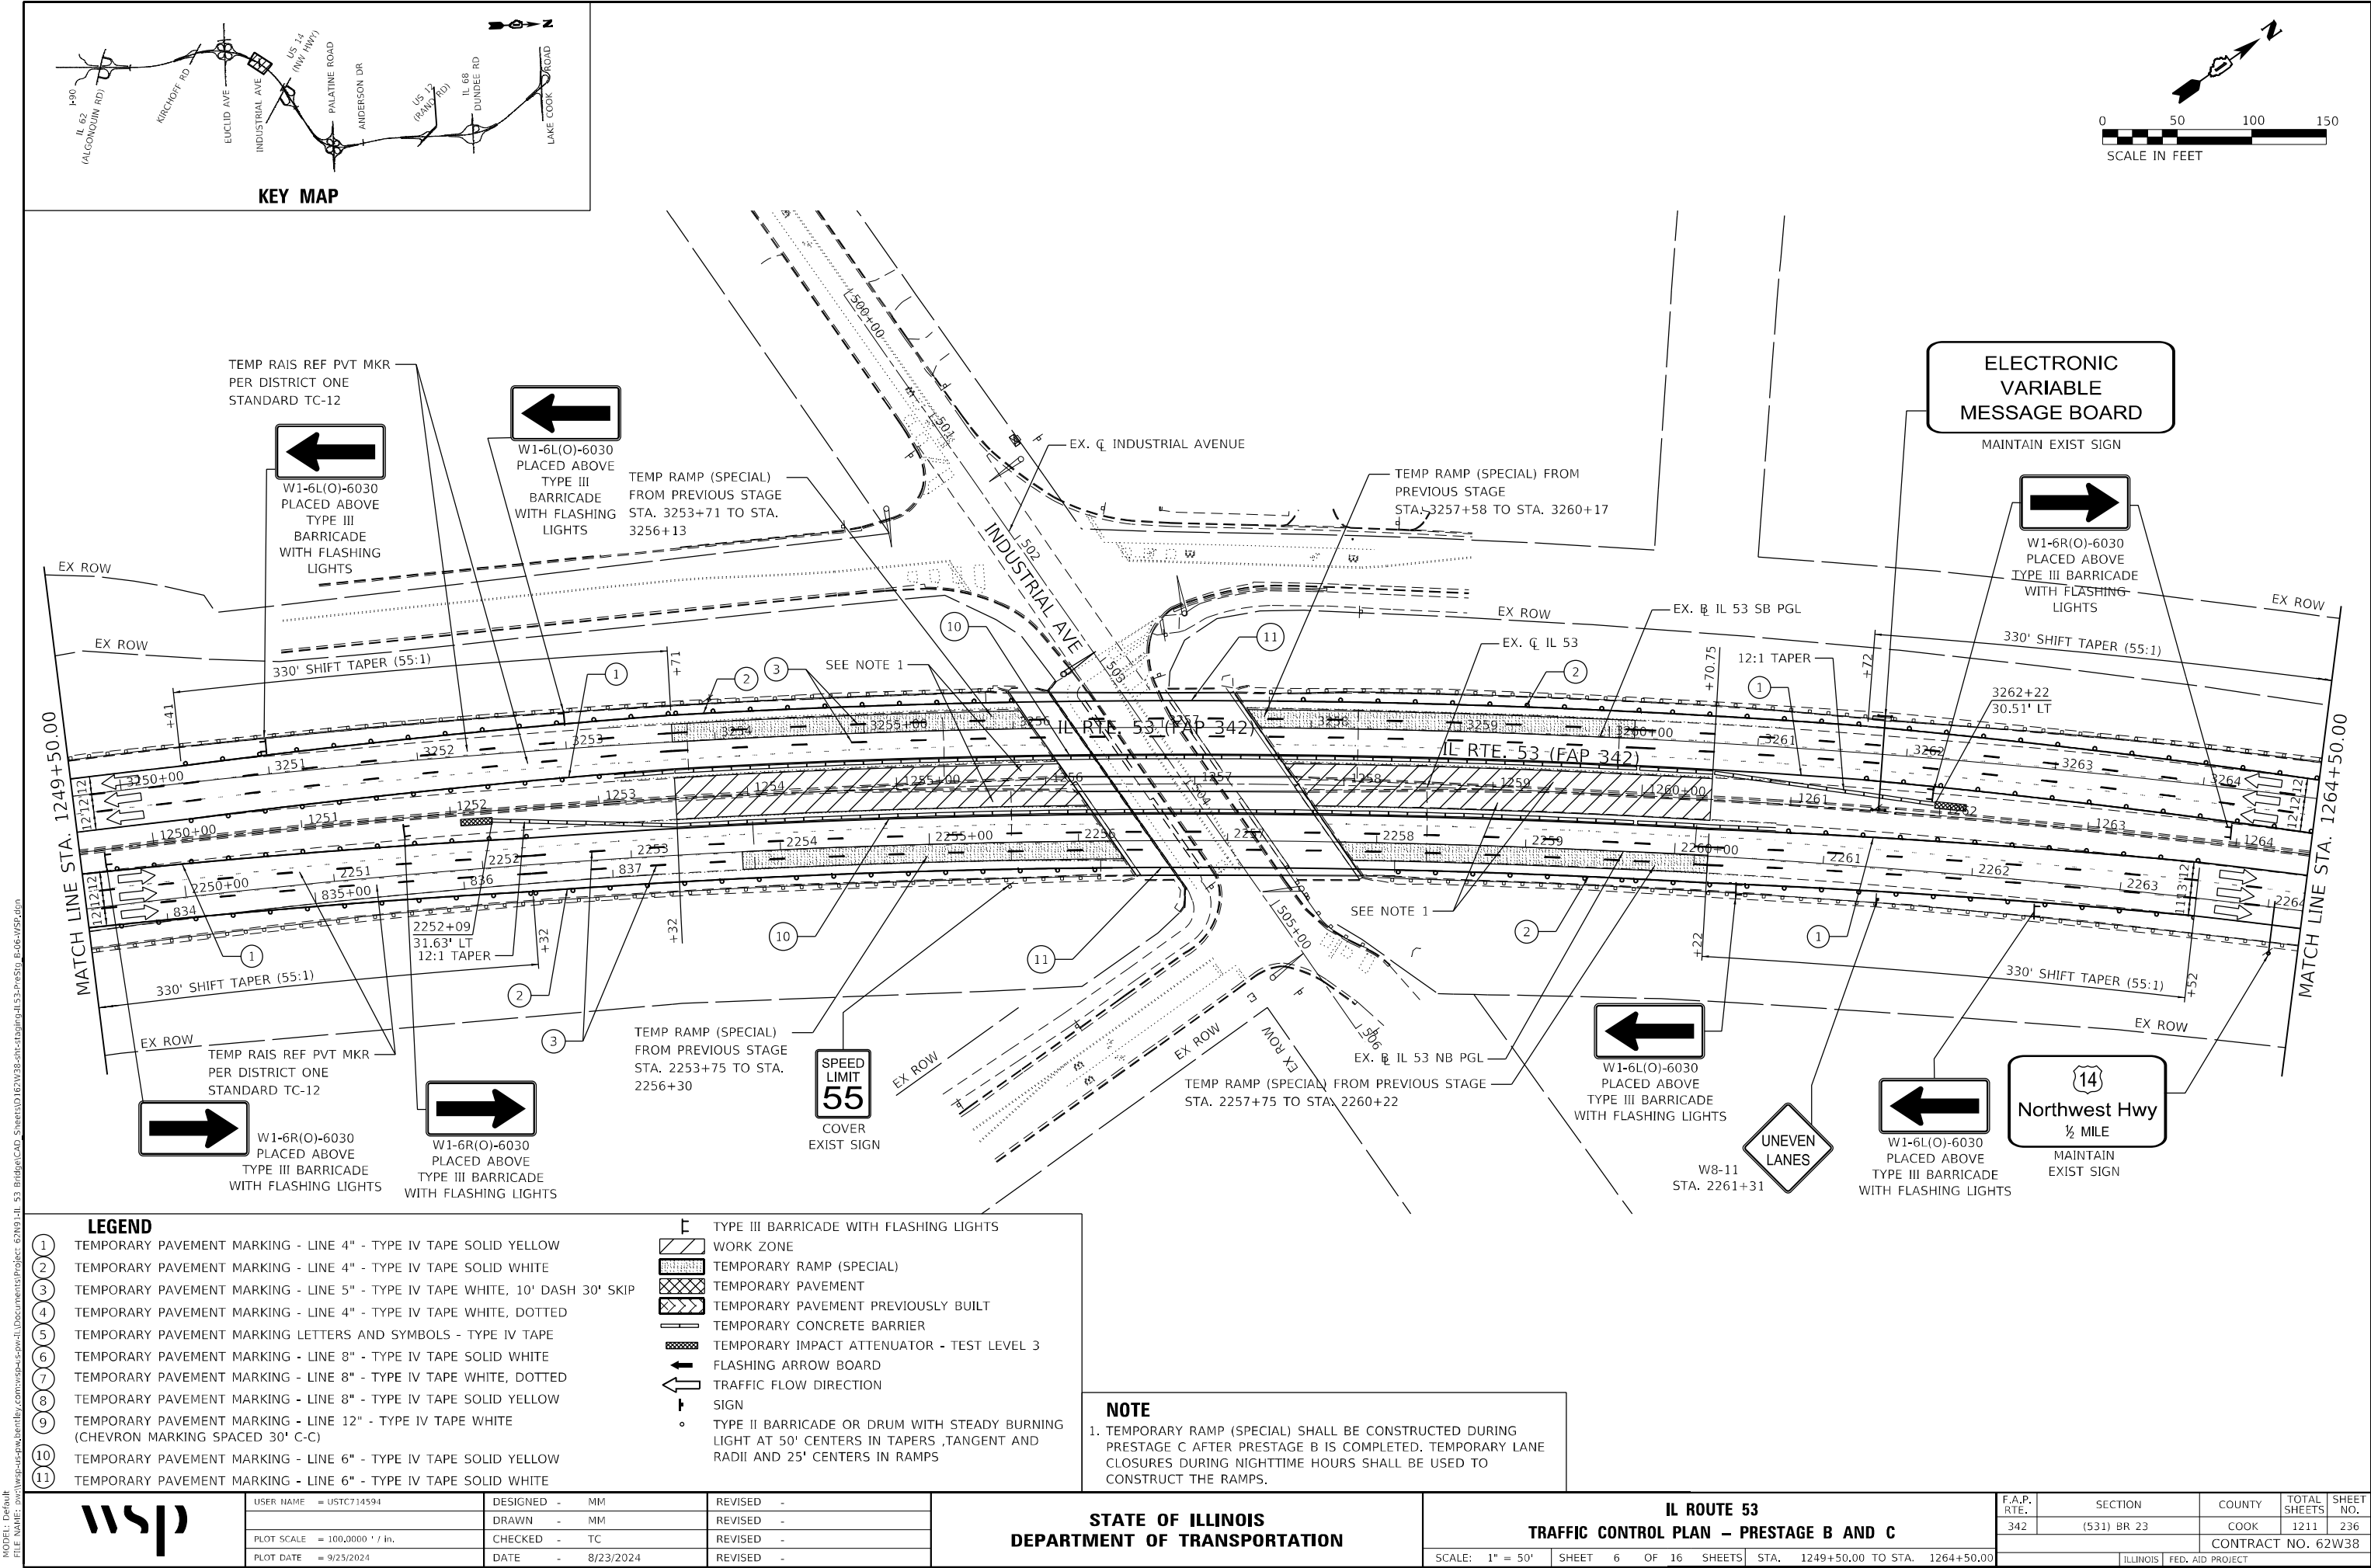

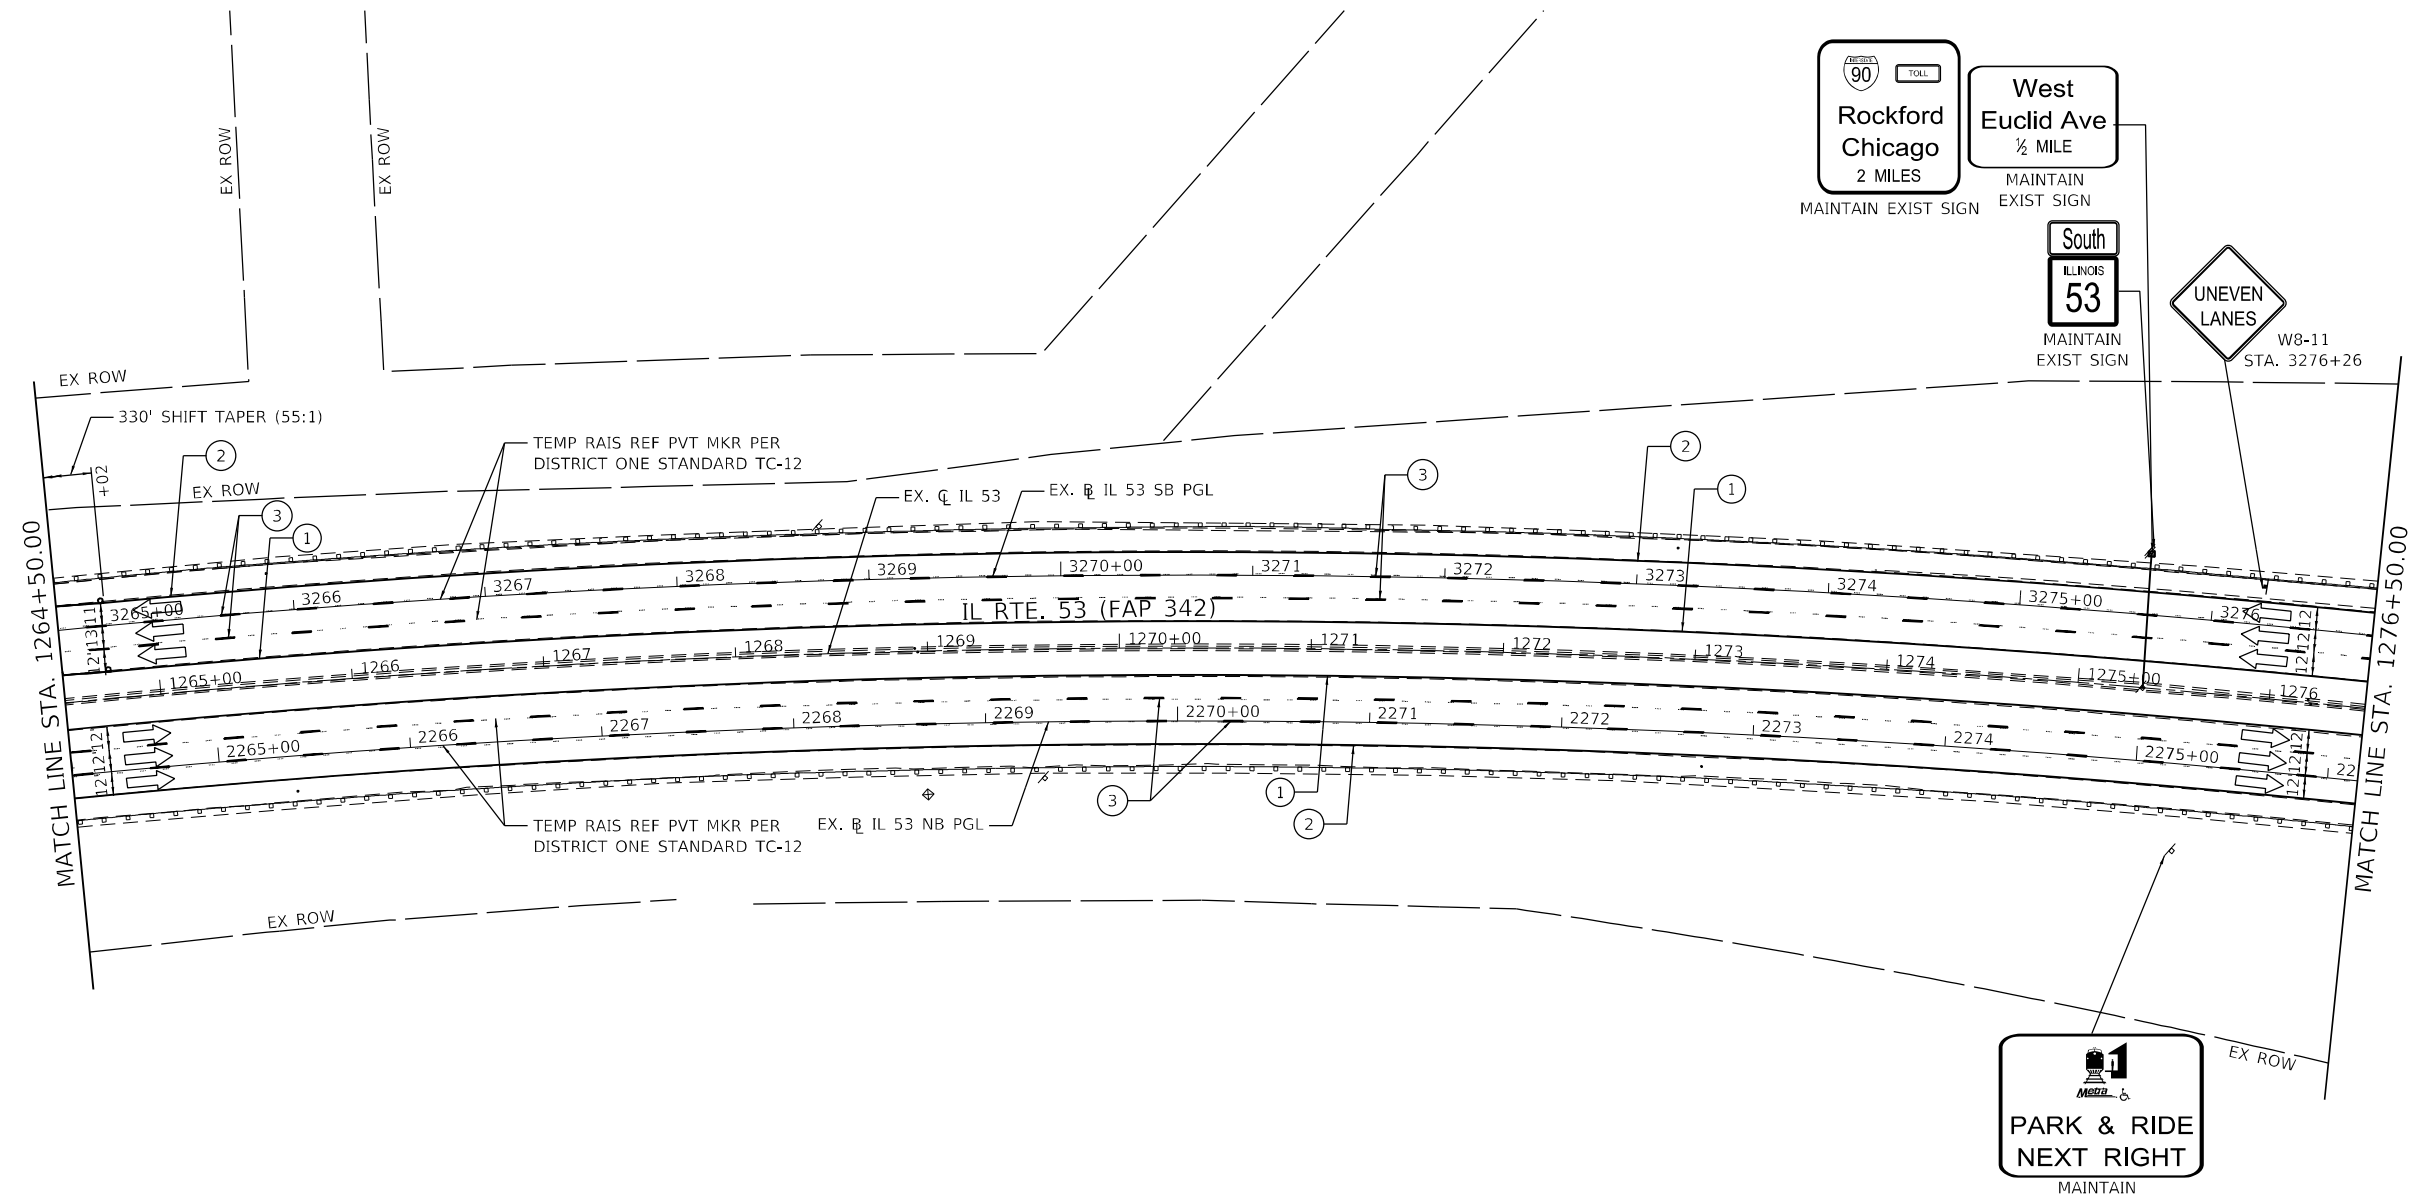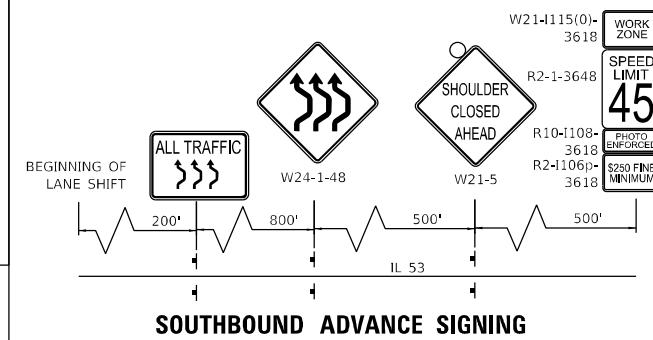

NORTHBOUND ADVANCE SIGNING

LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE


	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN – PRESTAGE B AND C

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	237
		CONTRACT NO. 62W38		
00	ILLINOIS	FED. AID PROJECT		

MODEL: Default
FILE NAME: c:\wsp-us-pw.bentley.com\wsp-us-pw-ll\Documents\Project_629\1-IL_53 Bridge\CAD_Sheets\0162W38-sh-staging-IL53-preSto-B-07-WSP.dgn

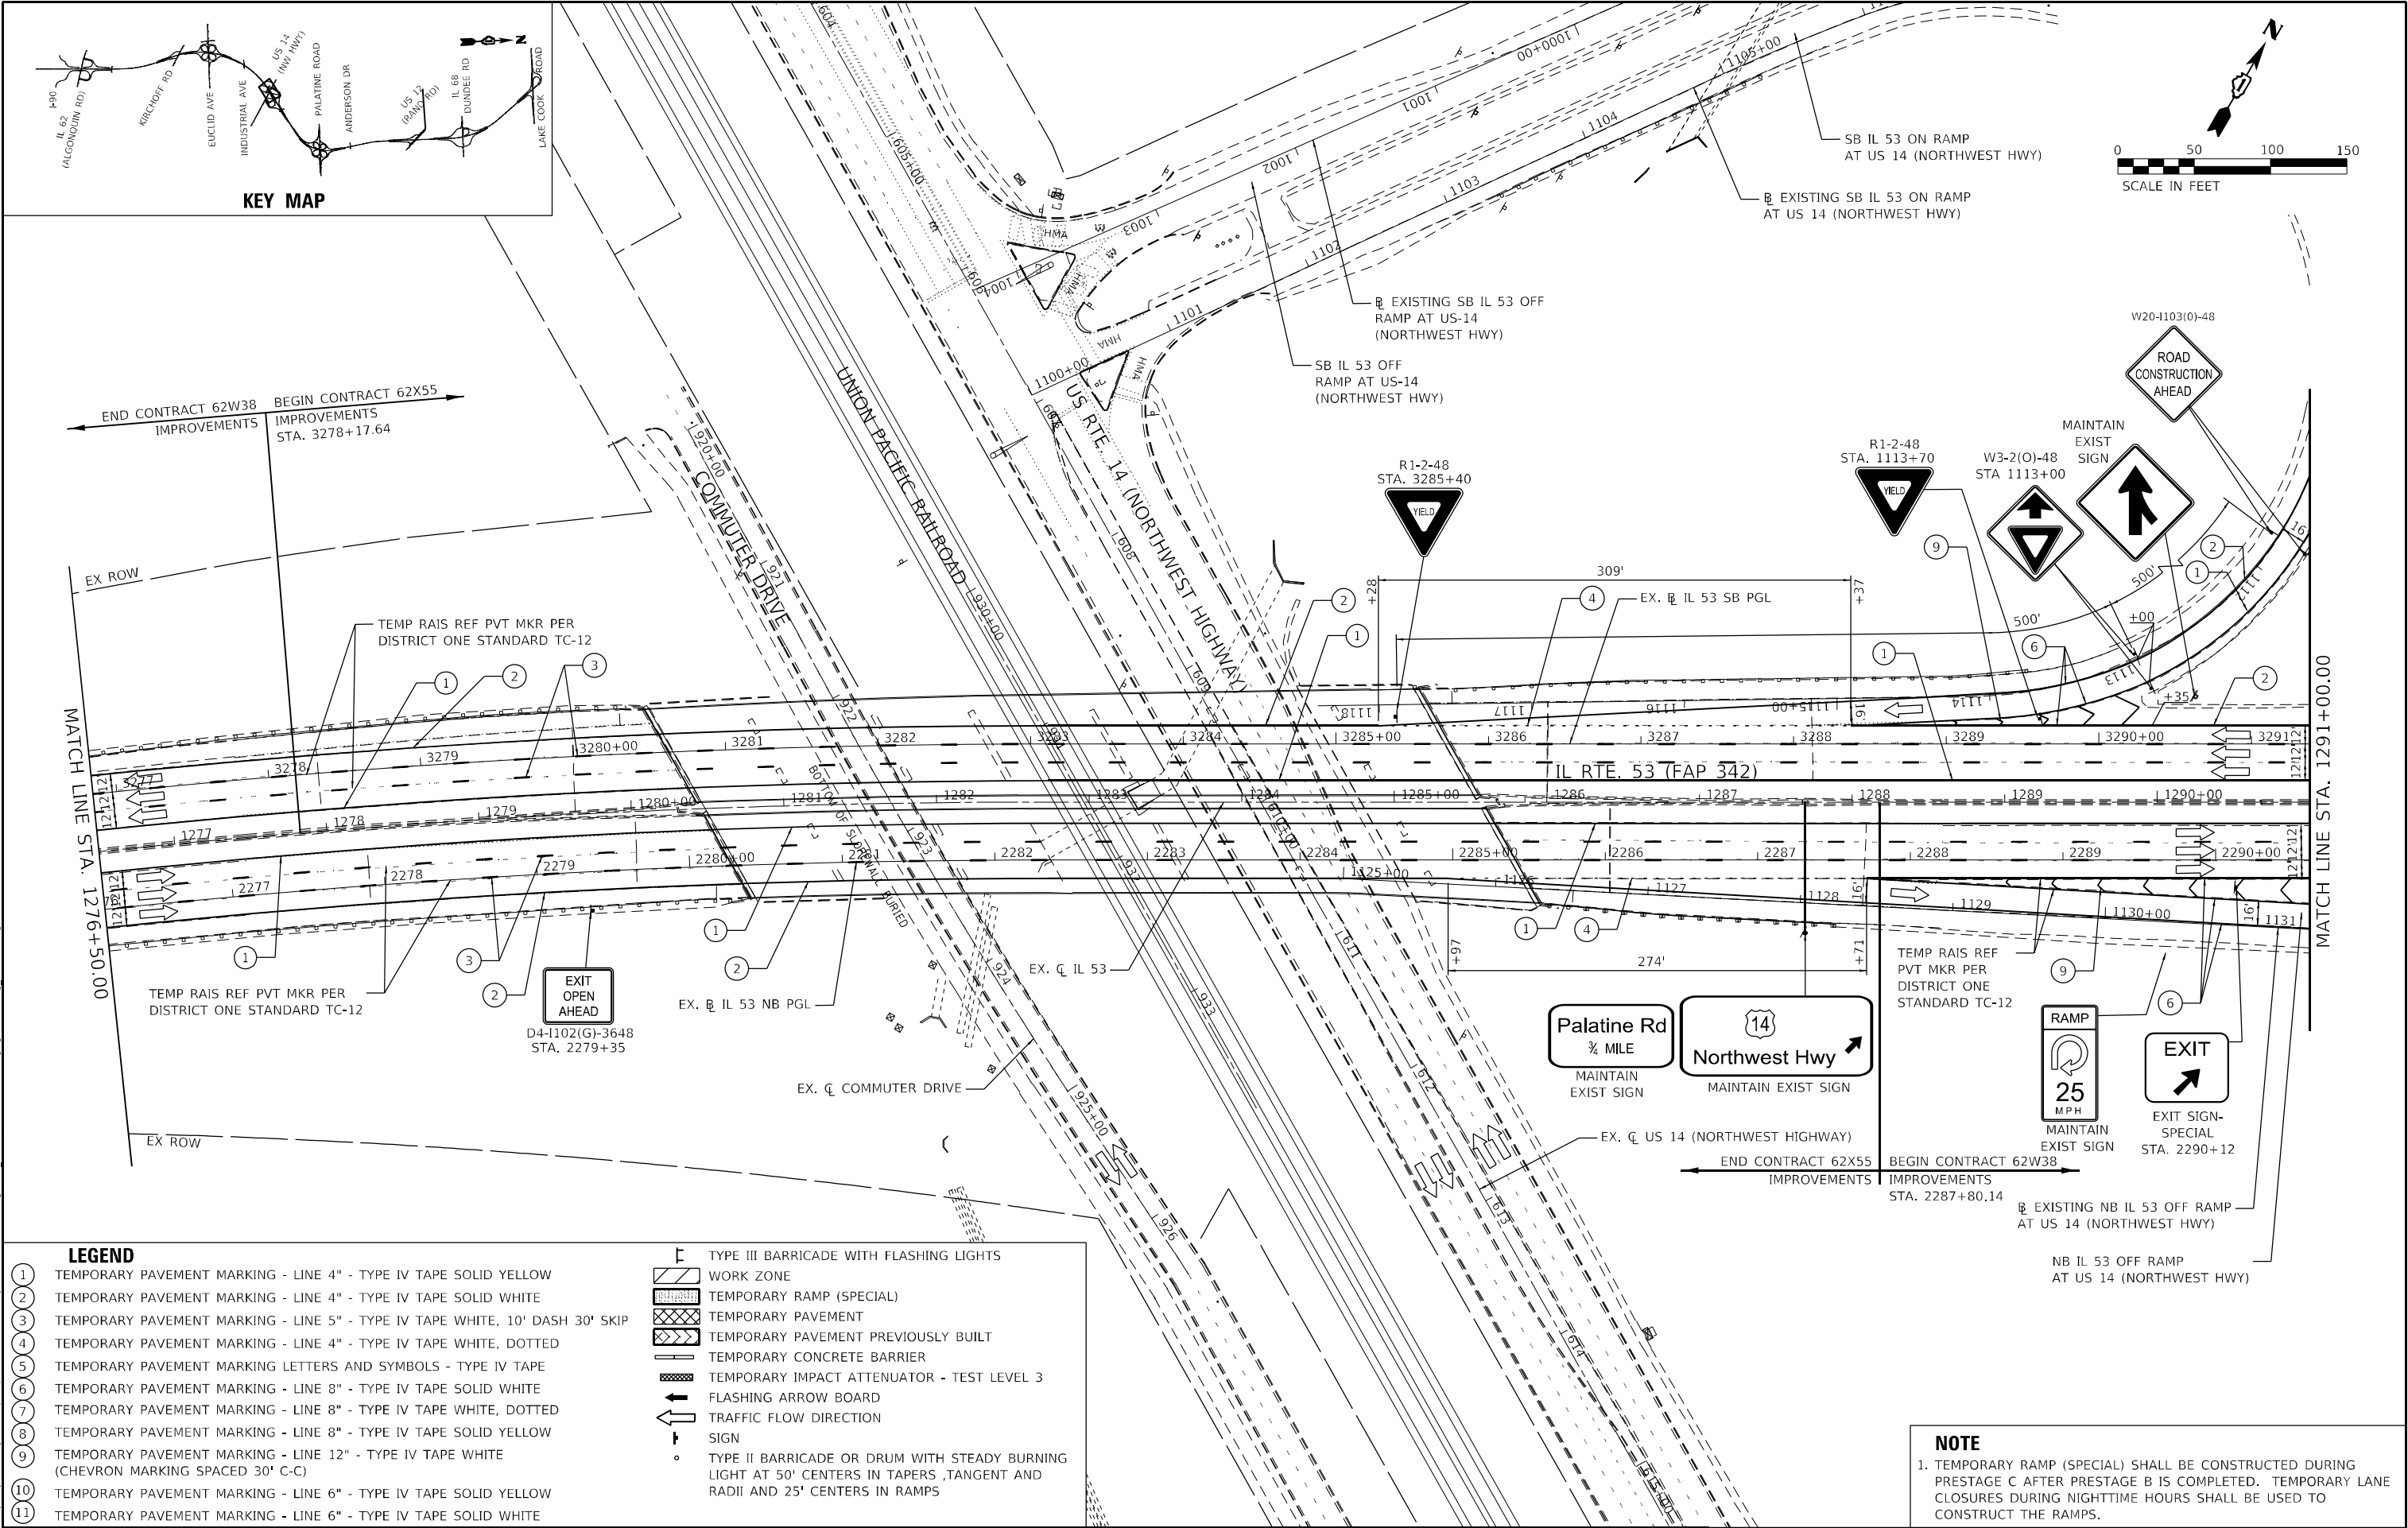

LEGEND

1

2

3

4

5

6

7

8

9

10

11

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

TYPE III BARRICADE WITH FLASHING LIGHTS

WORK ZONE

TEMPORARY RAMP (SPECIAL)

TEMPORARY PAVEMENT

TEMPORARY PAVEMENT PREVIOUSLY BUILT

TEMPORARY CONCRETE BARRIER

TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3

FLASHING ARROW BOARD

TRAFFIC FLOW DIRECTION SIGN

TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

USER NAME = USTC714594

DESIGNED - MM

REVISD -

DRAWN - MM

REVISD -

PLOT SCALE = 100,0000 ' / in.

CHECKED - TC

REVISD -

PLOT DATE = 9/23/2024

DATE - 8/23/2024

REVISD -

STATE OF ILLINOIS

DEPARTMENT OF TRANSPORTATION

IL ROUTE 53




TRAFFIC CONTROL PLAN - PRESTAGE B AND C

SCALE: 1" = 50'

SHEET 8 OF 16 SHEETS

STA. 1276+50.00 TO STA. 1291+00.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	238
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

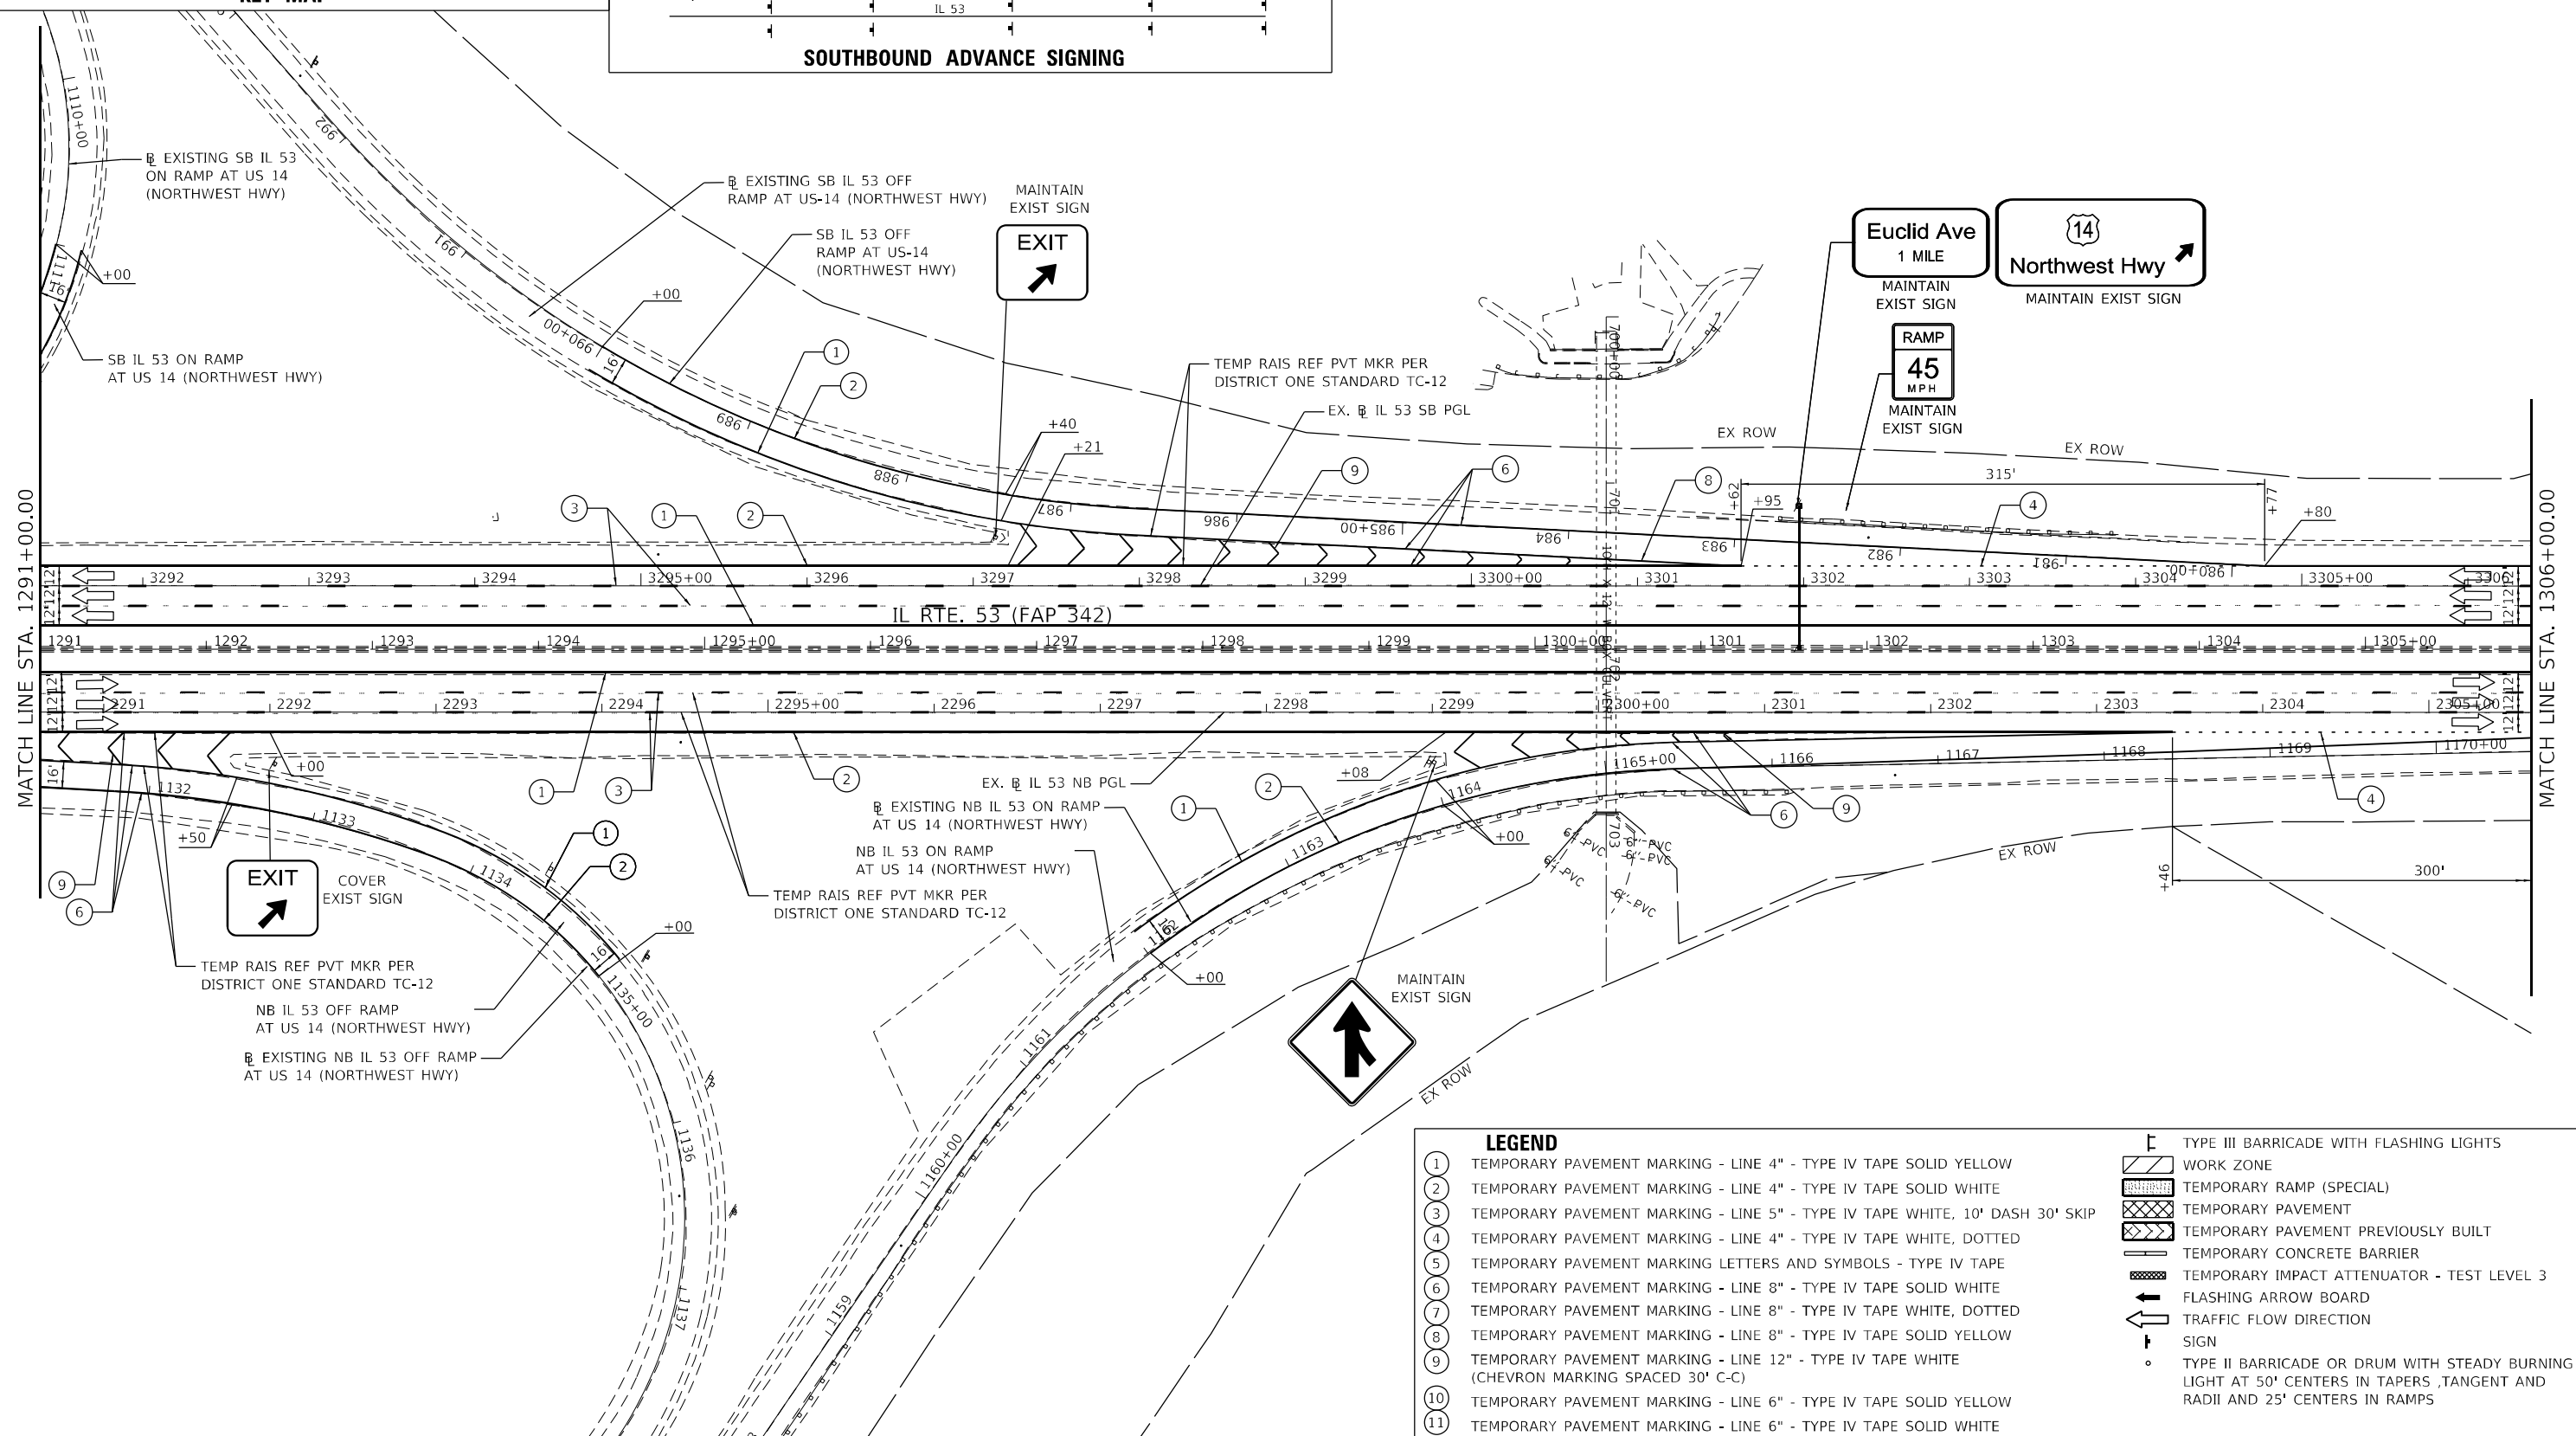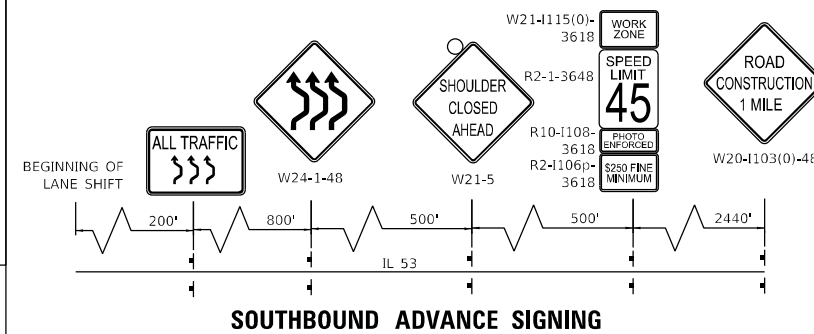



USER NAME = USTC714594	DESIGNED - MM
	DRAWN - MM
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC
PLOT DATE = 9/25/2024	DATE - 8/23/2024

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**





IL ROUTE 53
TRAFFIC CONTROL PLAN – PRESTAGE B AND C

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	239
		CONTRACT NO. 62W38		
00		ILLINOIS	FED. AID PROJECT	

MODEL: Default
FILE NAME: c:\wsp-us-pw-bentley.com\wsp-us-pw-ll\Documents\Project: 62N91-IL: 53 Bridge\CAD Sheets\0162N38-shr-stairing-IL53-PreSta_B-09-wSP.dgn

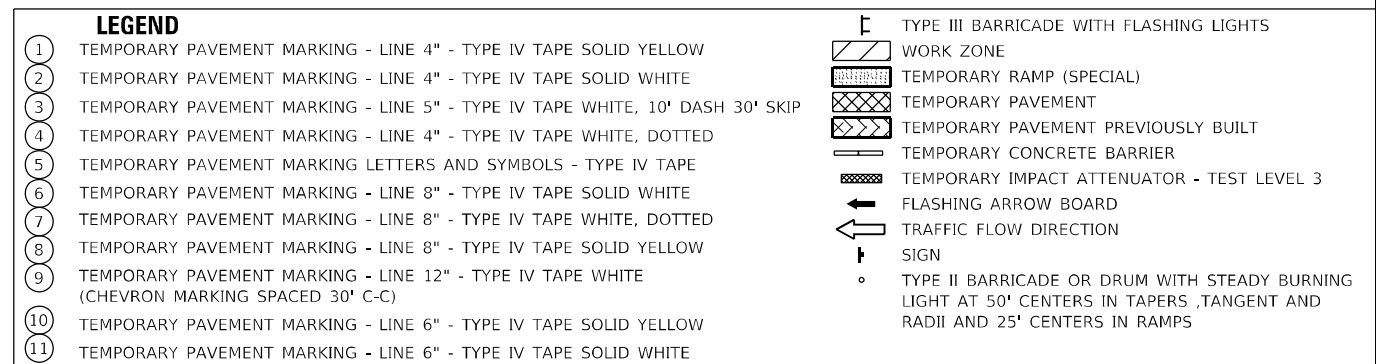


	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE B AND C					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -							342	(531) BR 23	COOK	1211	240
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		CONTRACT NO. 62W38									
					SCALE: 1" = 50'	SHEET 10 OF 16 SHEETS	STA. 1306+00.00 TO STA. 1321+00.00		ILLINOIS FED. AID PROJECT					

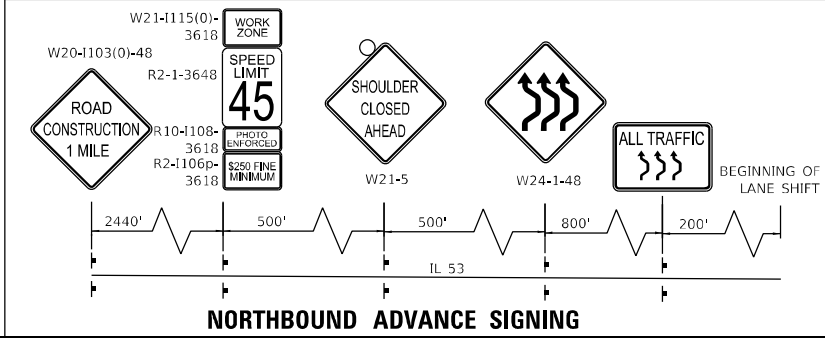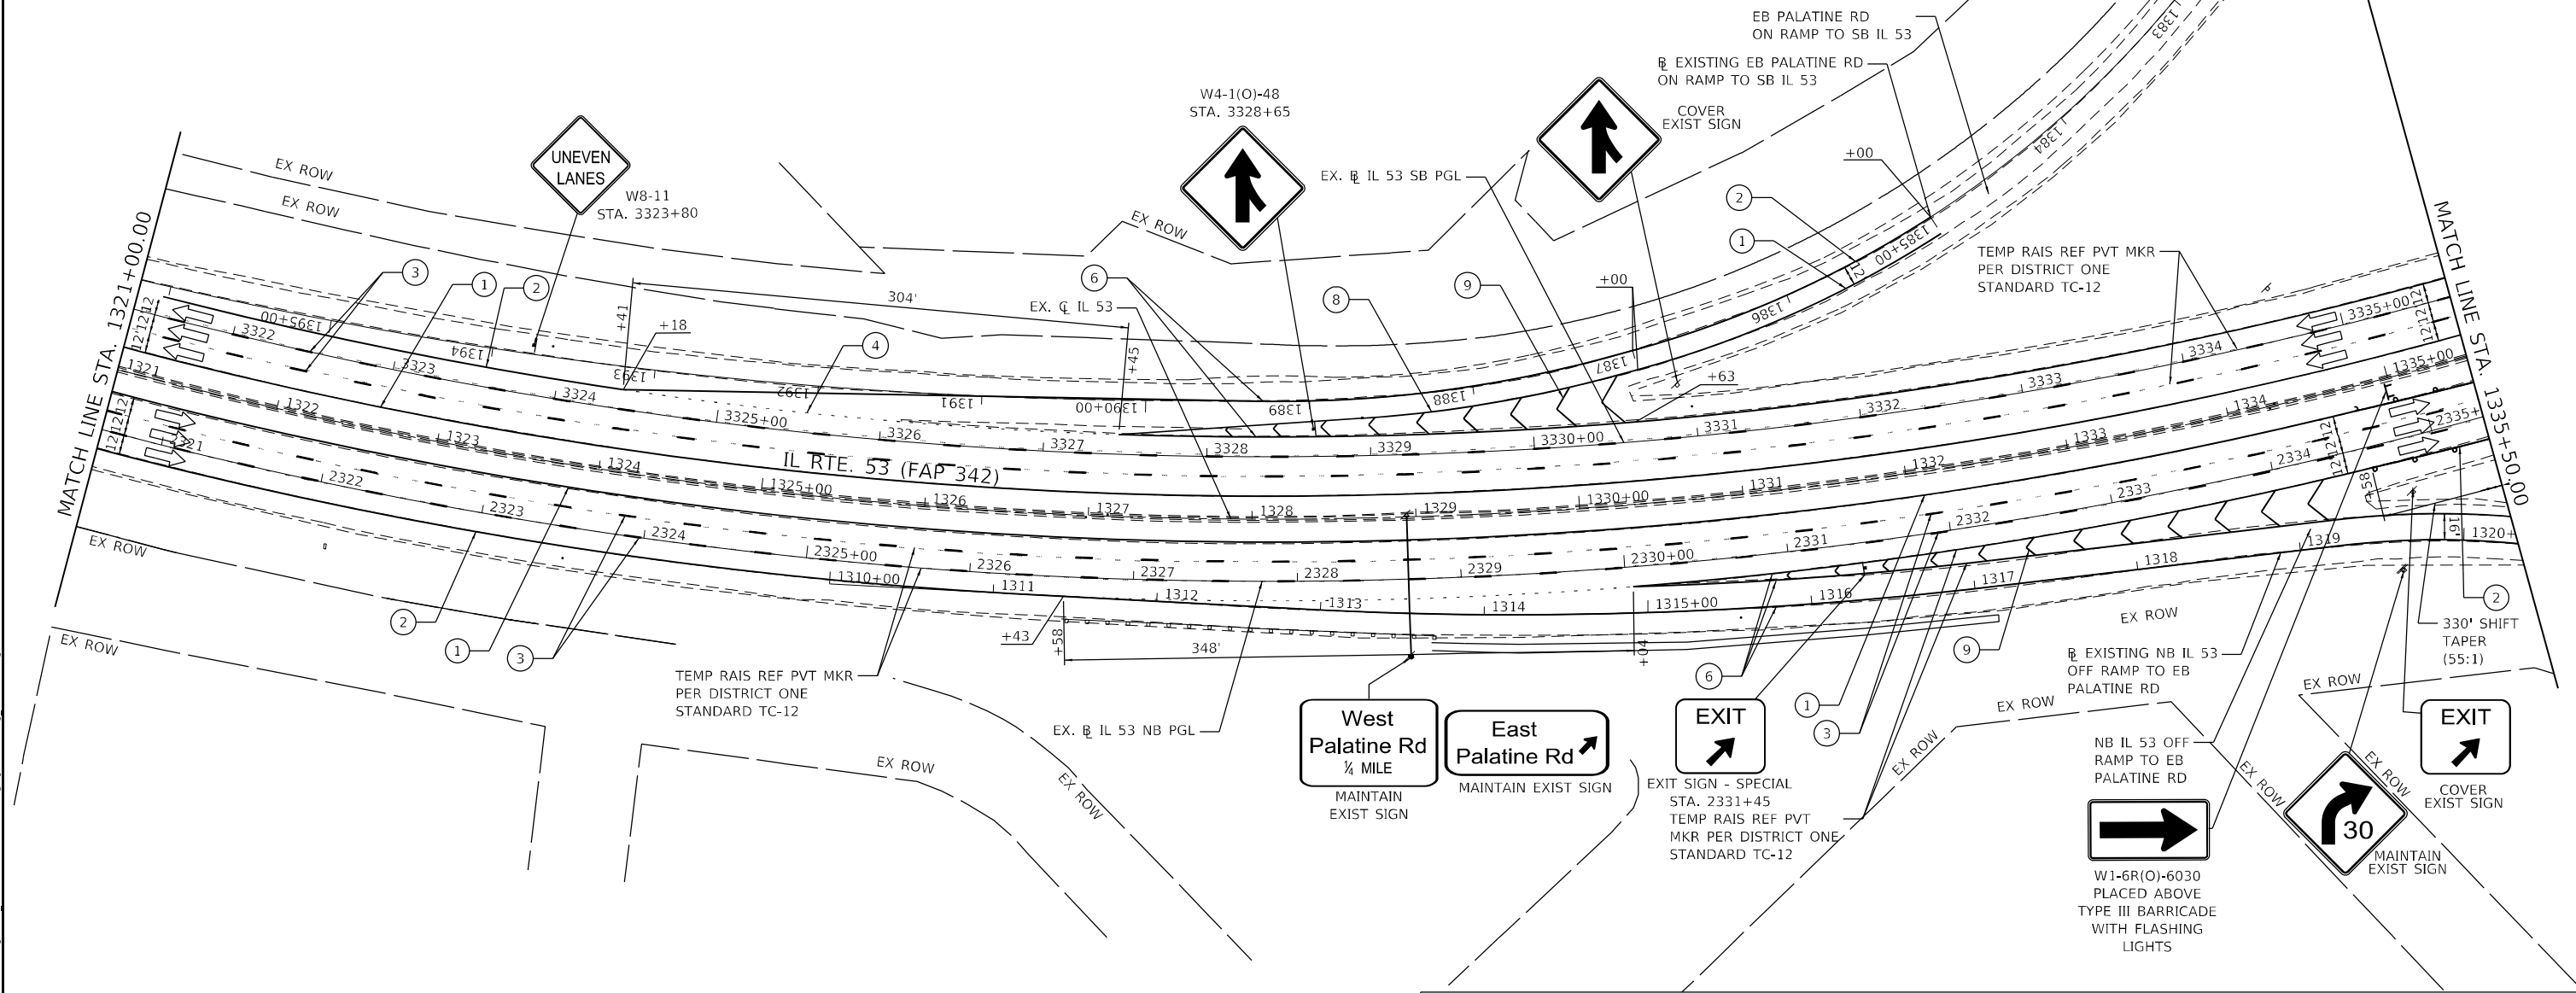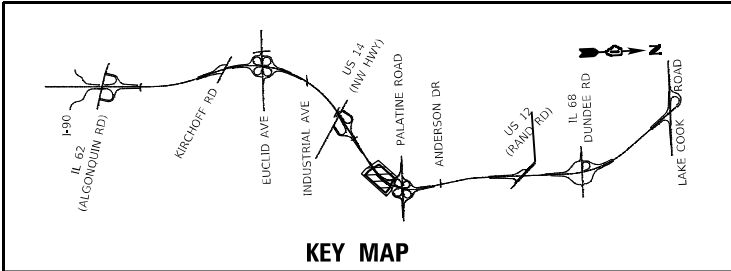

LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

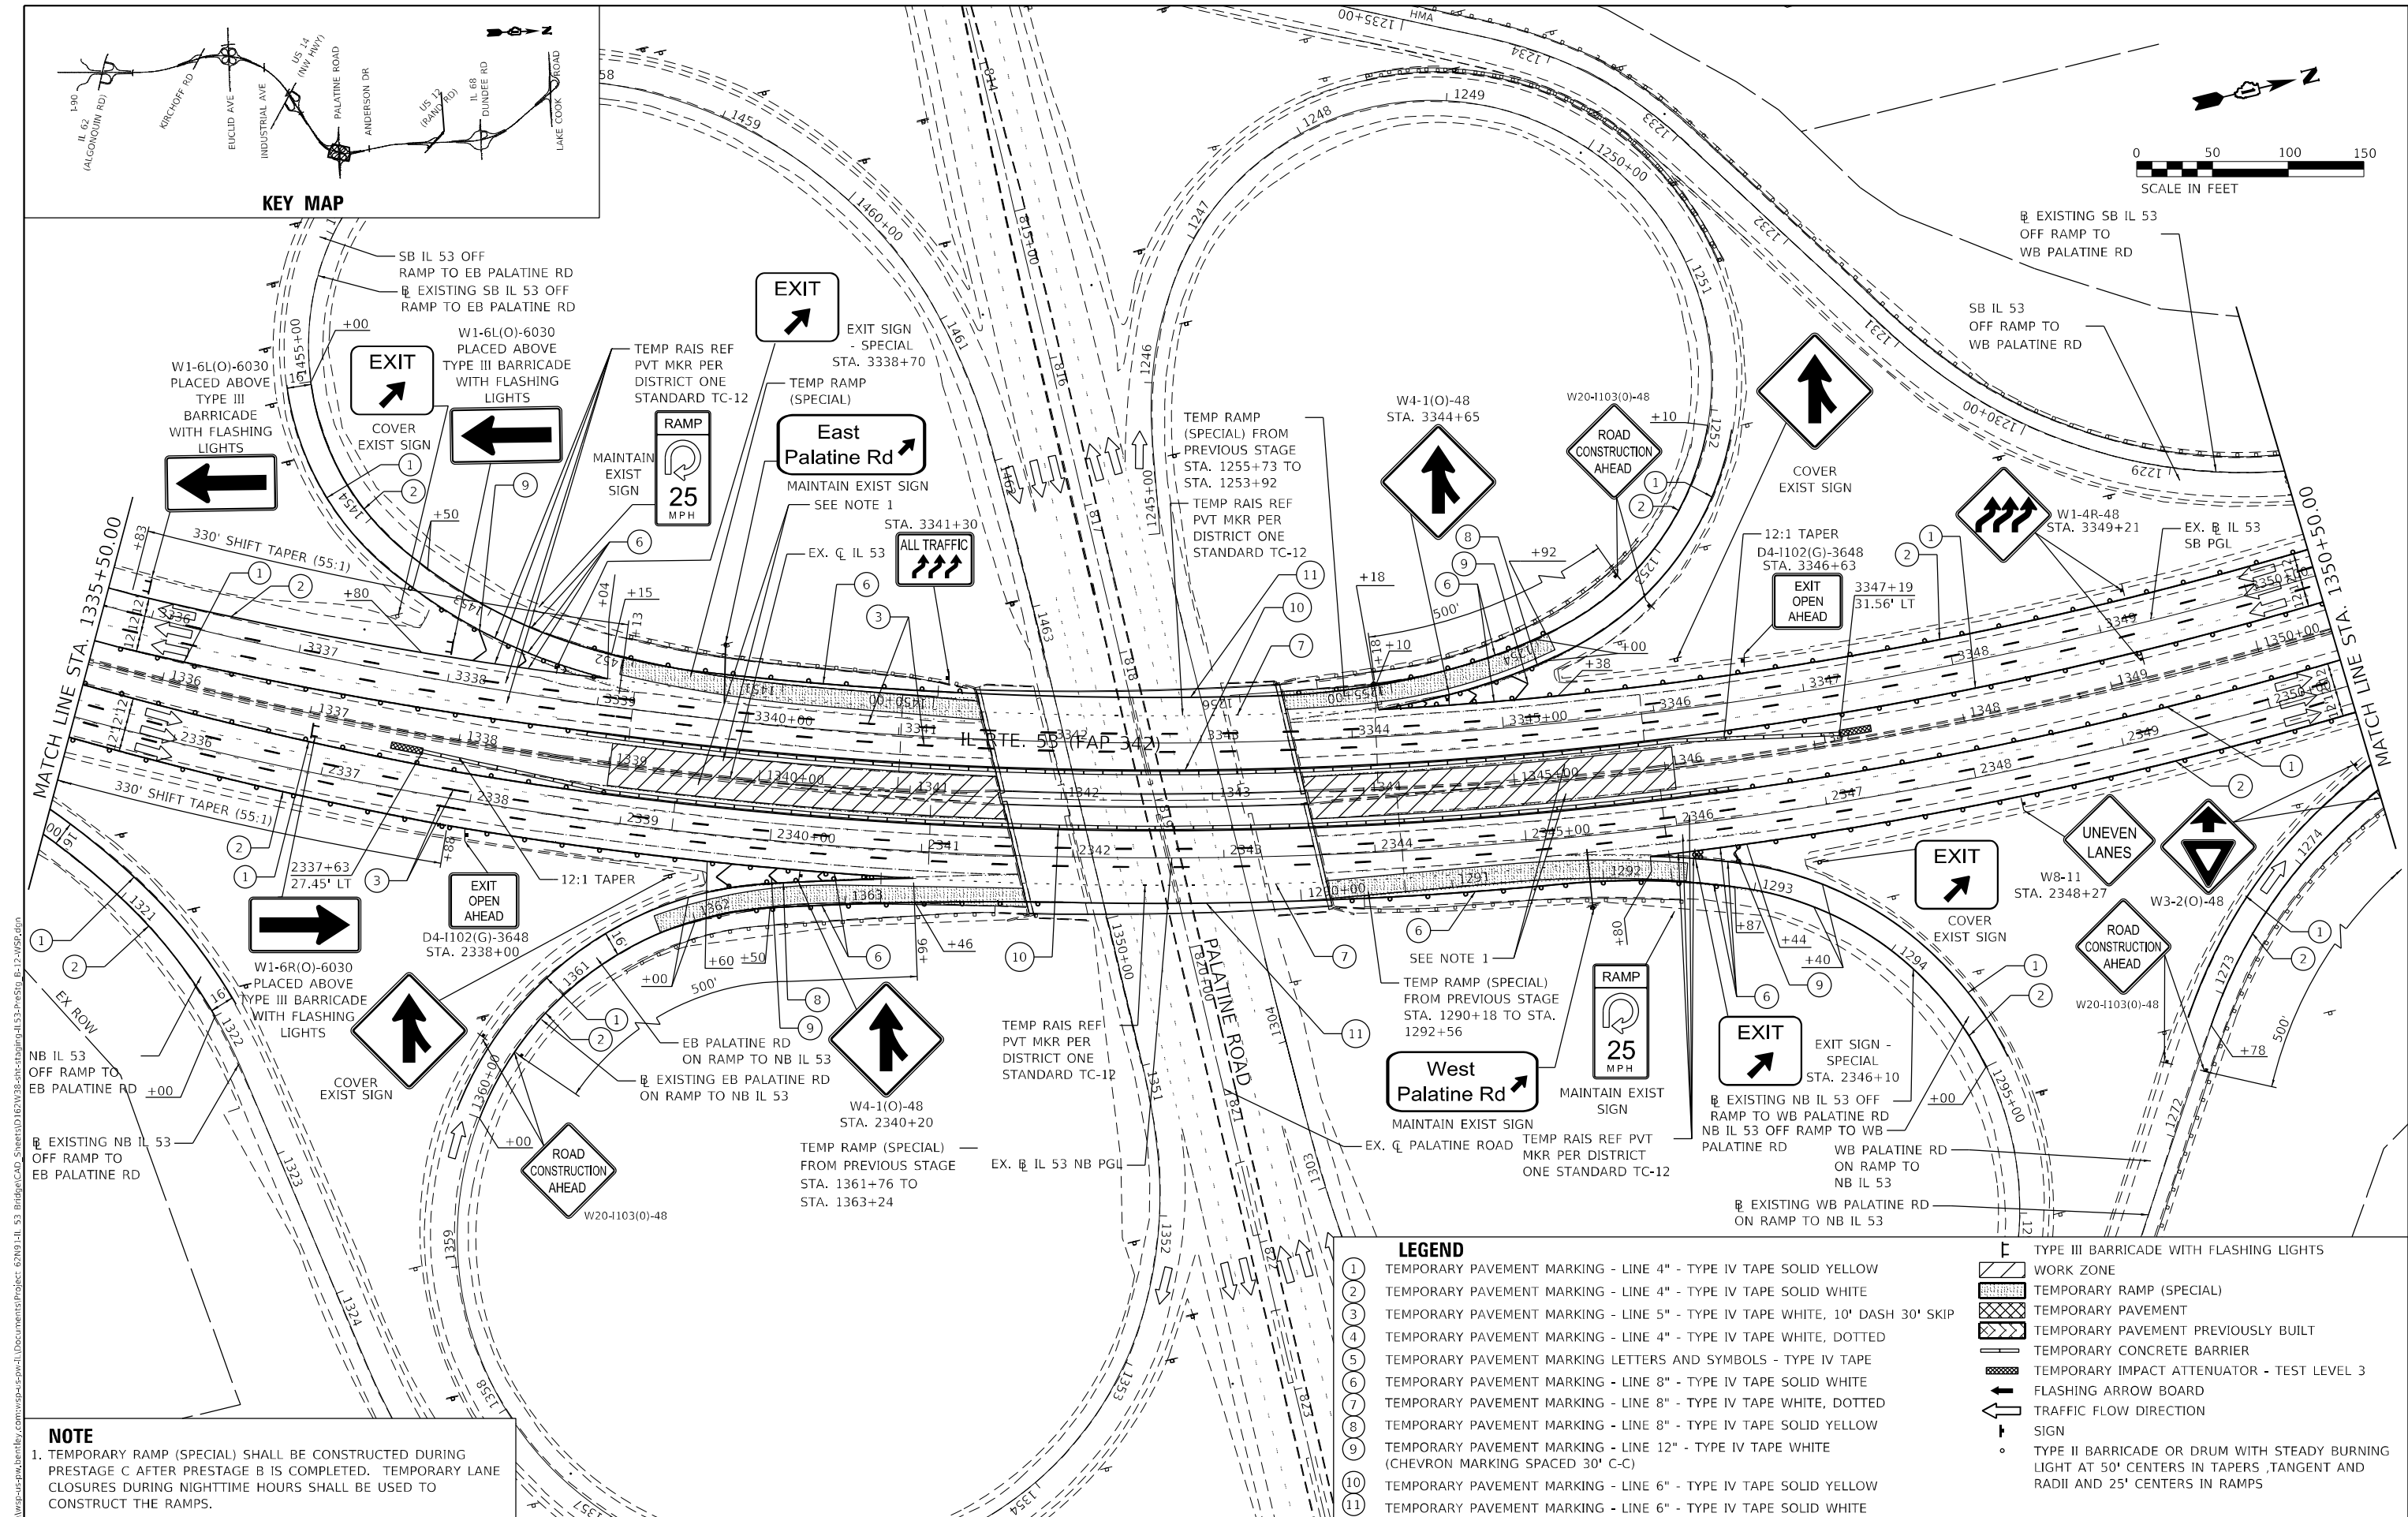



KEY MAP



0 50 100 150
SCALE IN FEET

NOTE
1. TEMPORARY RAMP (SPECIAL) SHALL BE CONSTRUCTED DURING PRESTAGE C AFTER PRESTAGE B IS COMPLETED. TEMPORARY LANE CLOSURES DURING NIGHTTIME HOURS SHALL BE USED TO CONSTRUCT THE RAMPS.

LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	TYPE III BARRICADE WITH FLASHING LIGHTS
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE	WORK ZONE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP	TEMPORARY RAMP (SPECIAL)
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY PAVEMENT
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE	TEMPORARY PAVEMENT PREVIOUSLY BUILT
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE	TEMPORARY CONCRETE BARRIER
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW	FLASHING ARROW BOARD
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)	TRAFFIC FLOW DIRECTION SIGN
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW	SIGN
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

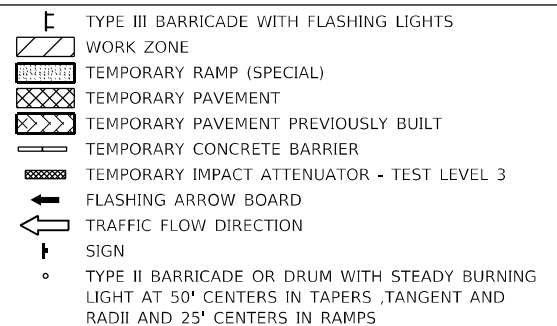



MATCH LINE STA. 1370+50.00

MAINTAIN
EXIST SIGN

2)

1

A. $2368+46$

— TEMP RAMP (SPECIAL) FROM PREVIOUS STAGE
STA. 2365+50 TO STA. 2368+46



①	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION
	SIGN
o	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS ,TANGENT AND RADII AND 25' CENTERS IN RAMPS

1. TEMPORARY RAMP (SPECIAL) SHALL BE CONSTRUCTED DURING PRESTAGE C AFTER PRESTAGE B IS COMPLETED. TEMPORARY LANE CLOSURES DURING NIGHTTIME HOURS SHALL BE USED TO CONSTRUCT THE RAMPS.




**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**IL ROUTE 53
TRAFFIC CONTROL PLAN – PRESTAGE B AND C**



SCALE: 1" = 50'	SHEET 14 OF 16 SHEETS	STA. 1360+00.00 TO STA. 1370+00.00
-----------------	-----------------------	------------------------------------

ILLINOIS	FED. AID PROJECT
----------	------------------




- | LEGEND | | | |
|--------|---|---|--|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW |  | TYPE III BARRICADE WITH FLASHING LIGHTS |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE |  | WORK ZONE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP |  | TEMPORARY RAMP (SPECIAL) |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED |  | TEMPORARY PAVEMENT |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE |  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE |  | TEMPORARY CONCRETE BARRIER |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED |  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW |  | FLASHING ARROW BOARD |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C) |  | TRAFFIC FLOW DIRECTION |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW |  | SIGN |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE |  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – PRESTAGE B AND C					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -							342	(531) BR 23	COOK	1211	245
	PLOT SCALE = 100,000' / in.	CHECKED - TC	REVISED -							CONTRACT NO. 62W38				
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -											
					SCALE: 1" = 50'	SHEET 15 OF 16 SHEETS	STA. 1370+50.00 TO STA. 1378+50.00							

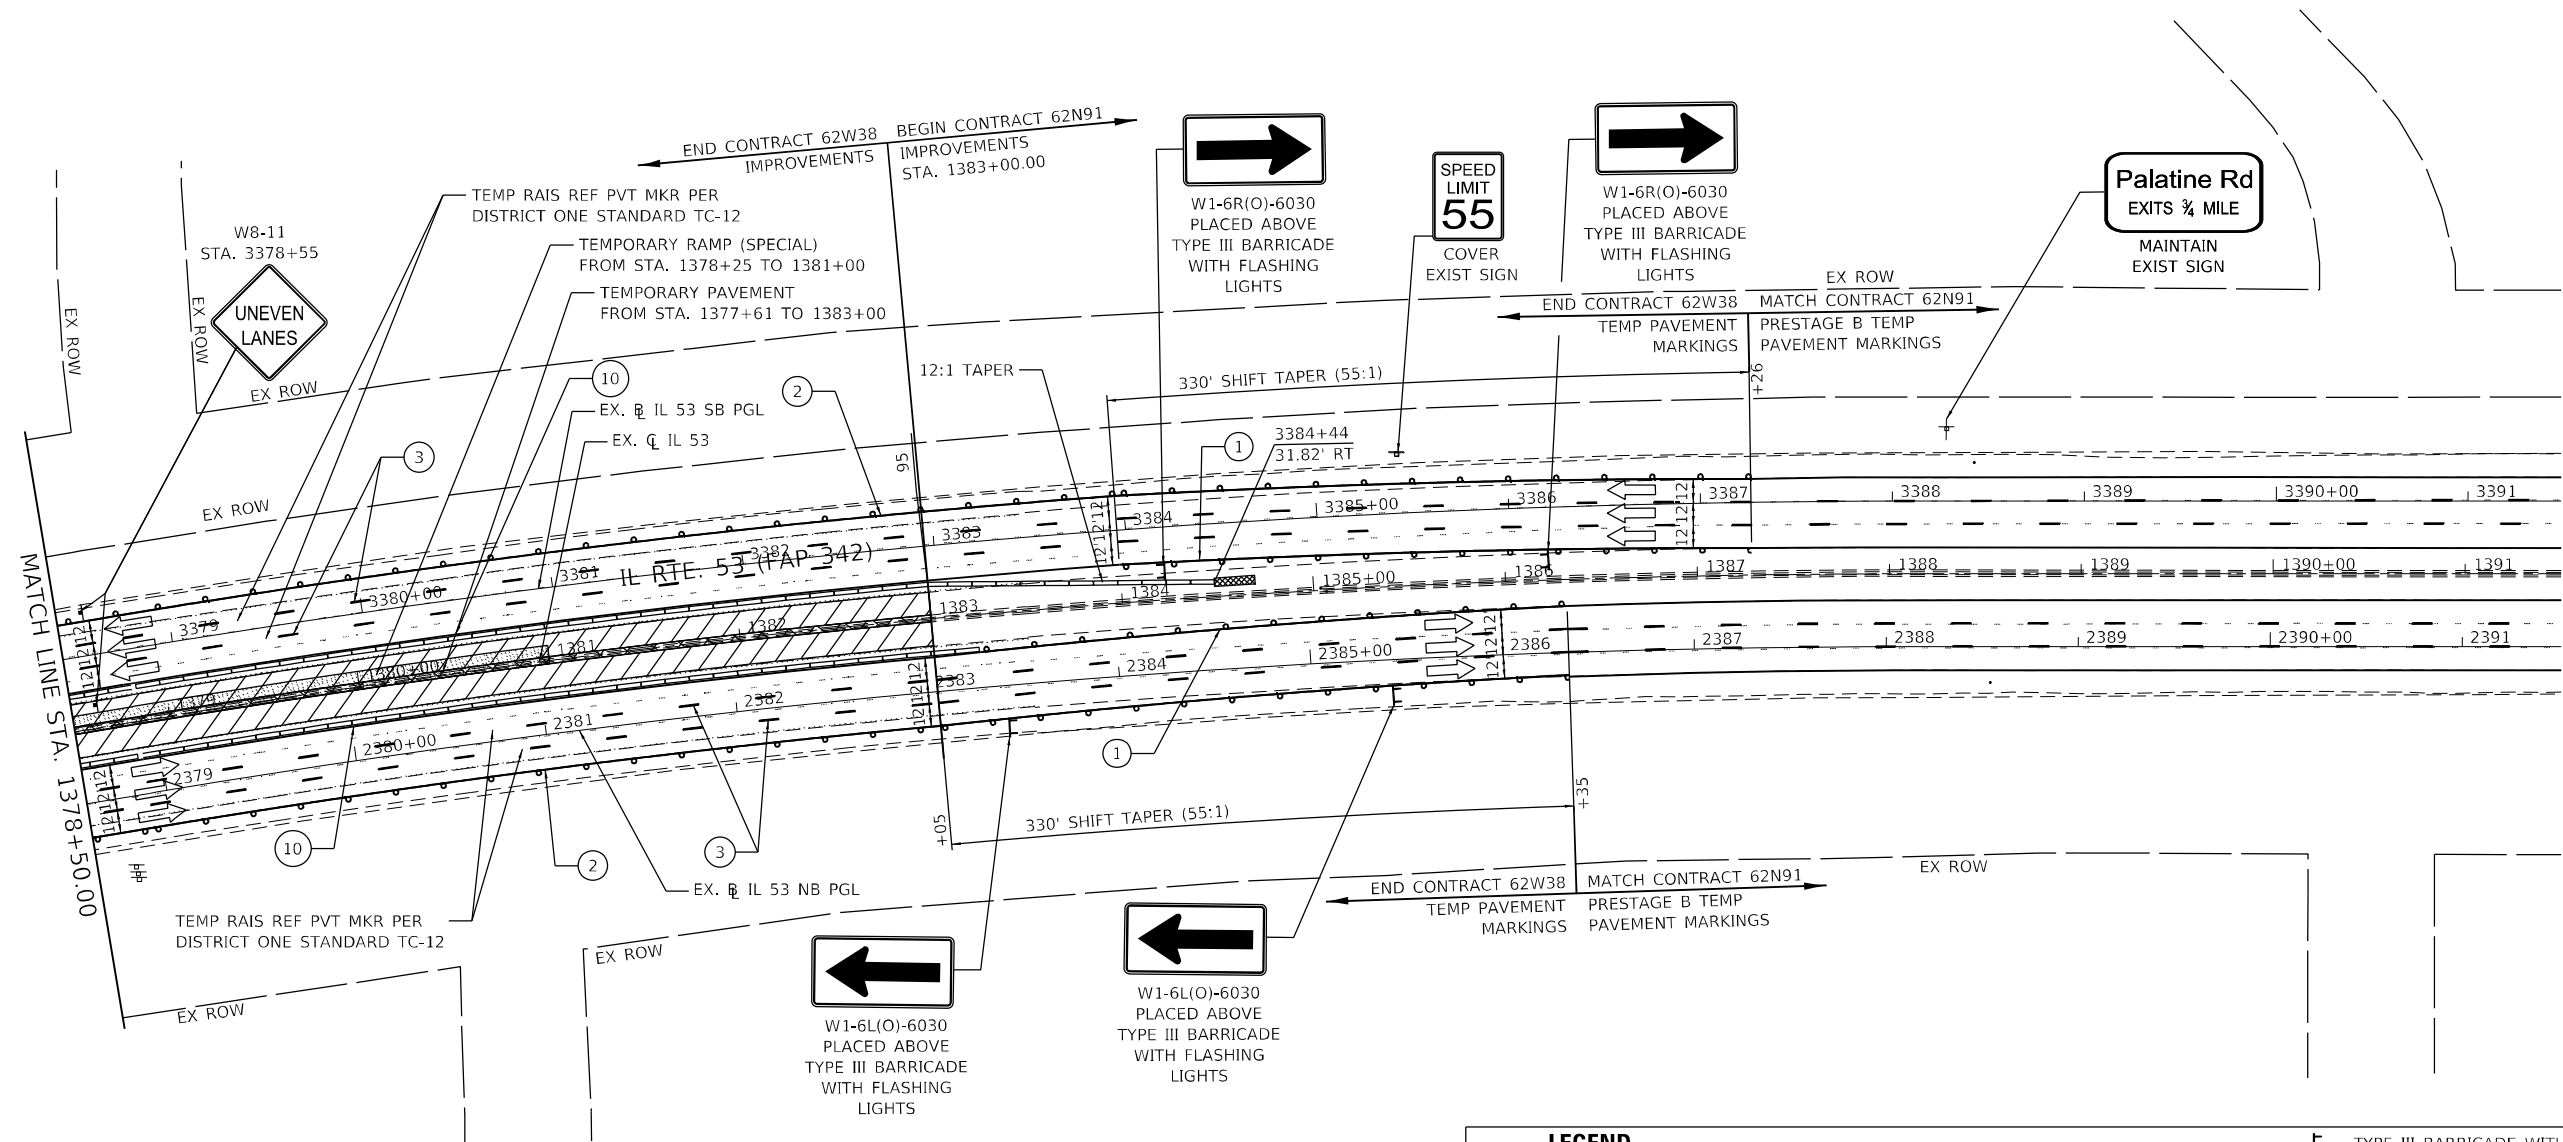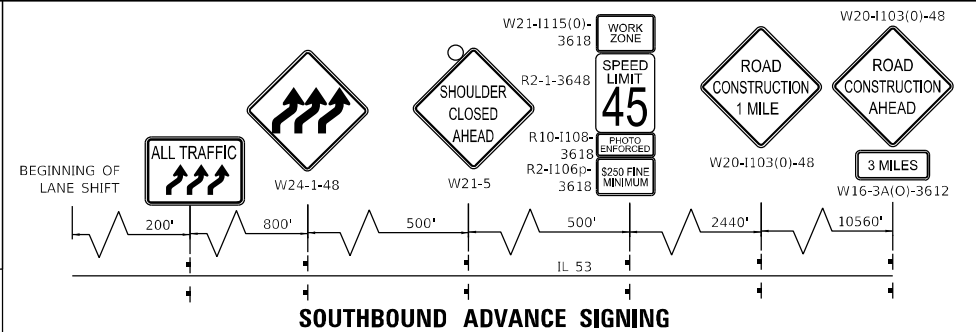




- | LEGEND | | | |
|--------|--|---|--|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW |  | TYPE III BARRICADE WITH FLASHING LIGHTS |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE |  | WORK ZONE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP |  | TEMPORARY RAMP (SPECIAL) |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED |  | TEMPORARY PAVEMENT |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE |  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE |  | TEMPORARY CONCRETE BARRIER |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED |  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW |  | FLASHING ARROW BOARD |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE
(CHEVRON MARKING SPACED 30' C-C) |  | TRAFFIC FLOW DIRECTION |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW |  | SIGN |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE |  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |

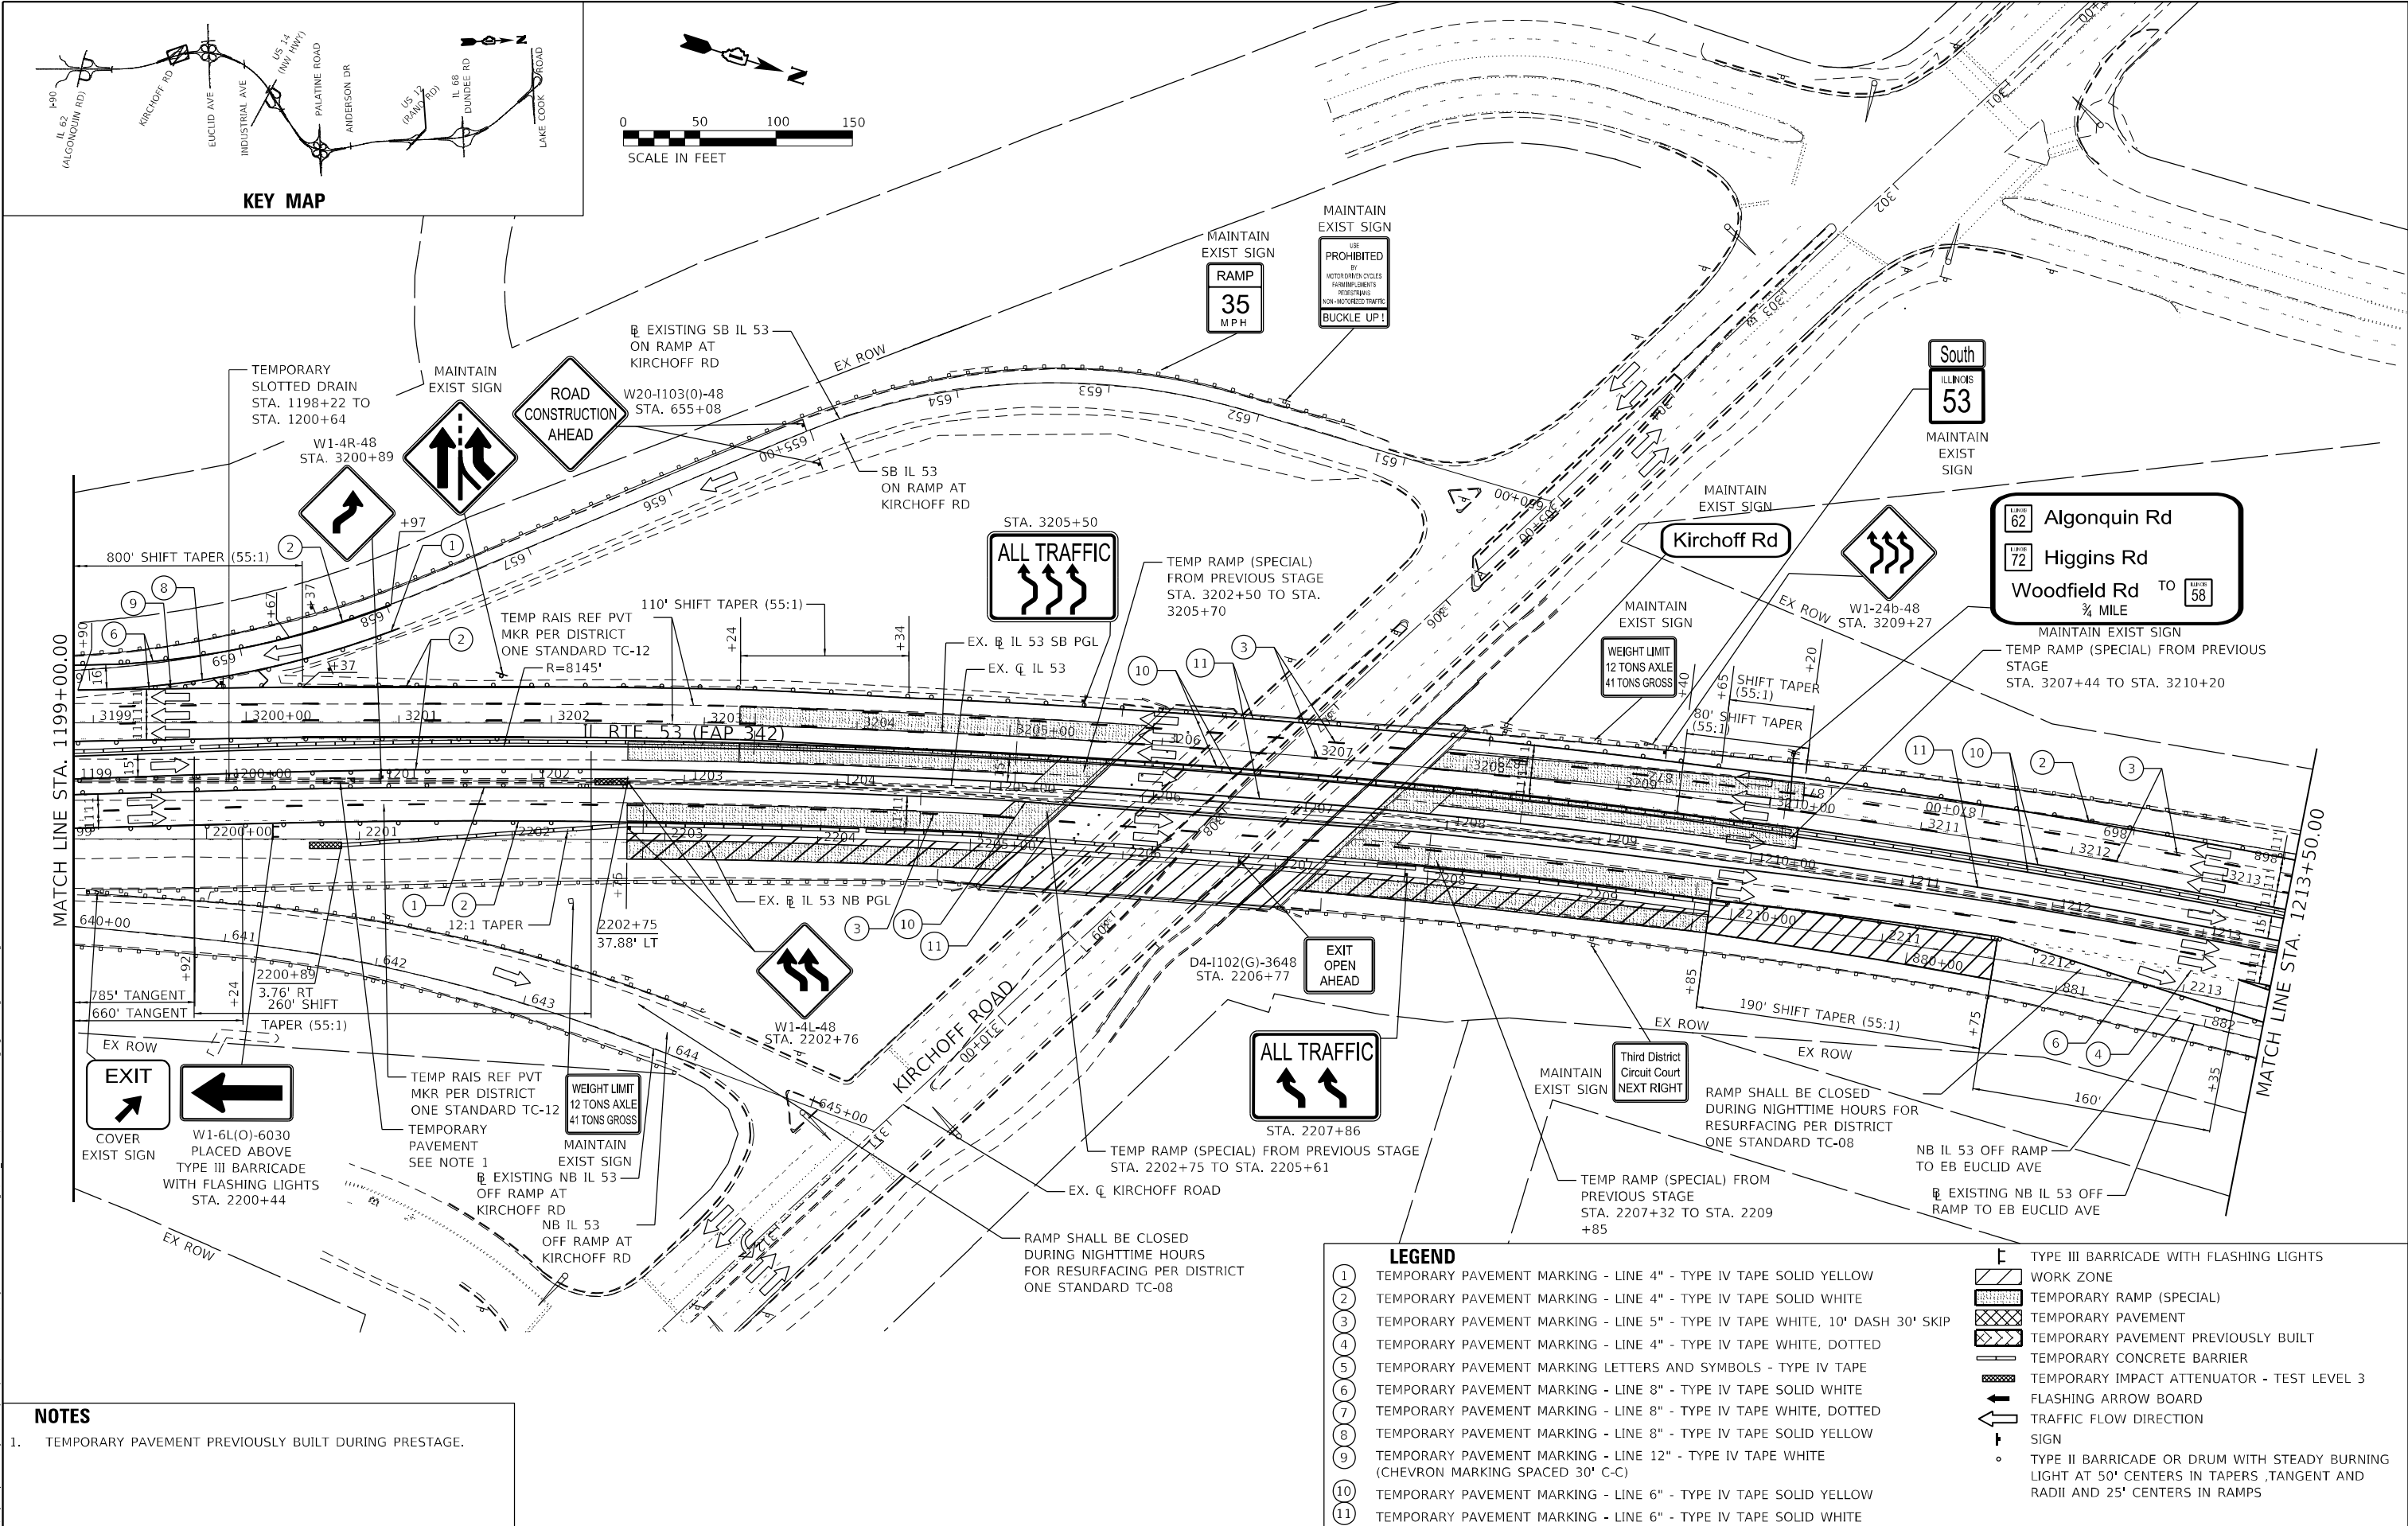

- NOTES
1.


TEMPORARY PAVEMENT PREVIOUSLY BUILT DURING PRESTAGE.

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – STAGE 1				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000 ' / in.	DRAWN - MM	REVISED -		342	(531) BR 23	COOK	1211	248				
	PLOT DATE = 9/23/2024	CHECKED - TC	REVISED -				CONTRACT NO. 62W38						
	DATE - 8/23/2024	REVISED -	SCALE: 1" = 50'		SHEET 2 OF 17 SHEETS	STA. 1186+00.00 TO STA. 1199+00.00	ILLINOIS FED. AID PROJECT						

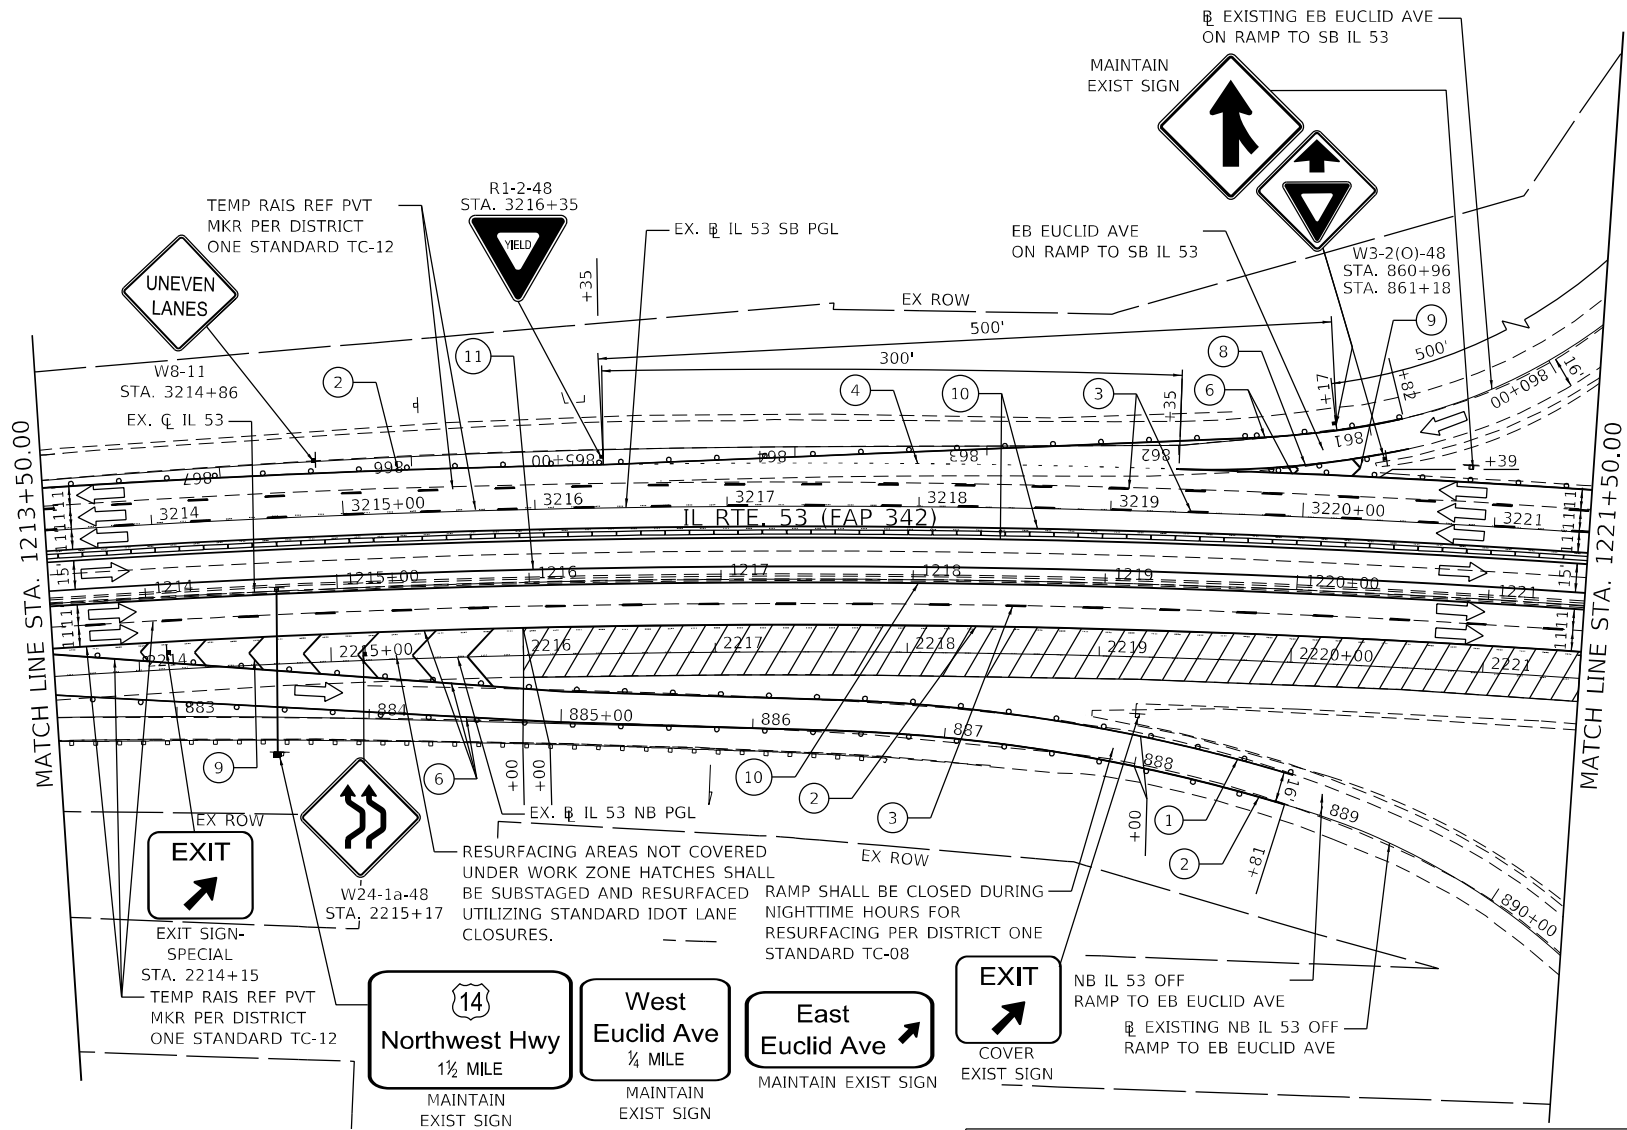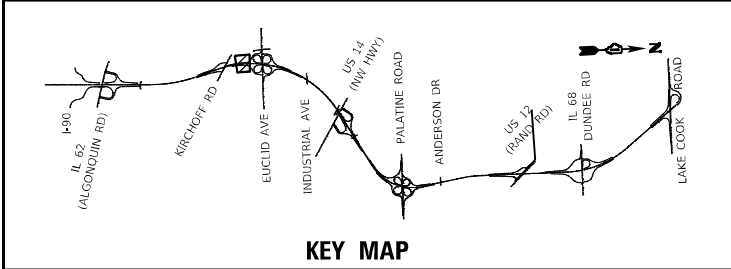


LEGEND



1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	TYPE III BARRICADE WITH FLASHING LIGHTS
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE	WORK ZONE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP	TEMPORARY RAMP (SPECIAL)
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY PAVEMENT
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE	TEMPORARY PAVEMENT PREVIOUSLY BUILT
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE	TEMPORARY CONCRETE BARRIER
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW	FLASHING ARROW BOARD
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)	TRAFFIC FLOW DIRECTION SIGN
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE	

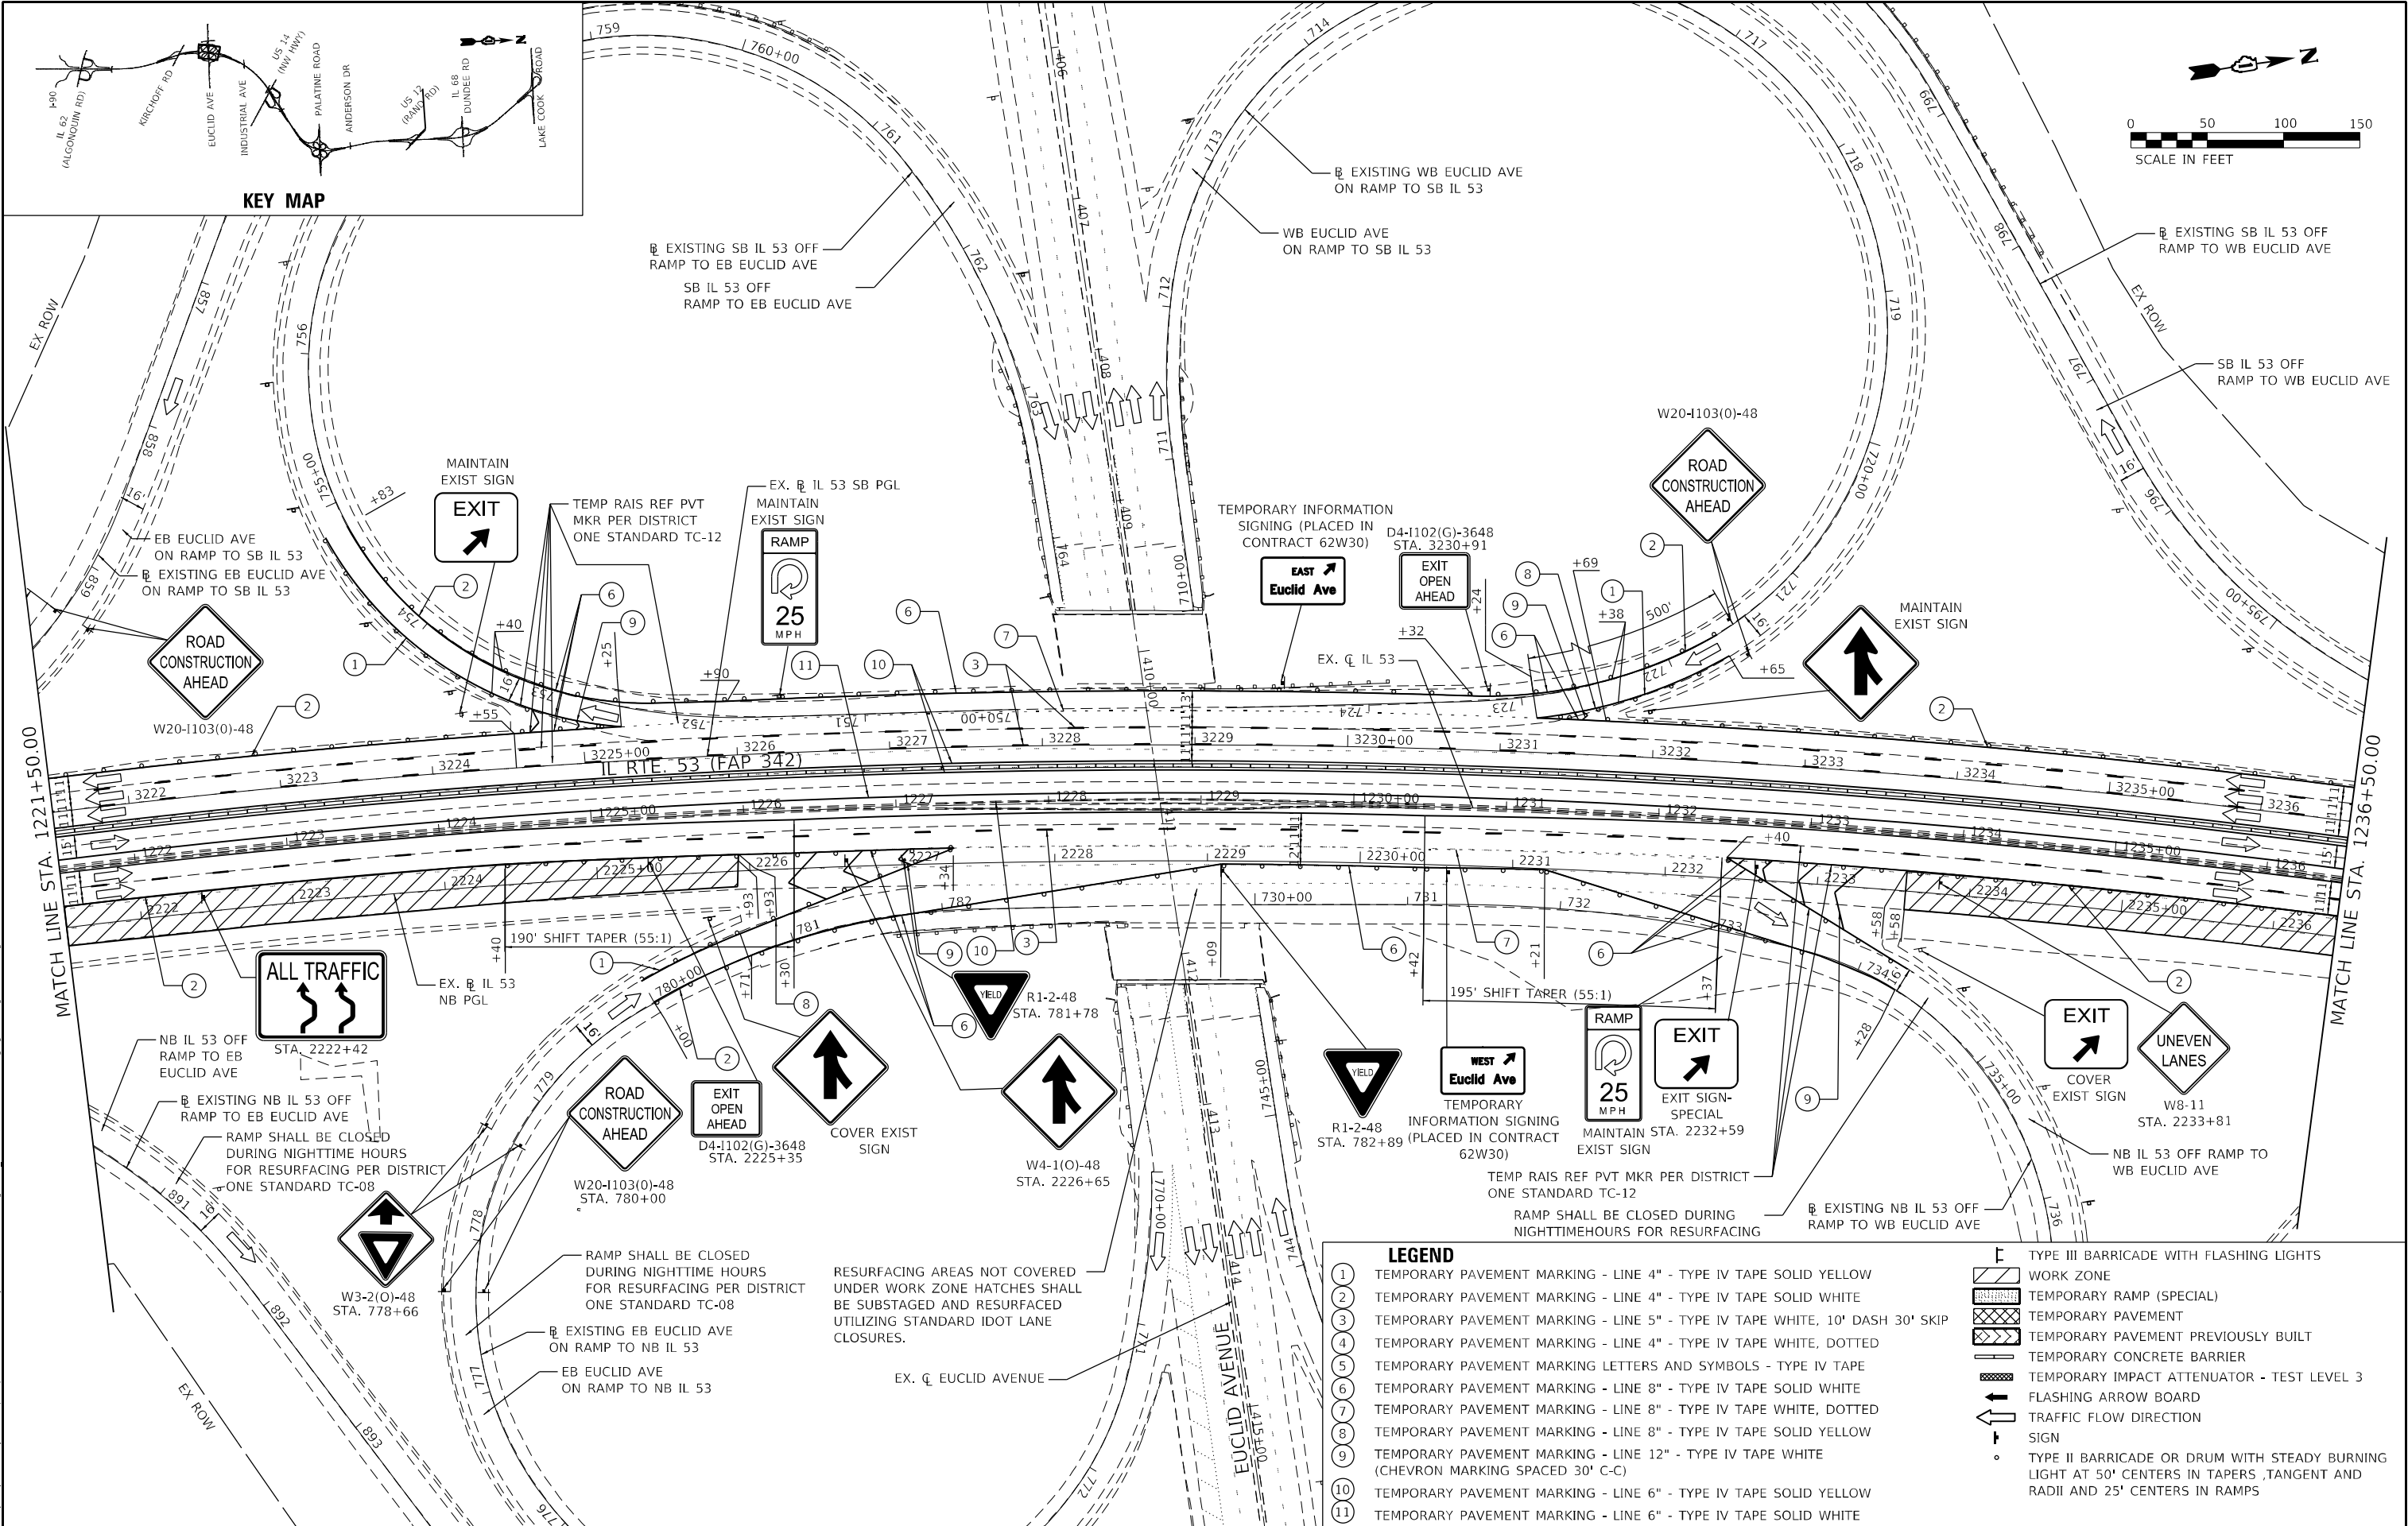

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – STAGE 1				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	PLOT SCALE = 100,0000' / in.	DRAWN - MM	REVISED -		342	(531) BR 23	COOK	1211	250				
	PLOT DATE = 9/23/2024	CHECKED - TC	REVISED -		CONTRACT NO. 62W38								
	DATE - 8/23/2024	REVISED -	SCALE: 1" = 50' SHEET 4 OF 17 SHEETS STA. 1221+50.00 TO STA. 1236+50.00										
ILLINOIS FED. AID PROJECT													



KEY MAP

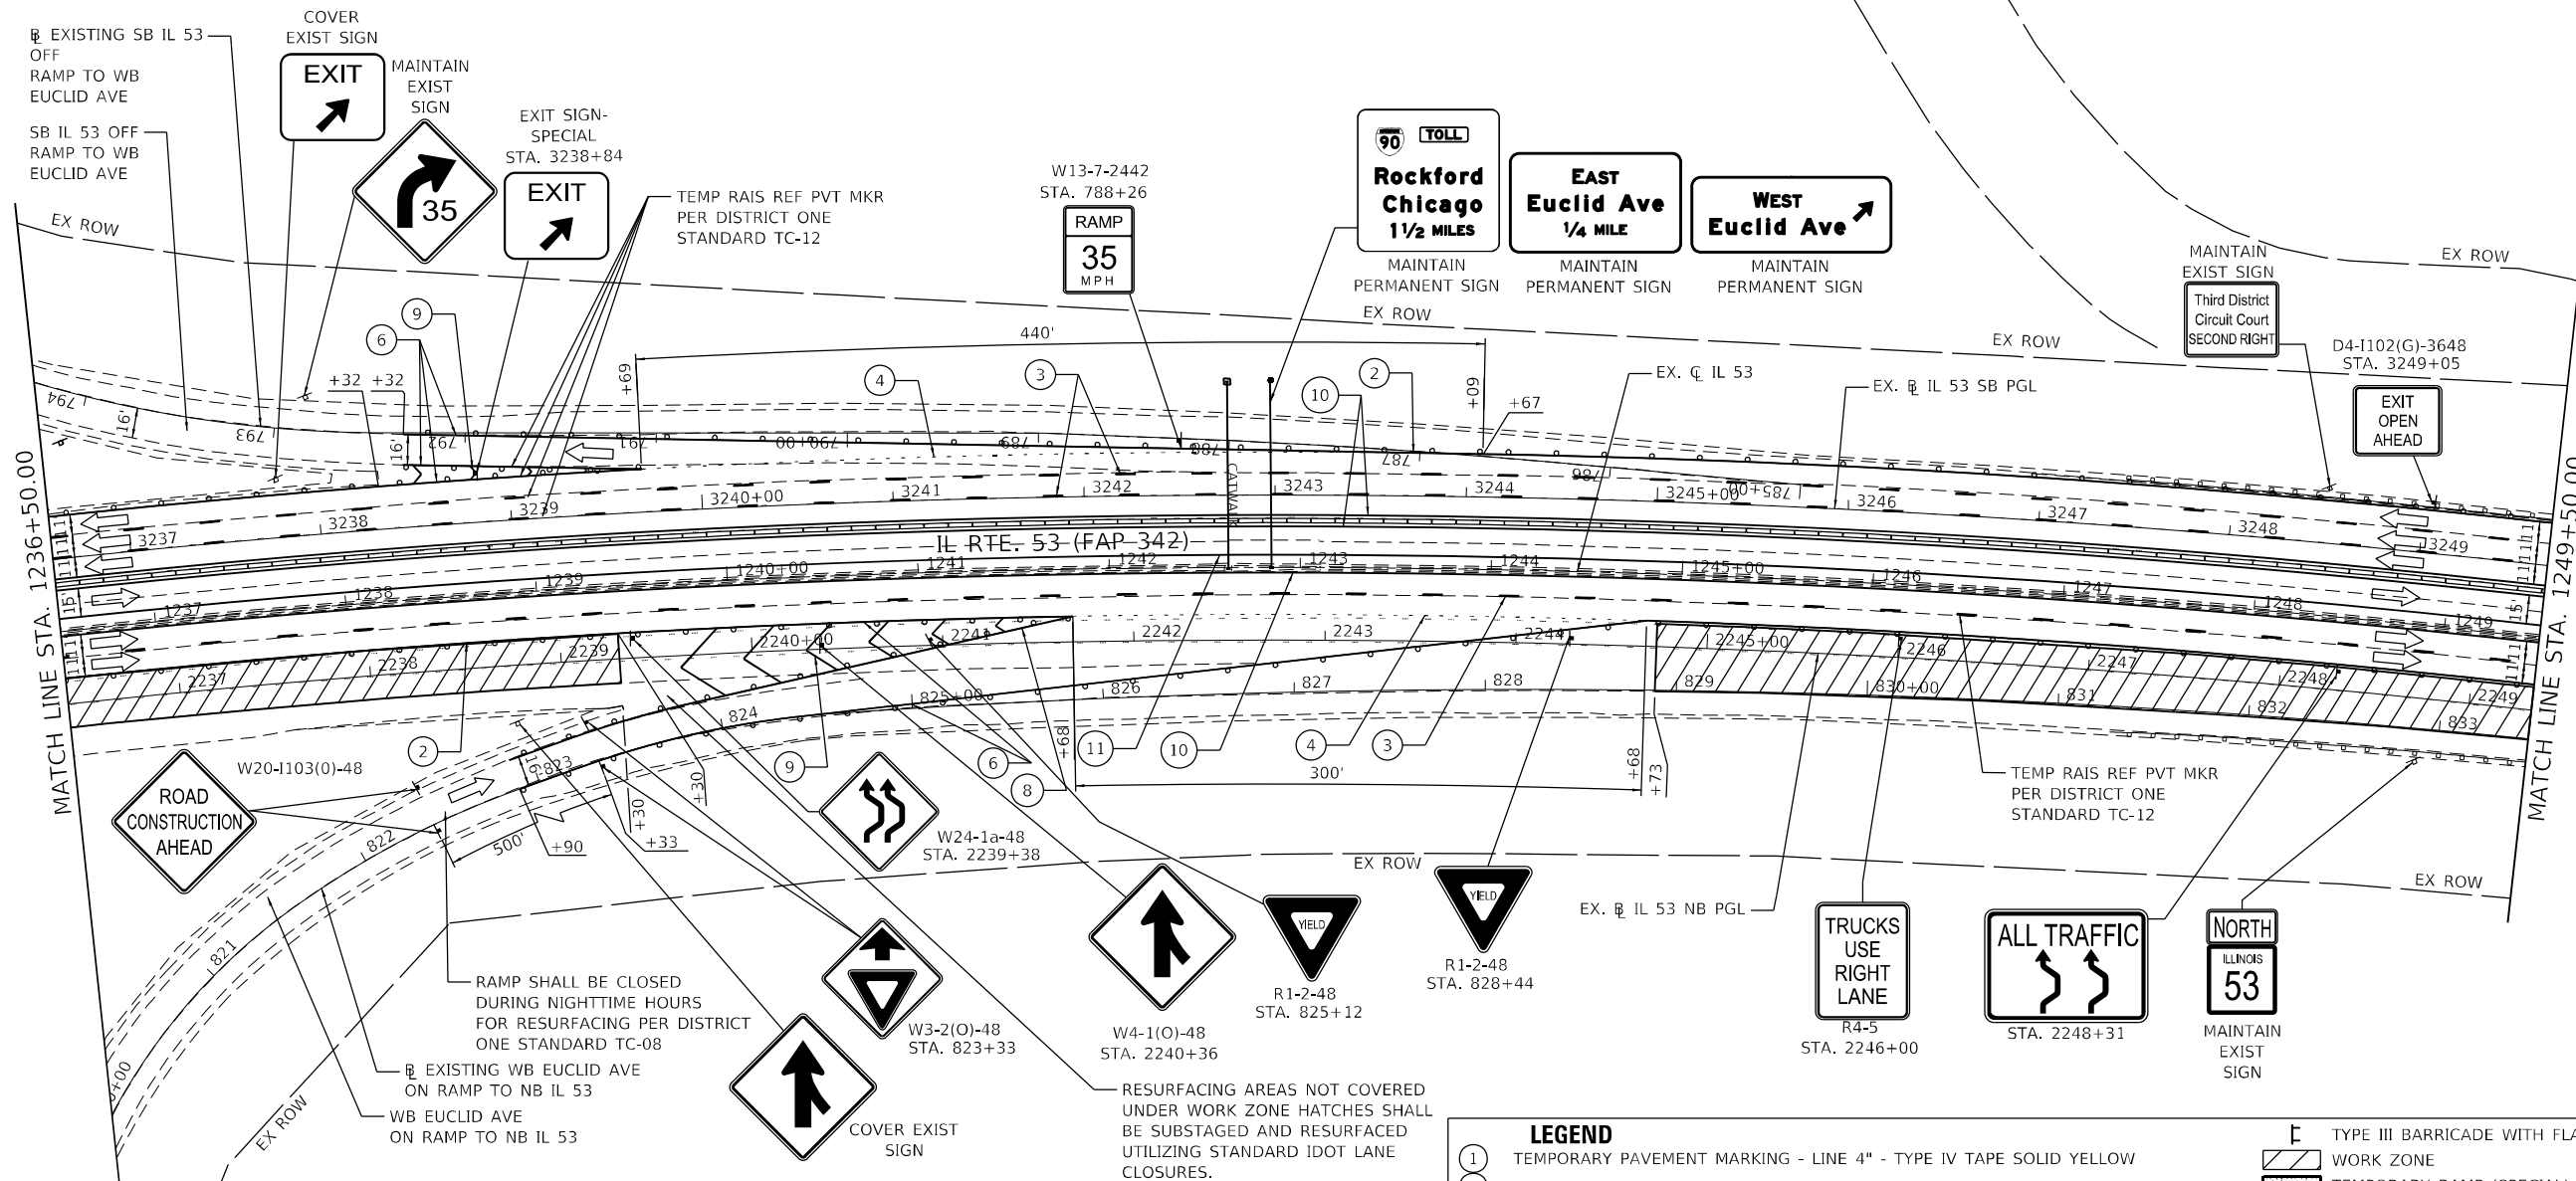

- LEGEND**
- | | | |
|----|---|--|
| 1 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW | TYPE III BARRICADE WITH FLASHING LIGHTS |
| 2 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE | WORK ZONE |
| 3 | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP | TEMPORARY RAMP (SPECIAL) |
| 4 | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED | TEMPORARY PAVEMENT |
| 5 | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
| 6 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE | TEMPORARY CONCRETE BARRIER |
| 7 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
| 8 | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW | FLASHING ARROW BOARD |
| 9 | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C) | TRAFFIC FLOW DIRECTION SIGN |
| 10 | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |
| 11 | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE | |

MODEL: Default
FILE: \\wsp-045-pw-bentley.com\usps45-pw-bentley.com\usps45-pw-bentley.com\Documents\Project: 62N01-IL 53 Bridge\CAD Sheets\1D163\N38-01r-ctg-01g-IL53-S1g-1-05-1050.dgn



USER NAME = USTC714594	DESIGNED - MM	REVISED -
PLOT SCALE = 100,0000' / in.	DRAWN - MM	REVISED -
PLOT DATE = 9/23/2024	CHECKED - TC	REVISED -
	DATE - 8/23/2024	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN - STAGE 1

SCALE: 1" = 50' SHEET 5 OF 17 SHEETS STA. 1236+50.00 TO STA. 1249+50.00



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	251
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				




- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
| <ul style="list-style-type: none"> ◦ TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADIUS AND 25' CENTERS IN RAMPS | |



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	252
		CONTRACT NO. 62W38		
ILLINOIS		FED. AID PROJECT		




MODEL: Default

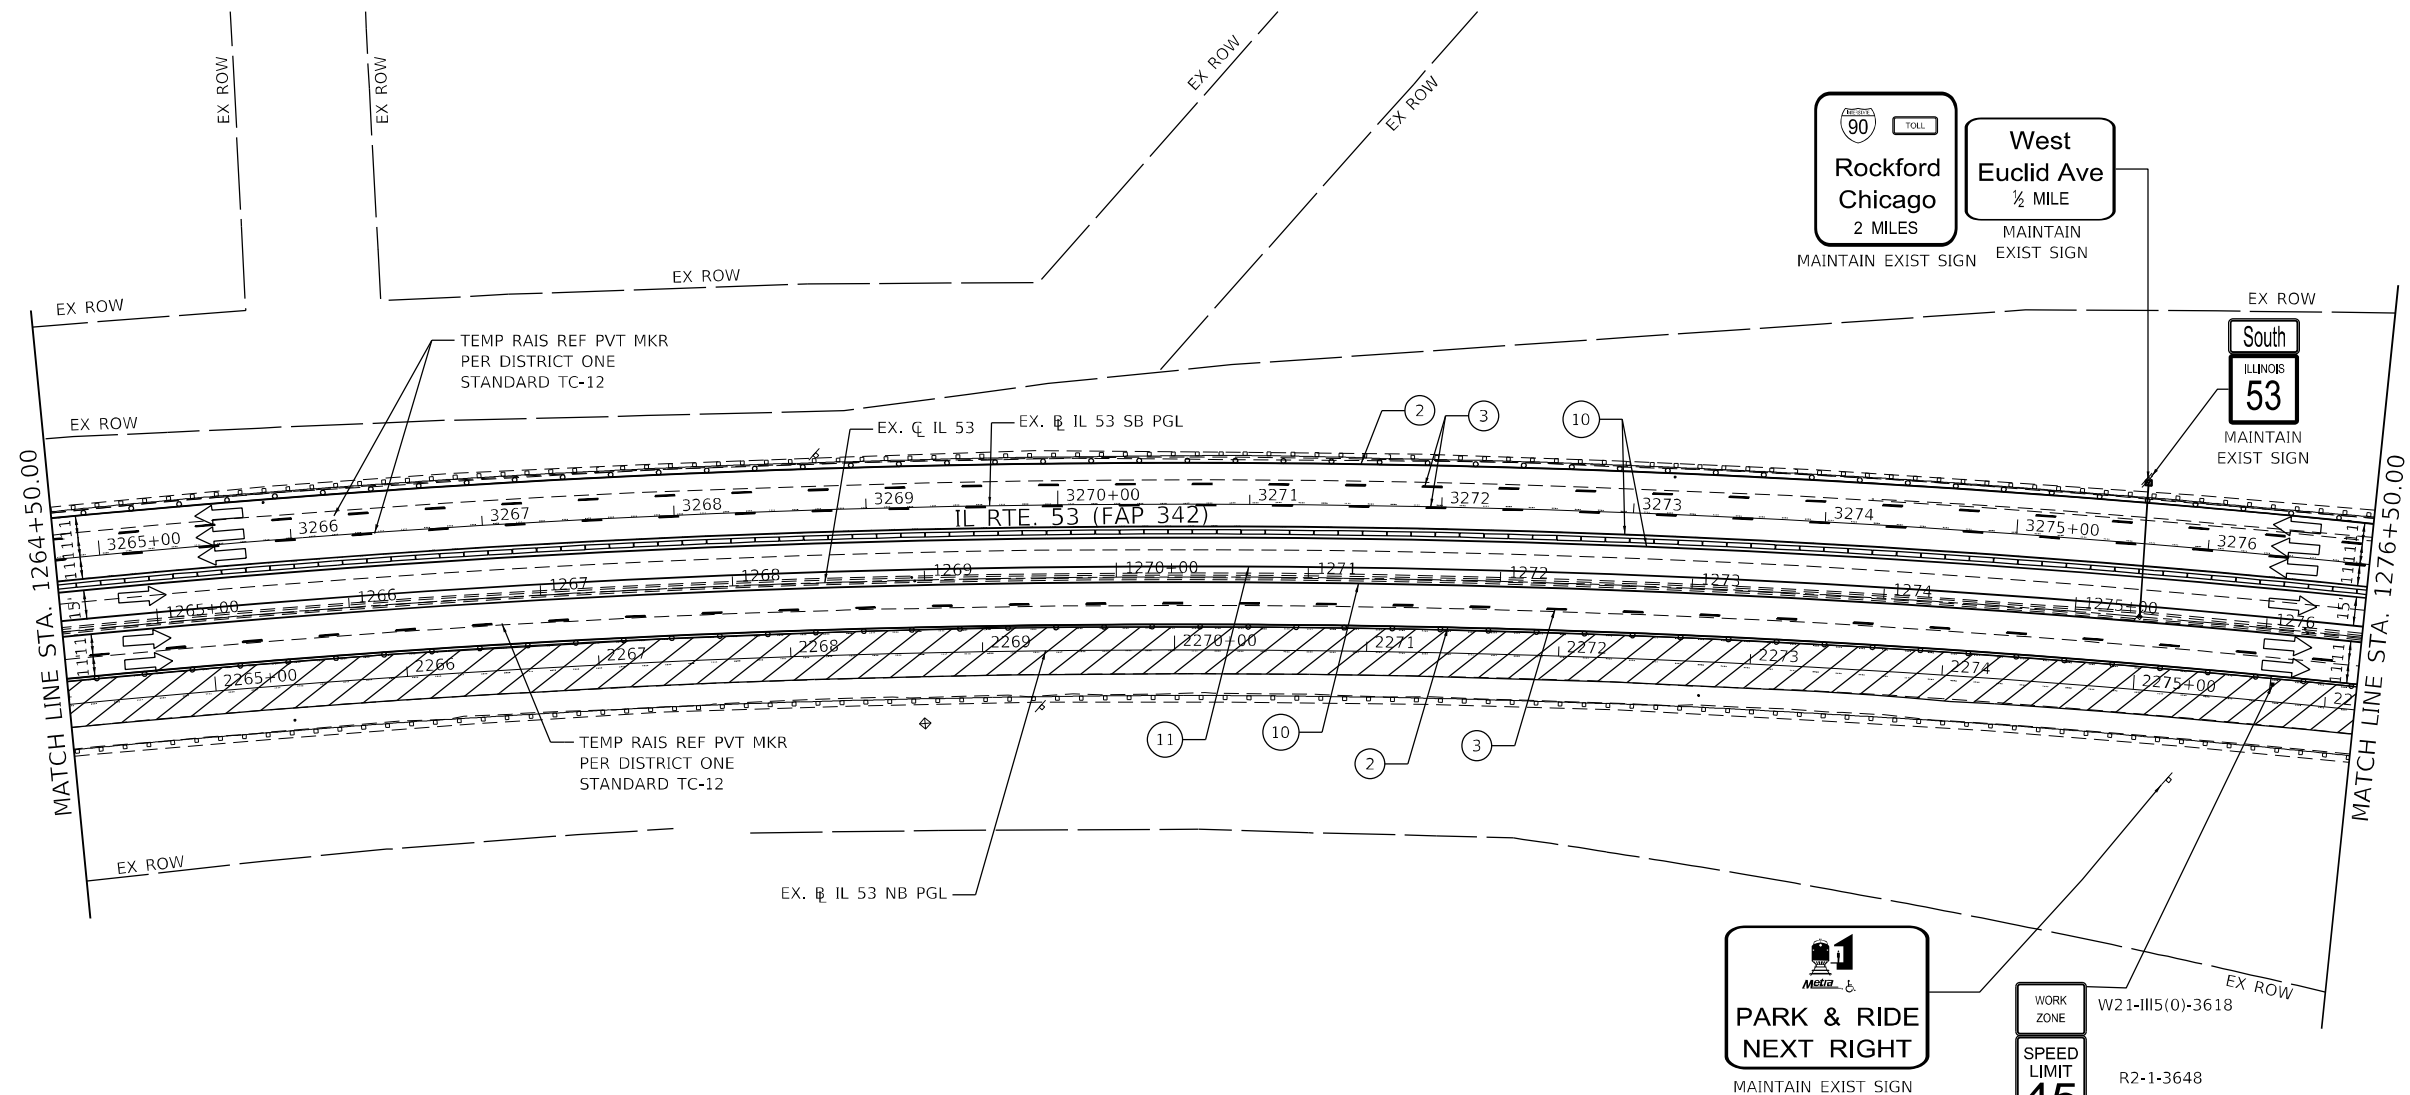

USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -

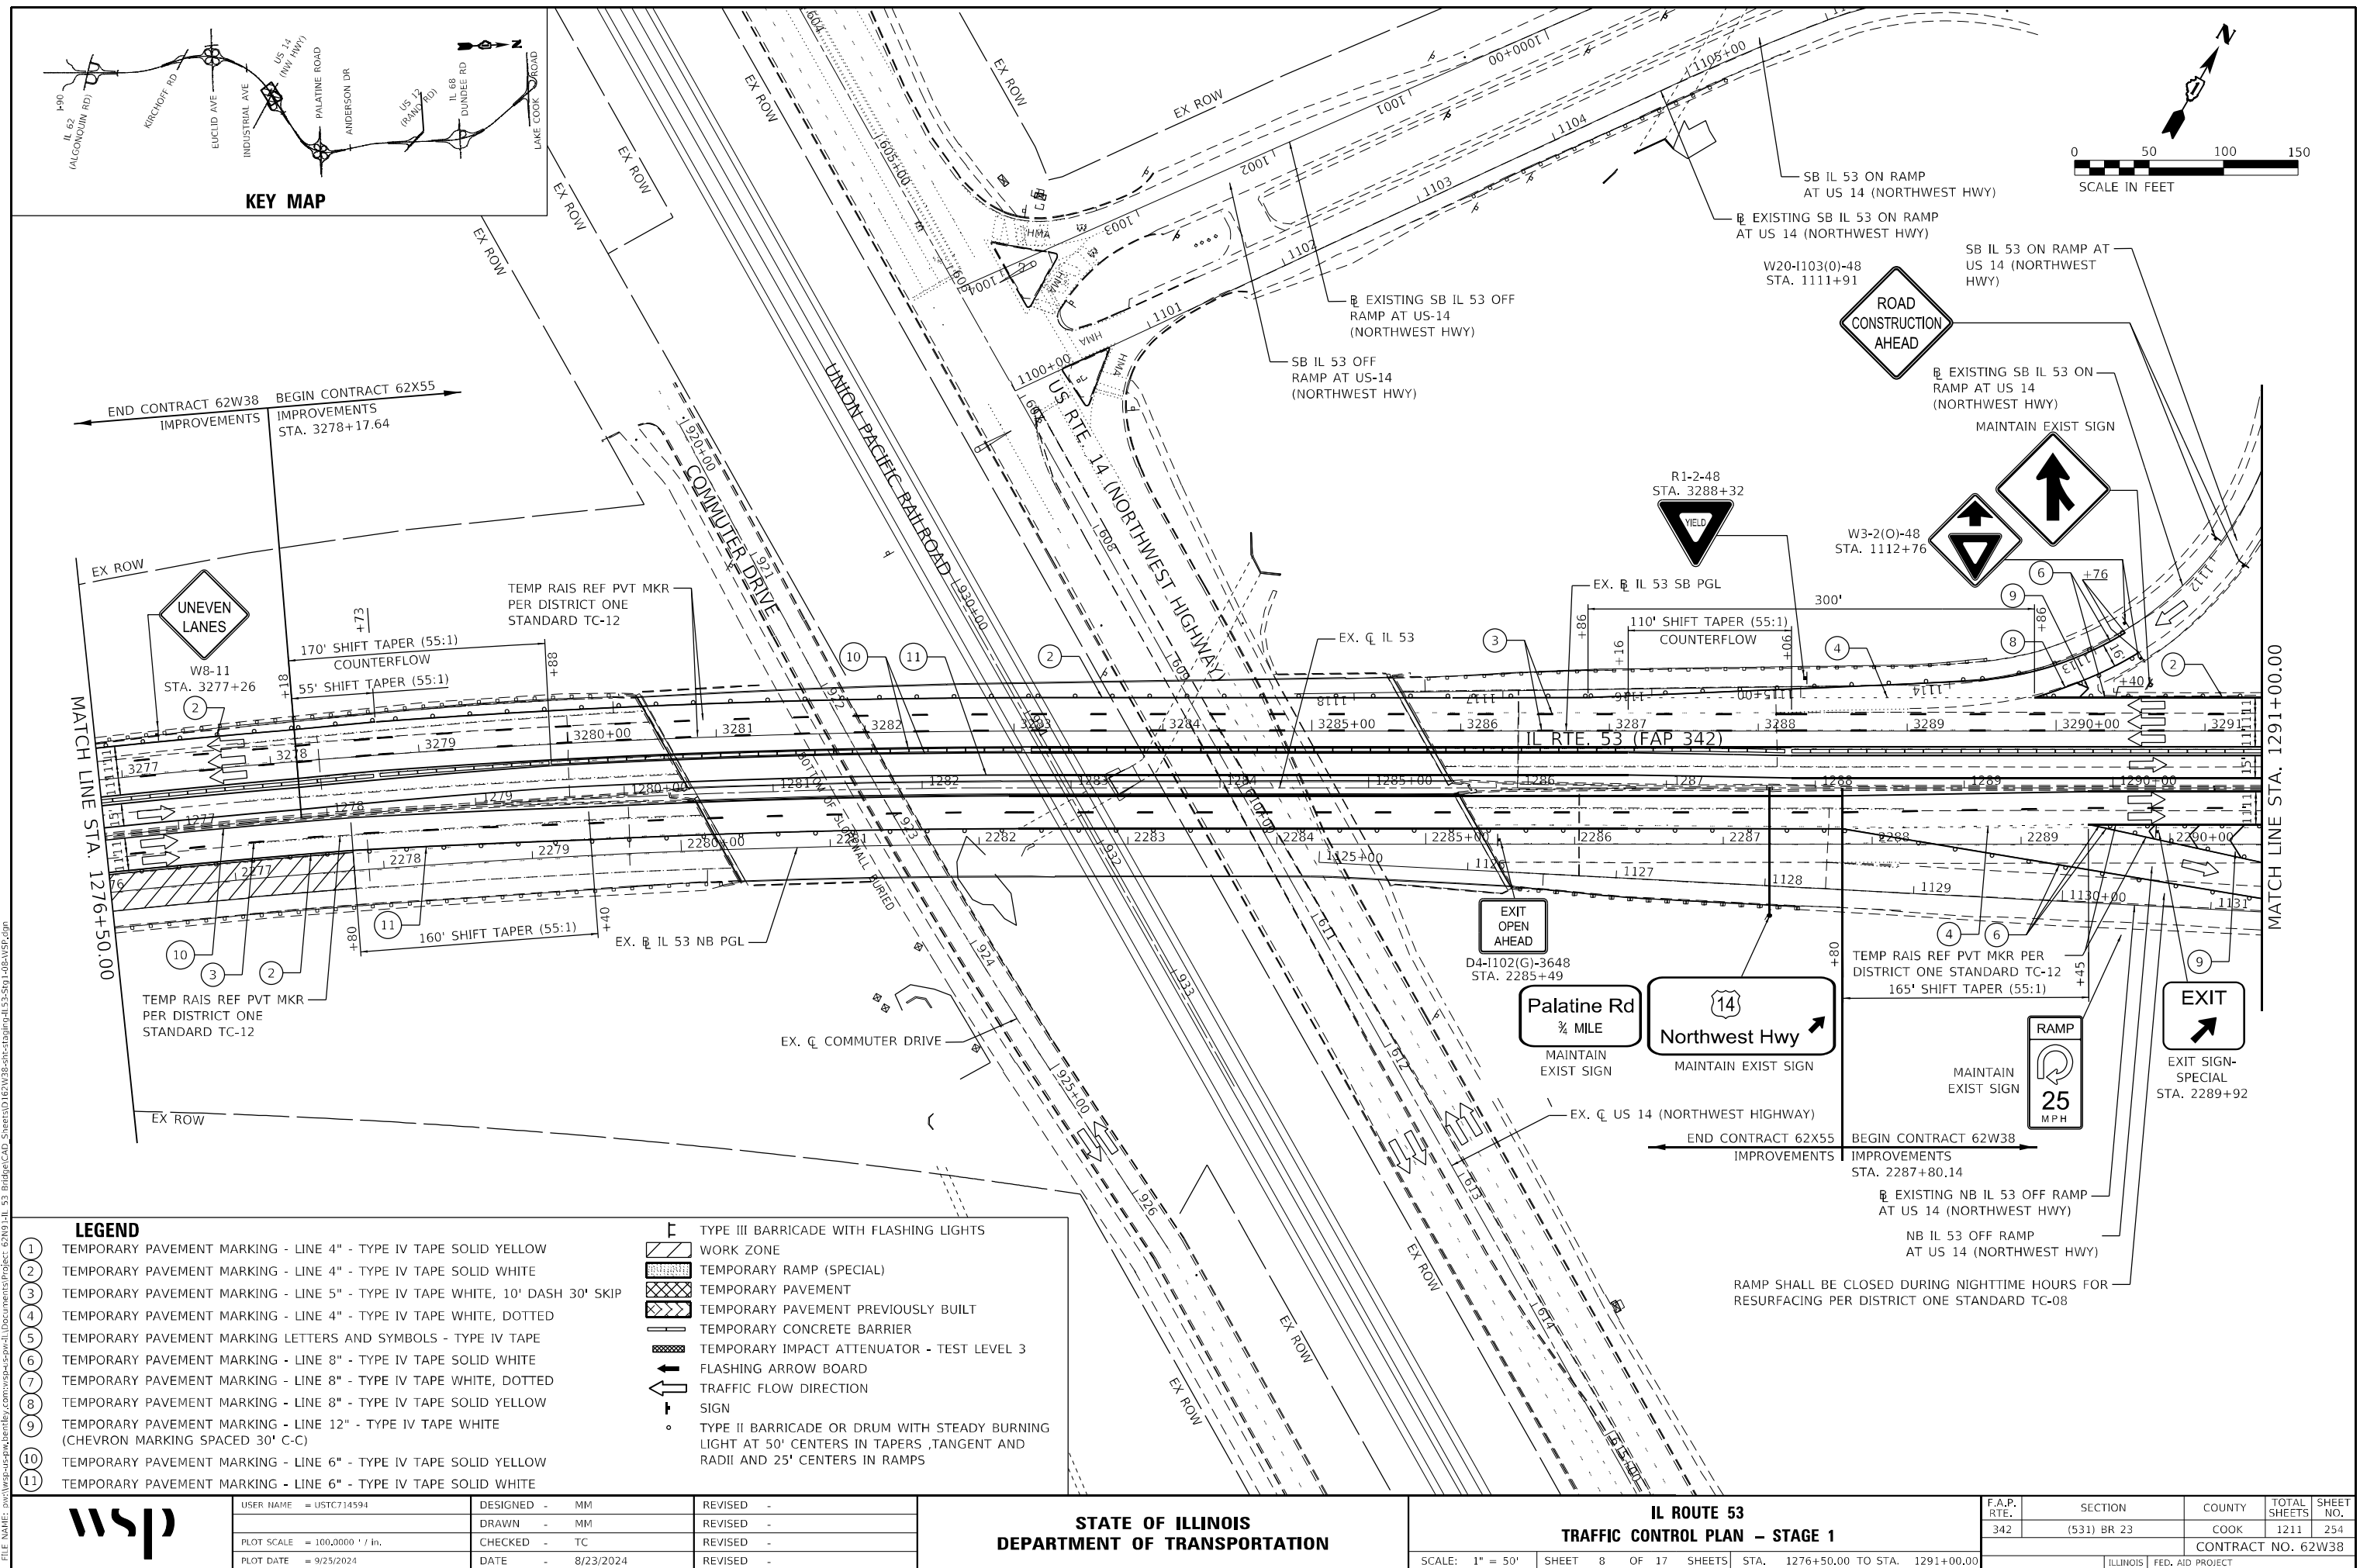

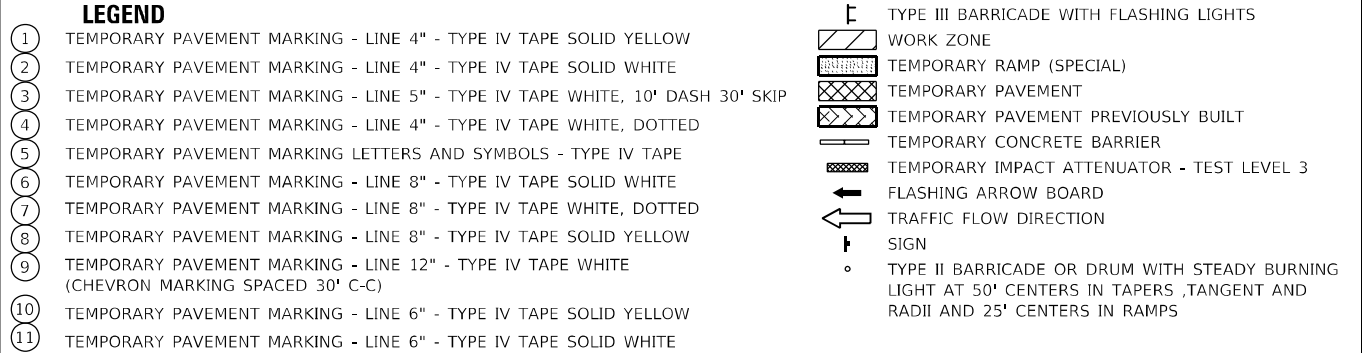

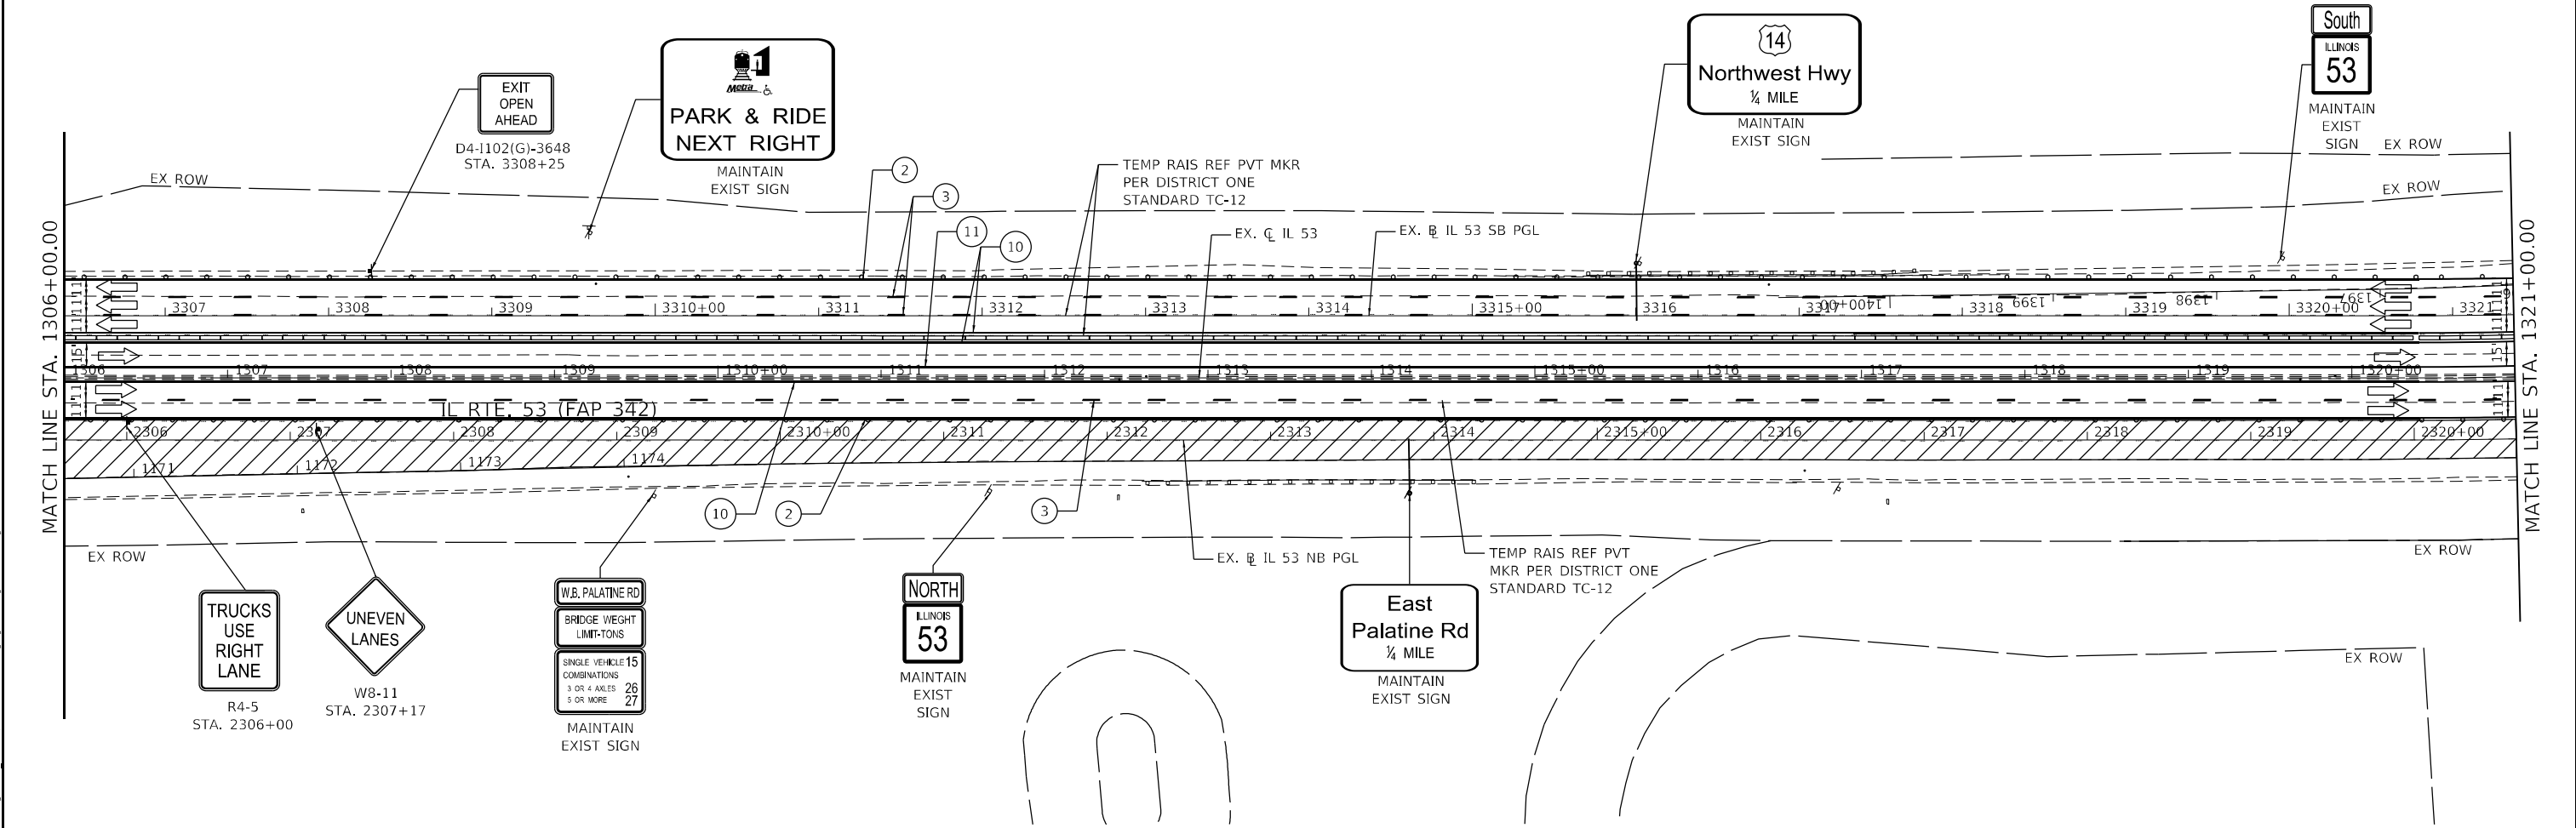

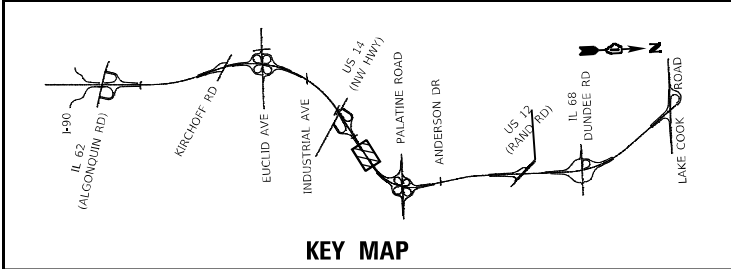


LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



MODEL: Default
FILE: A:\Users\pawel.bentley.com\userpawel.bentley.com\workspace\illinois\Documents\Project: 62W38-111_53_Bridge\CAD_Sheets\1062W38-111_53-Stage1-10AUSD.dgn

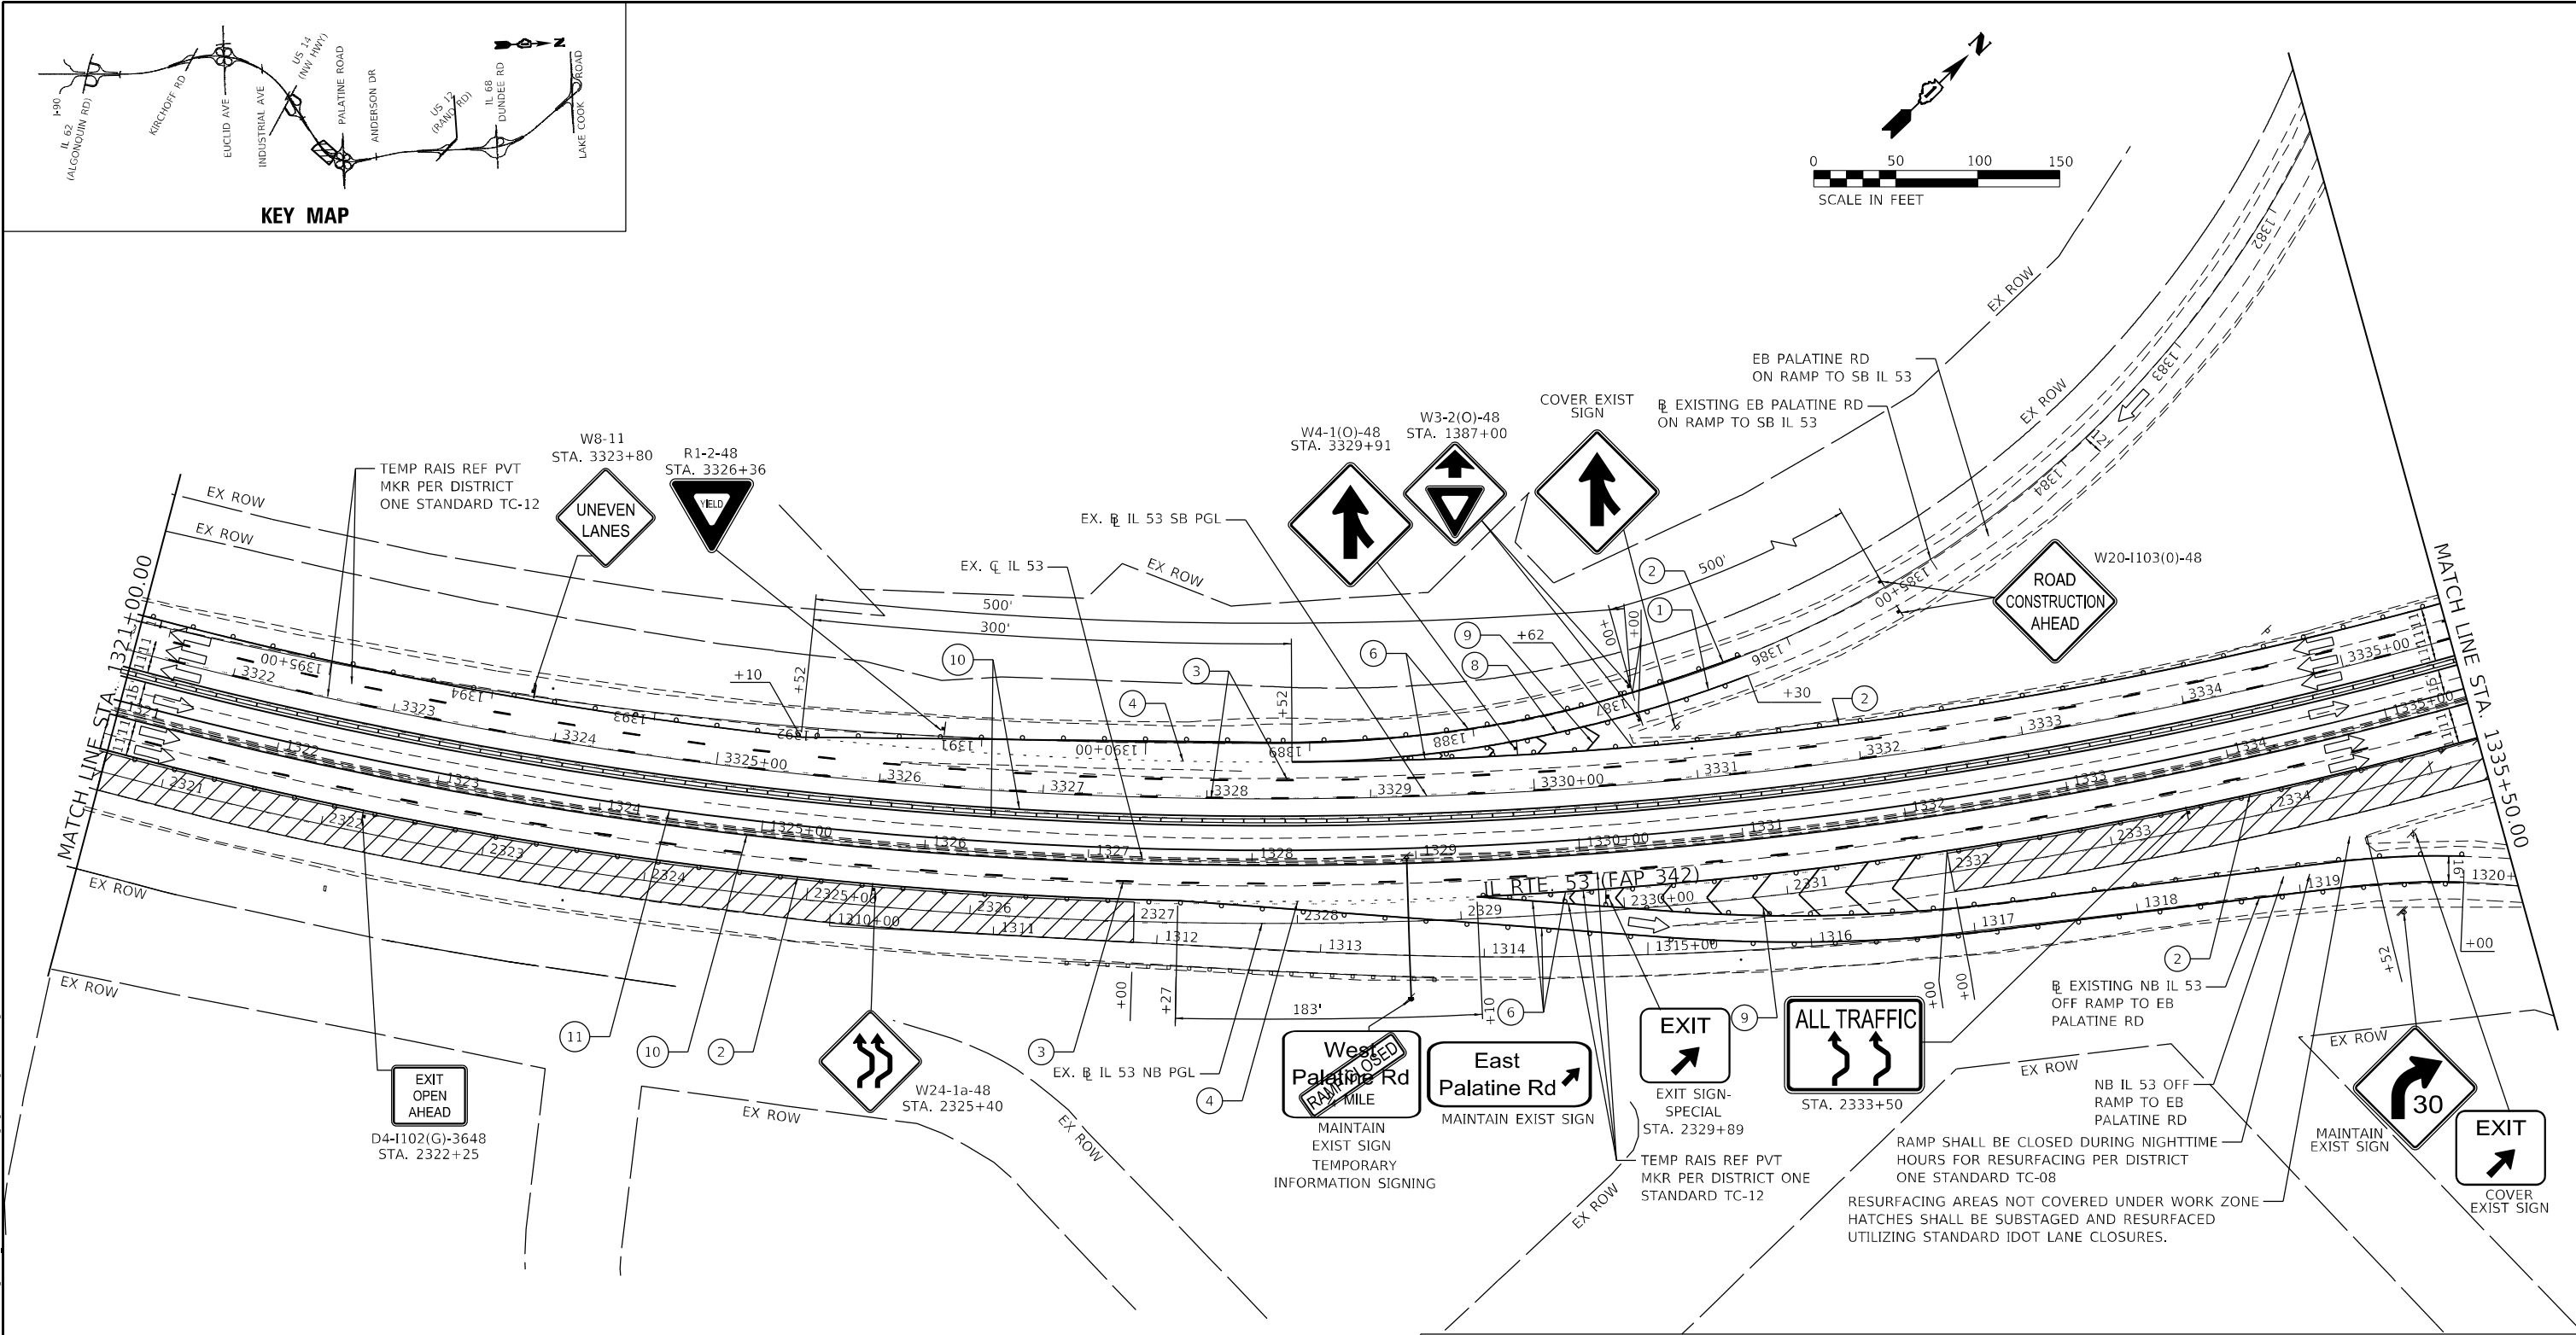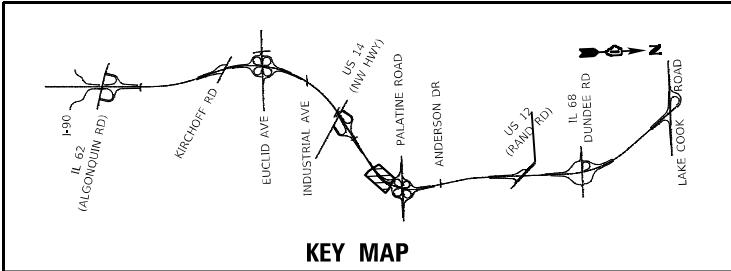


LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE



- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMP

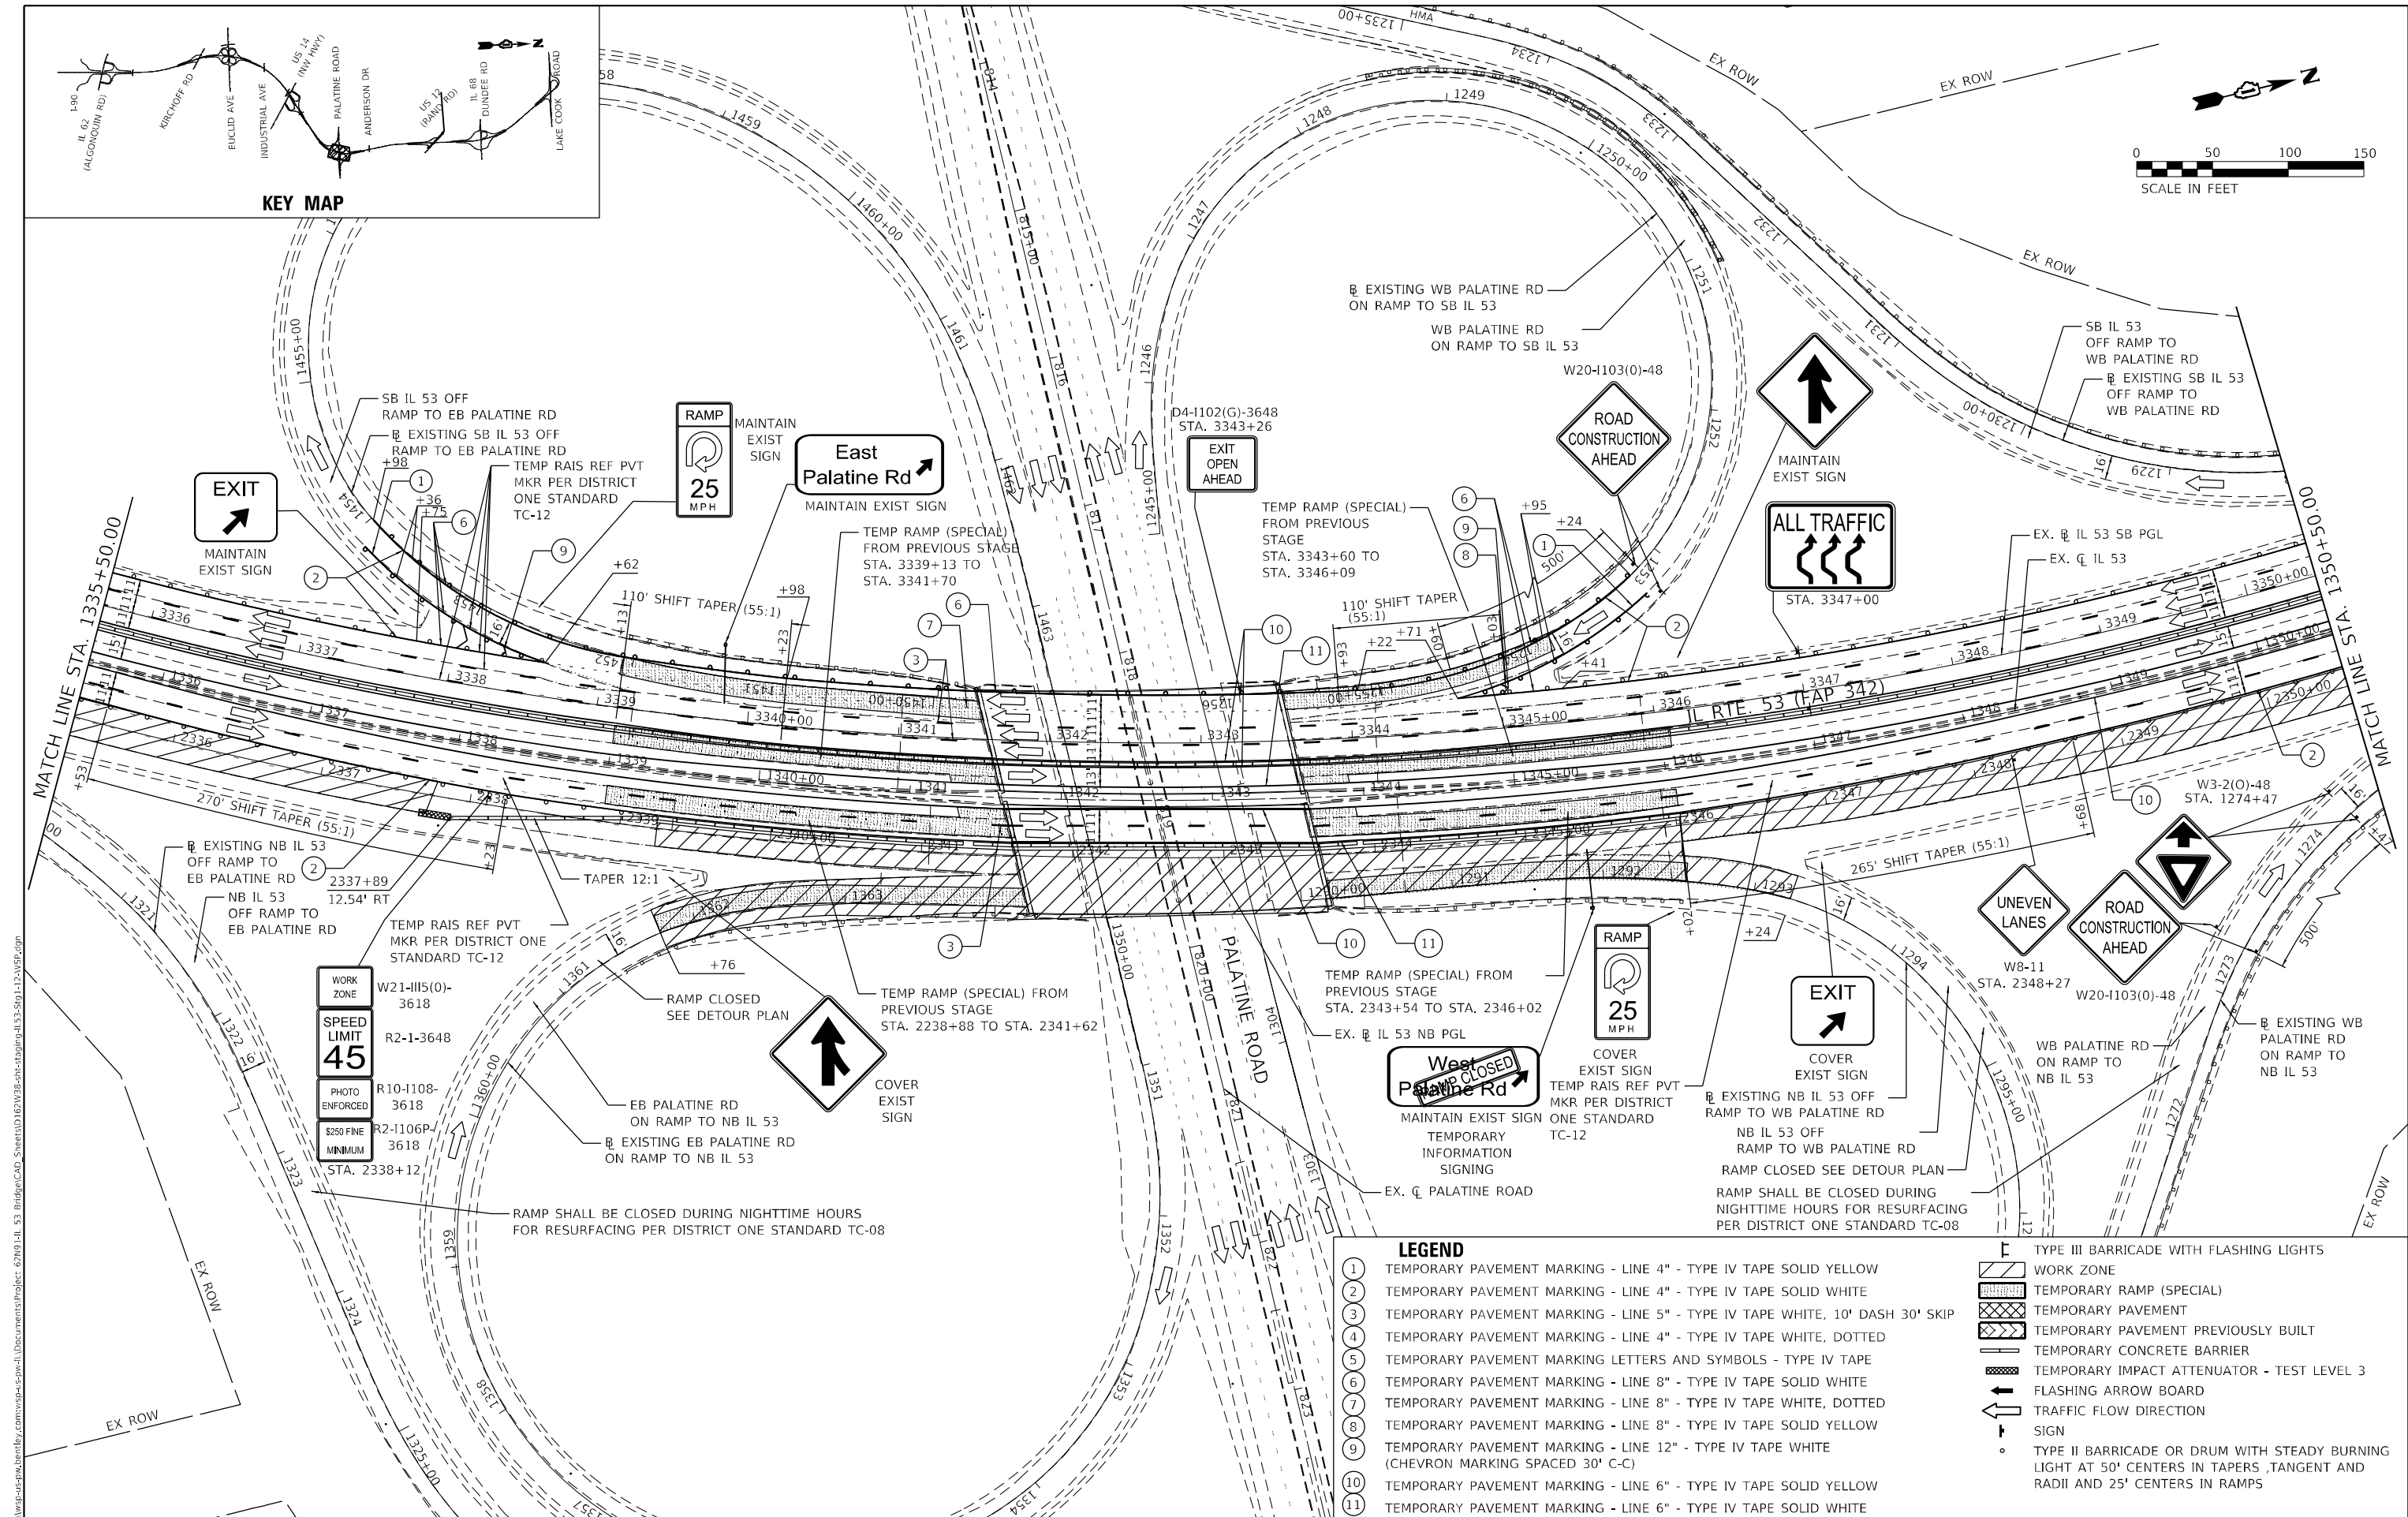

- LEGEND**
- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
 - 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
 - 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
 - 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
 - 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
 - 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
 - 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
 - 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
 - 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
 - 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
 - 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
- TYPE III BARRICADE WITH FLASHING LIGHTS
 - WORK ZONE
 - TEMPORARY RAMP (SPECIAL)
 - TEMPORARY PAVEMENT
 - TEMPORARY PAVEMENT PREVIOUSLY BUILT
 - TEMPORARY CONCRETE BARRIER
 - TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
 - FLASHING ARROW BOARD
 - TRAFFIC FLOW DIRECTION SIGN
 - TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMP



KEY MAP

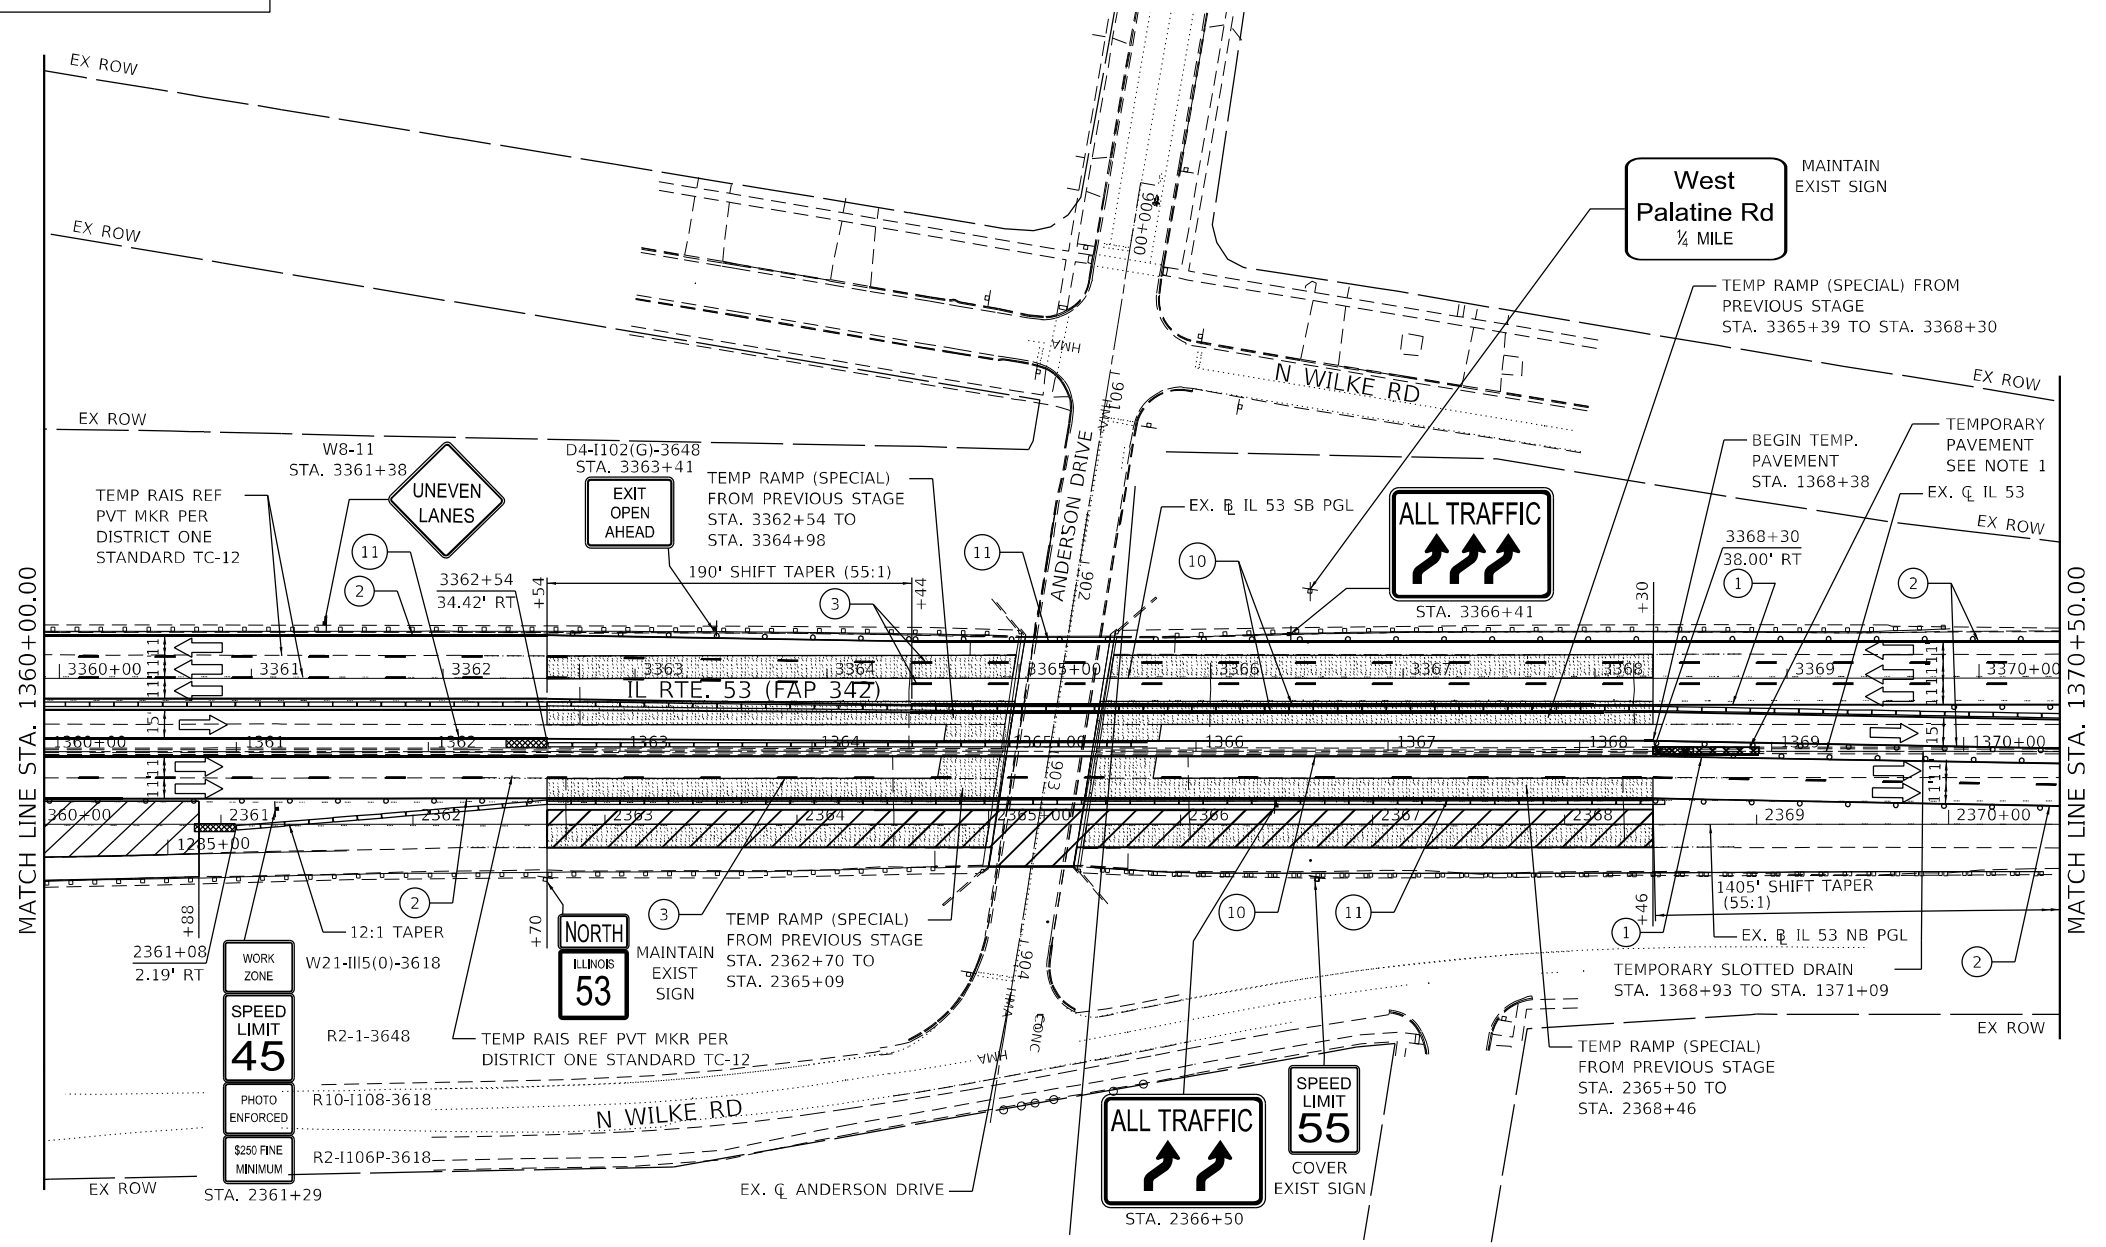

- NOTES**
1. TEMPORARY PAVEMENT PREVIOUSLY BUILT DURING PRESTAGE.


LEGEND

①	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW	⚡	TYPE III BARRICADE WITH FLASHING LIGHTS
②	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE	▨	WORK ZONE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP	▩	TEMPORARY RAMP (SPECIAL)
④	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED	▤	TEMPORARY PAVEMENT
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE	▥	TEMPORARY PAVEMENT PREVIOUSLY BUILT
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE	▧	TEMPORARY CONCRETE BARRIER
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED	▩	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW	↔	FLASHING ARROW BOARD
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)	➡	TRAFFIC FLOW DIRECTION
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW	⬆	SIGN
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE	⦿	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



MODEL: Default
FILE: \\uspc-01\uspc-01\uspc-01\Documents\Projects\62W38-01\Drawings\IL53-Stage1-14-USP.dgn

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - STAGE 1	SCALE: 1" = 50'	SHEET 14 OF 17 SHEETS	STA. 1360+00.00 TO STA. 1370+00.00	F.A.P. RTE. 342	SECTION (531) BR 23	COUNTY COOK	TOTAL SHEETS 1211	SHEET NO. 260
	PLOT SCALE = 100,0000' / in.	CHECKED - TC	REVISED -						CONTRACT NO. 62W38				
	PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -						ILLINOIS FED. AID PROJECT				

MODEL: Default
FILE: \\nautilus-prod-wsp-usp-bentley.com\usps4-usp-ill\Documents\Project: 62W38-01-IL 53 Bridge\CAD Sheets\11-53-Stage1-15AUSD.dgn



KEY MAP

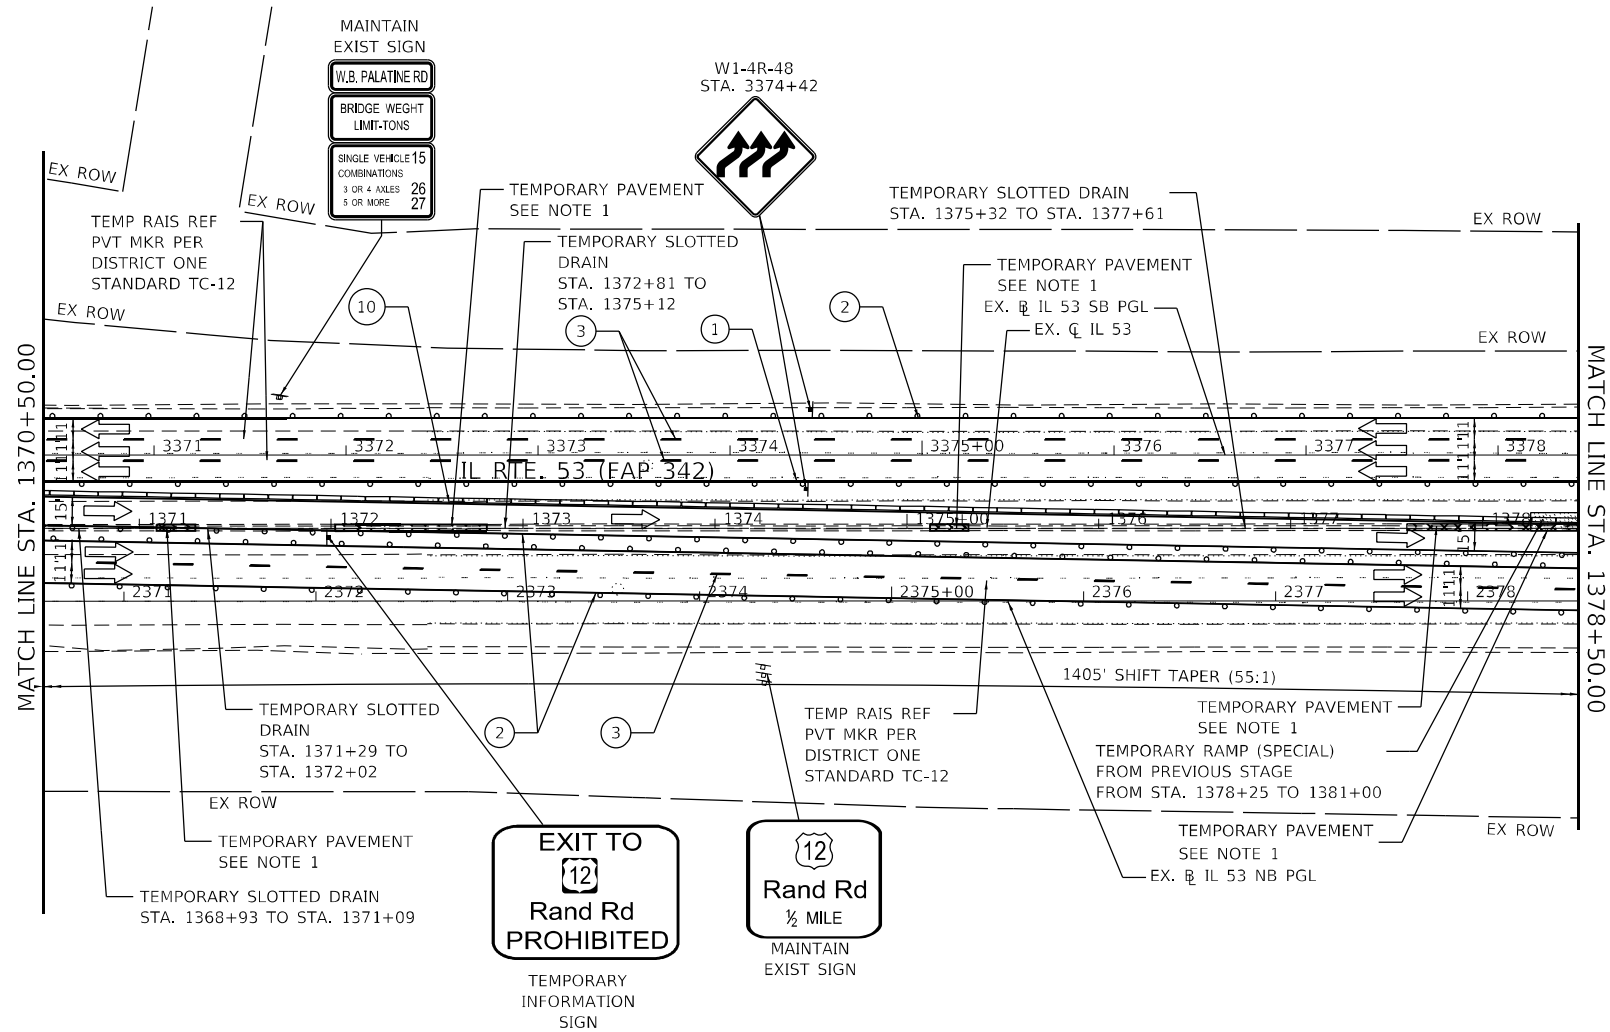

NOTES

1. TEMPORARY PAVEMENT PREVIOUSLY BUILT DURING PRESTAGE.

LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



USER NAME = USTC714594
PLOT SCALE = 100,0000 ' / in.
PLOT DATE = 9/23/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024



REVISED -
REVISED -
REVISED -
REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN - STAGE 1


SCALE: 1" = 50' SHEET 15 OF 17 SHEETS STA. 1370+50.00 TO STA. 1378+50.00


F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	261
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				





1. PORTABLE CHANGEABLE MESSAGE SIGN CONTENT SHALL BE DETERMINED BY THE ENGINEER.
2. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMP SHALL REMAIN IN PLACE FROM STAGE 1.

- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |

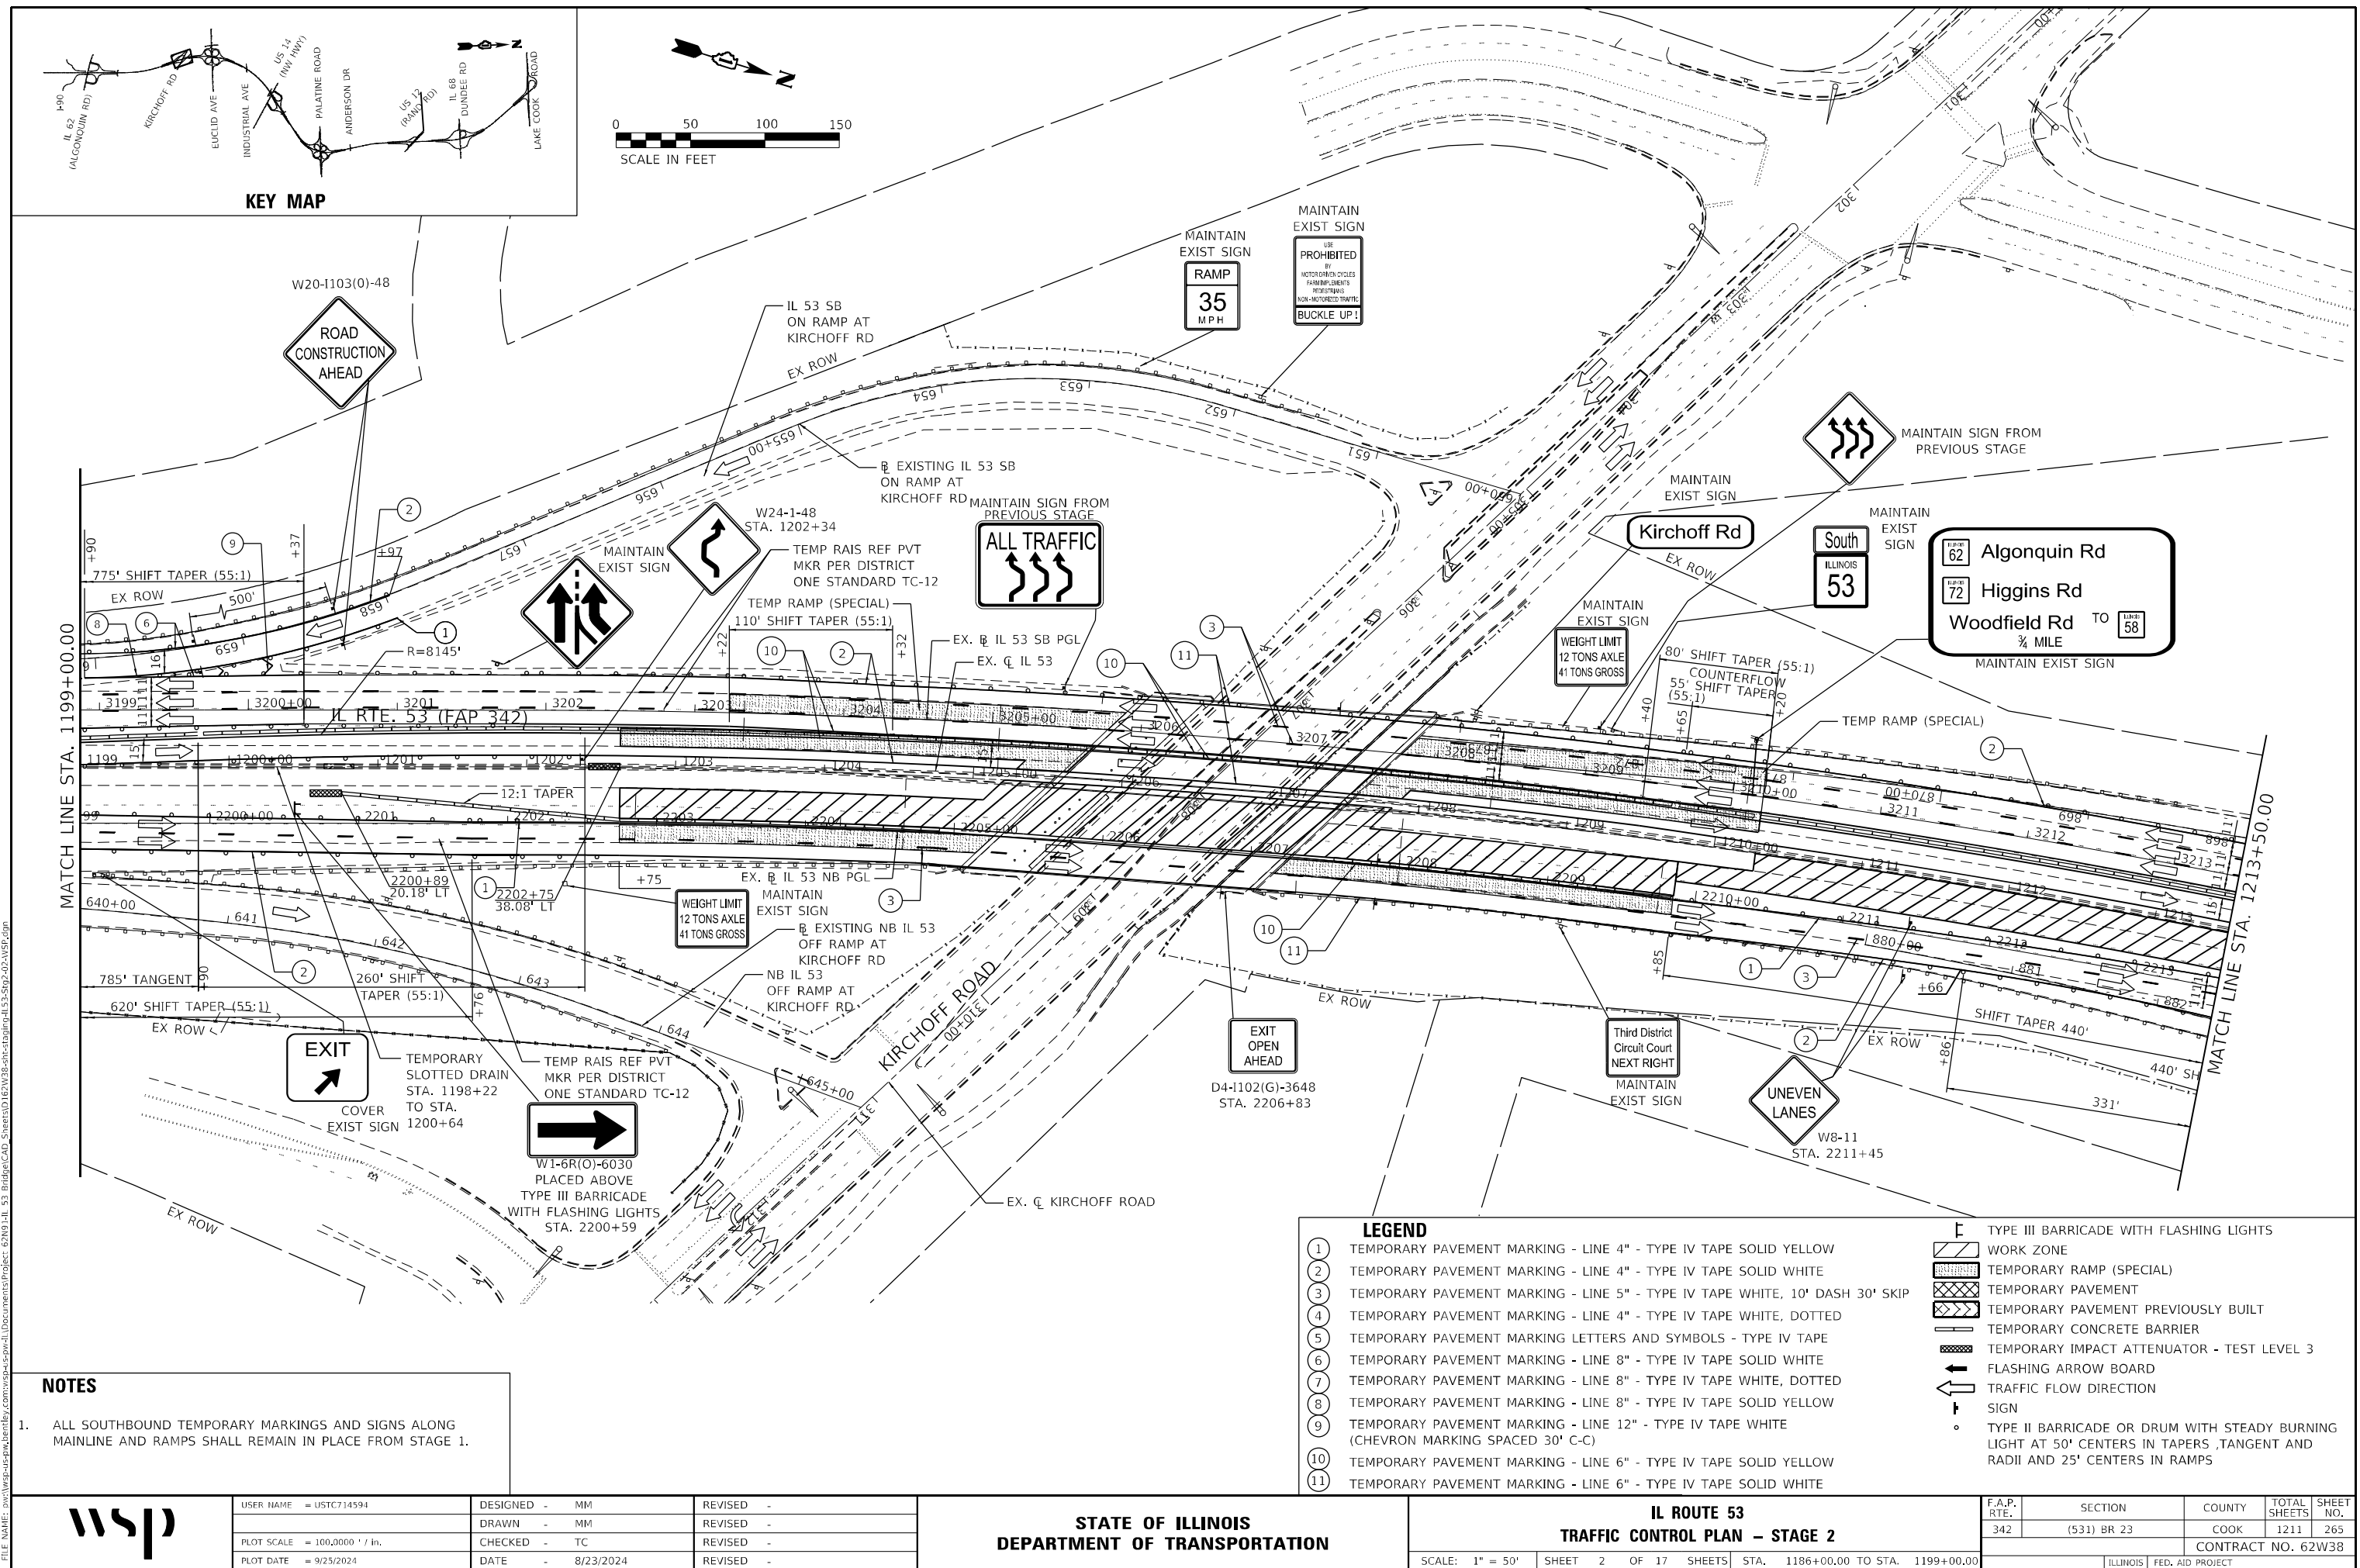



KEY MAP

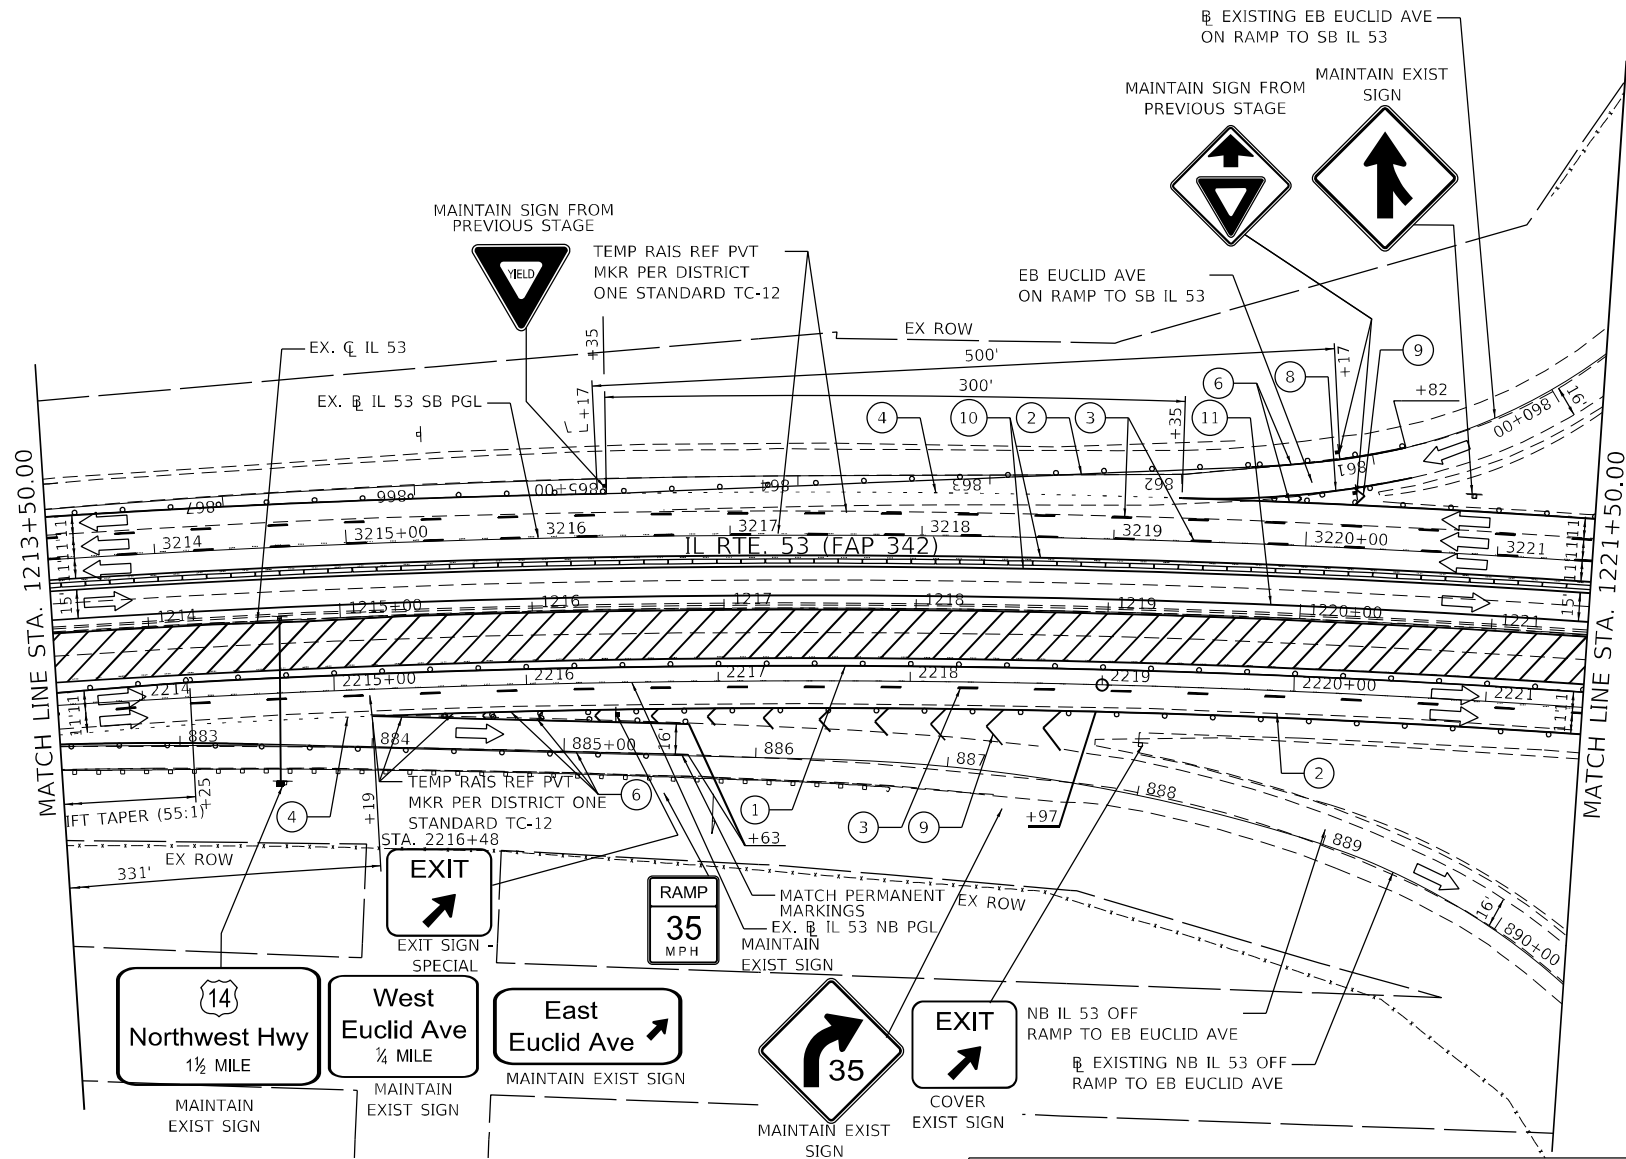

LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.



USER NAME	= USTC714594
PLOT SCALE	= 100,0000 ' / in.
PLOT DATE	= 9/23/2024


DESIGNED	-	MM	REVISED	-
DRAWN	-	MM	REVISED	-
CHECKED	-	TC	REVISED	-
DATE	-	8/23/2024	REVISED	-




STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN – STAGE 2

SCALE: 1" = 50' SHEET 3 OF 17 SHEETS STA. 1213+50.00 TO STA. 1221+50.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	266
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

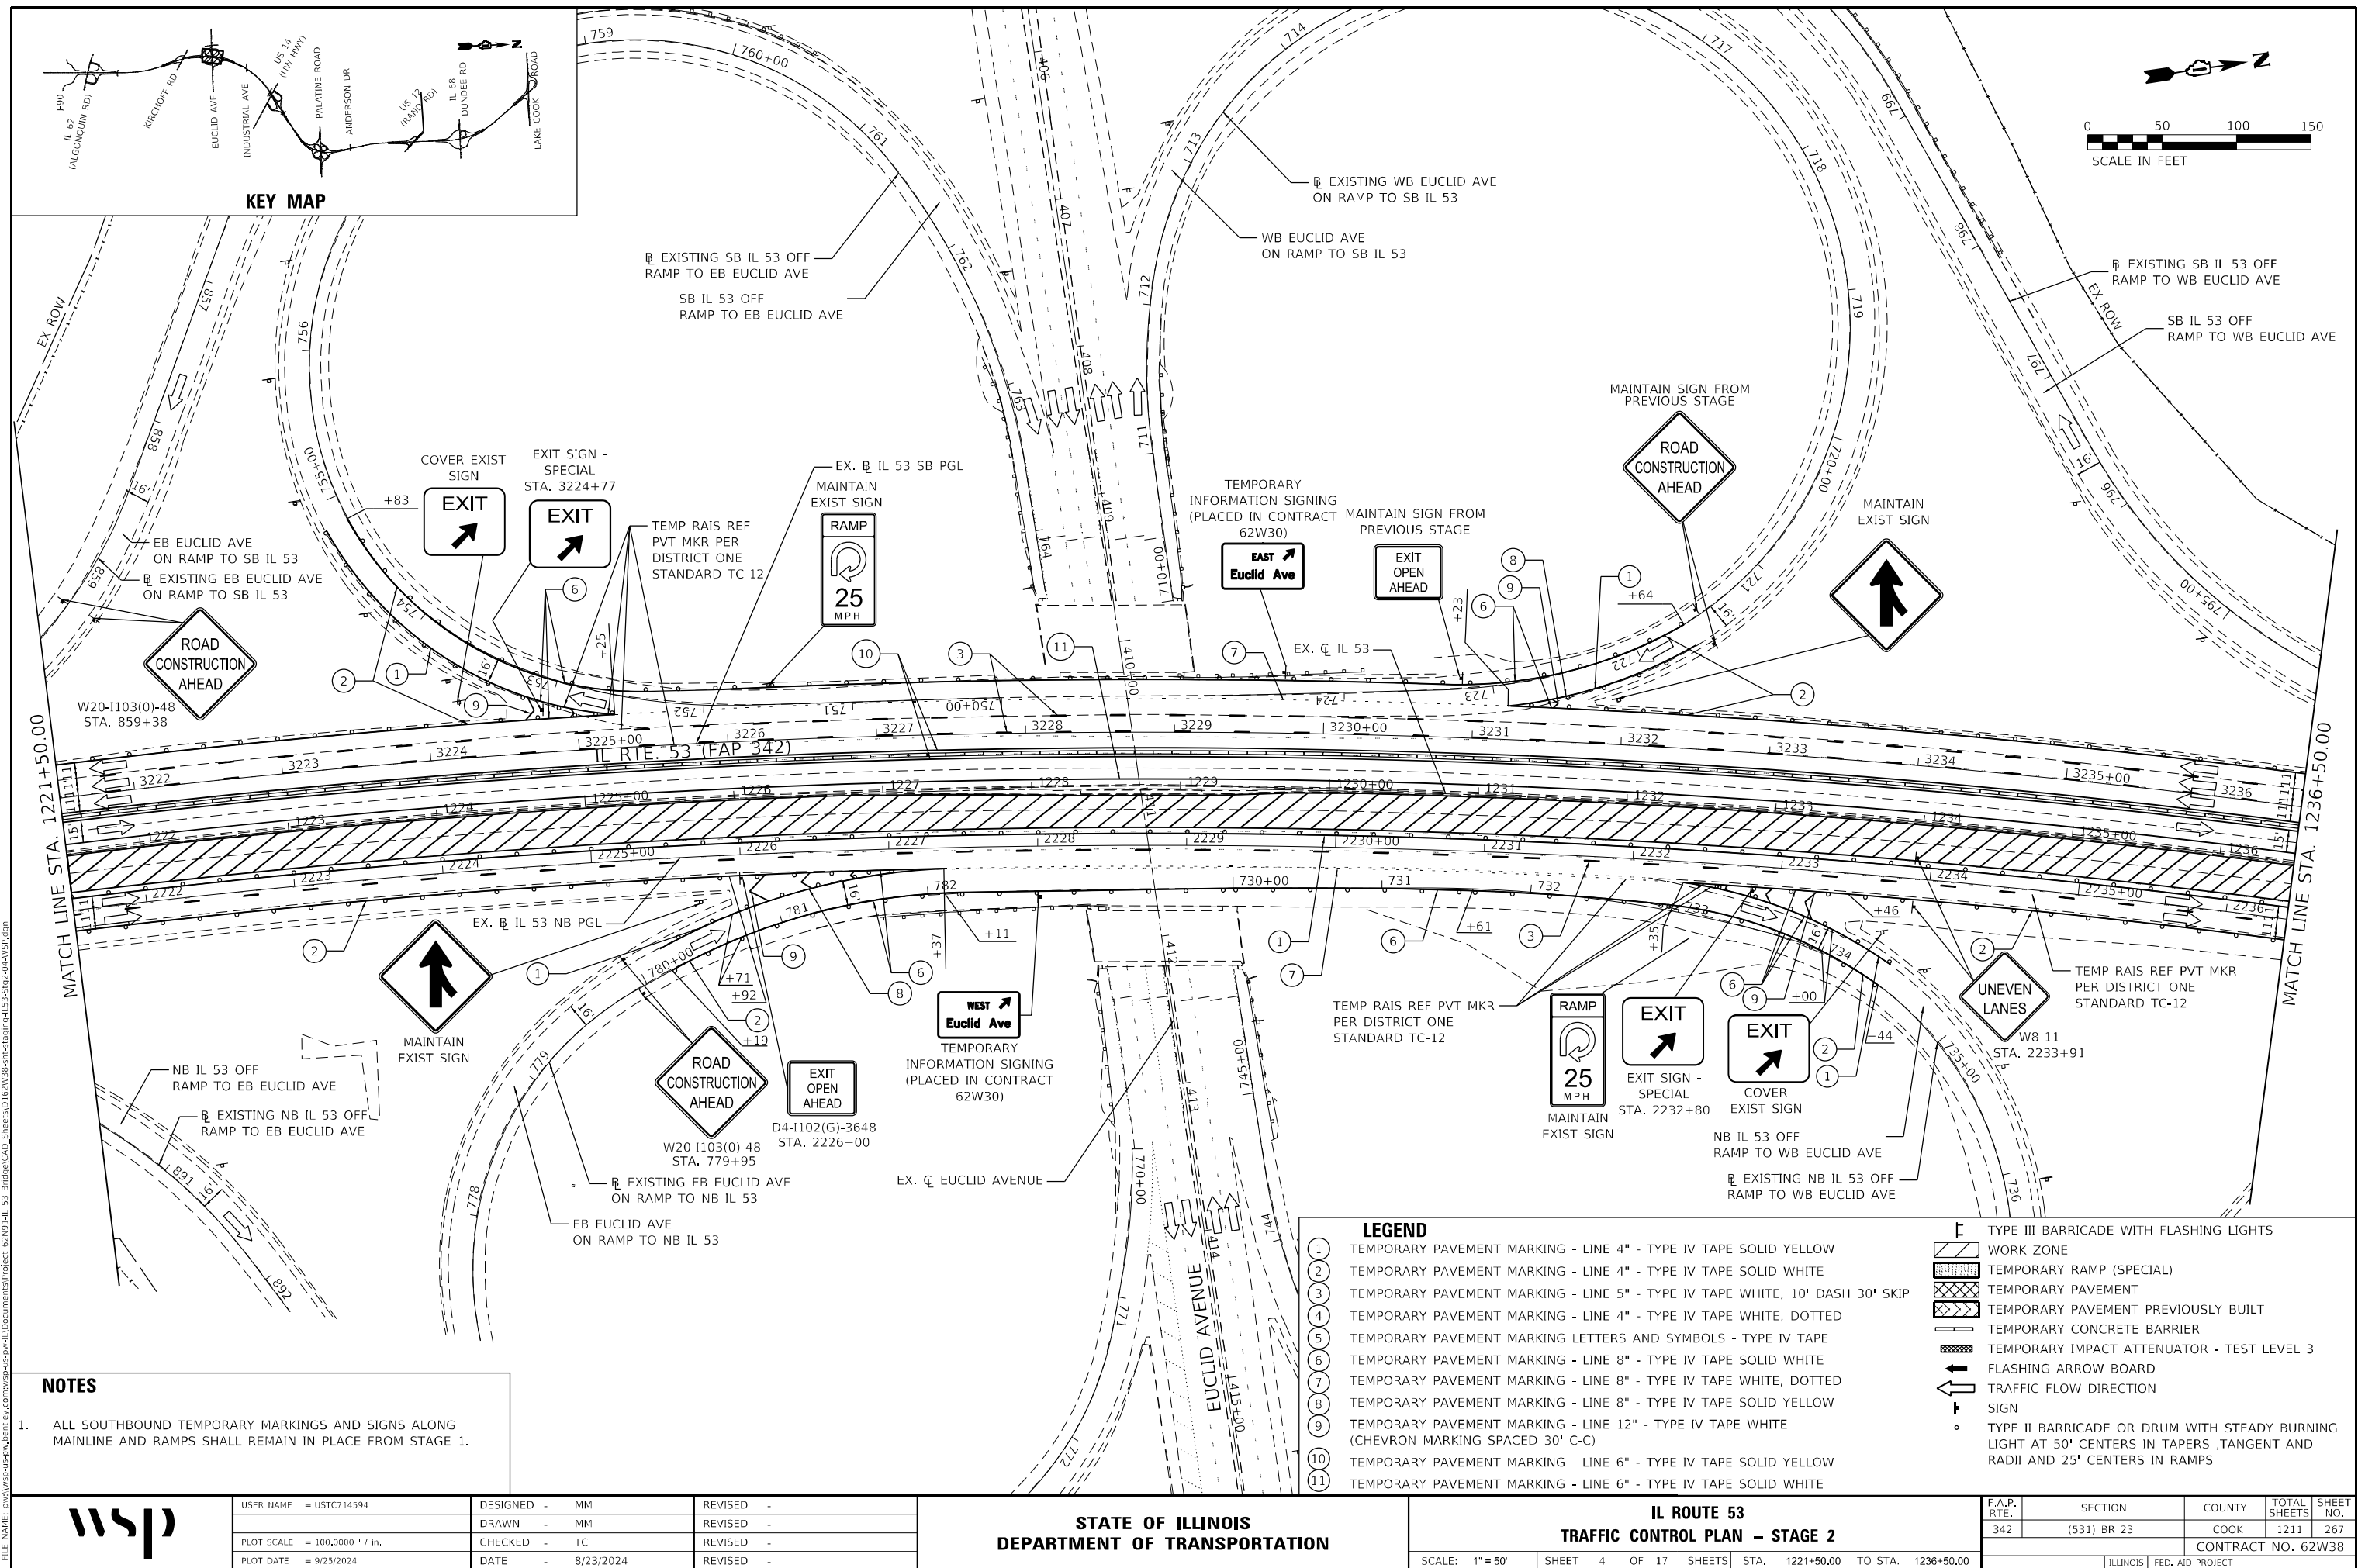

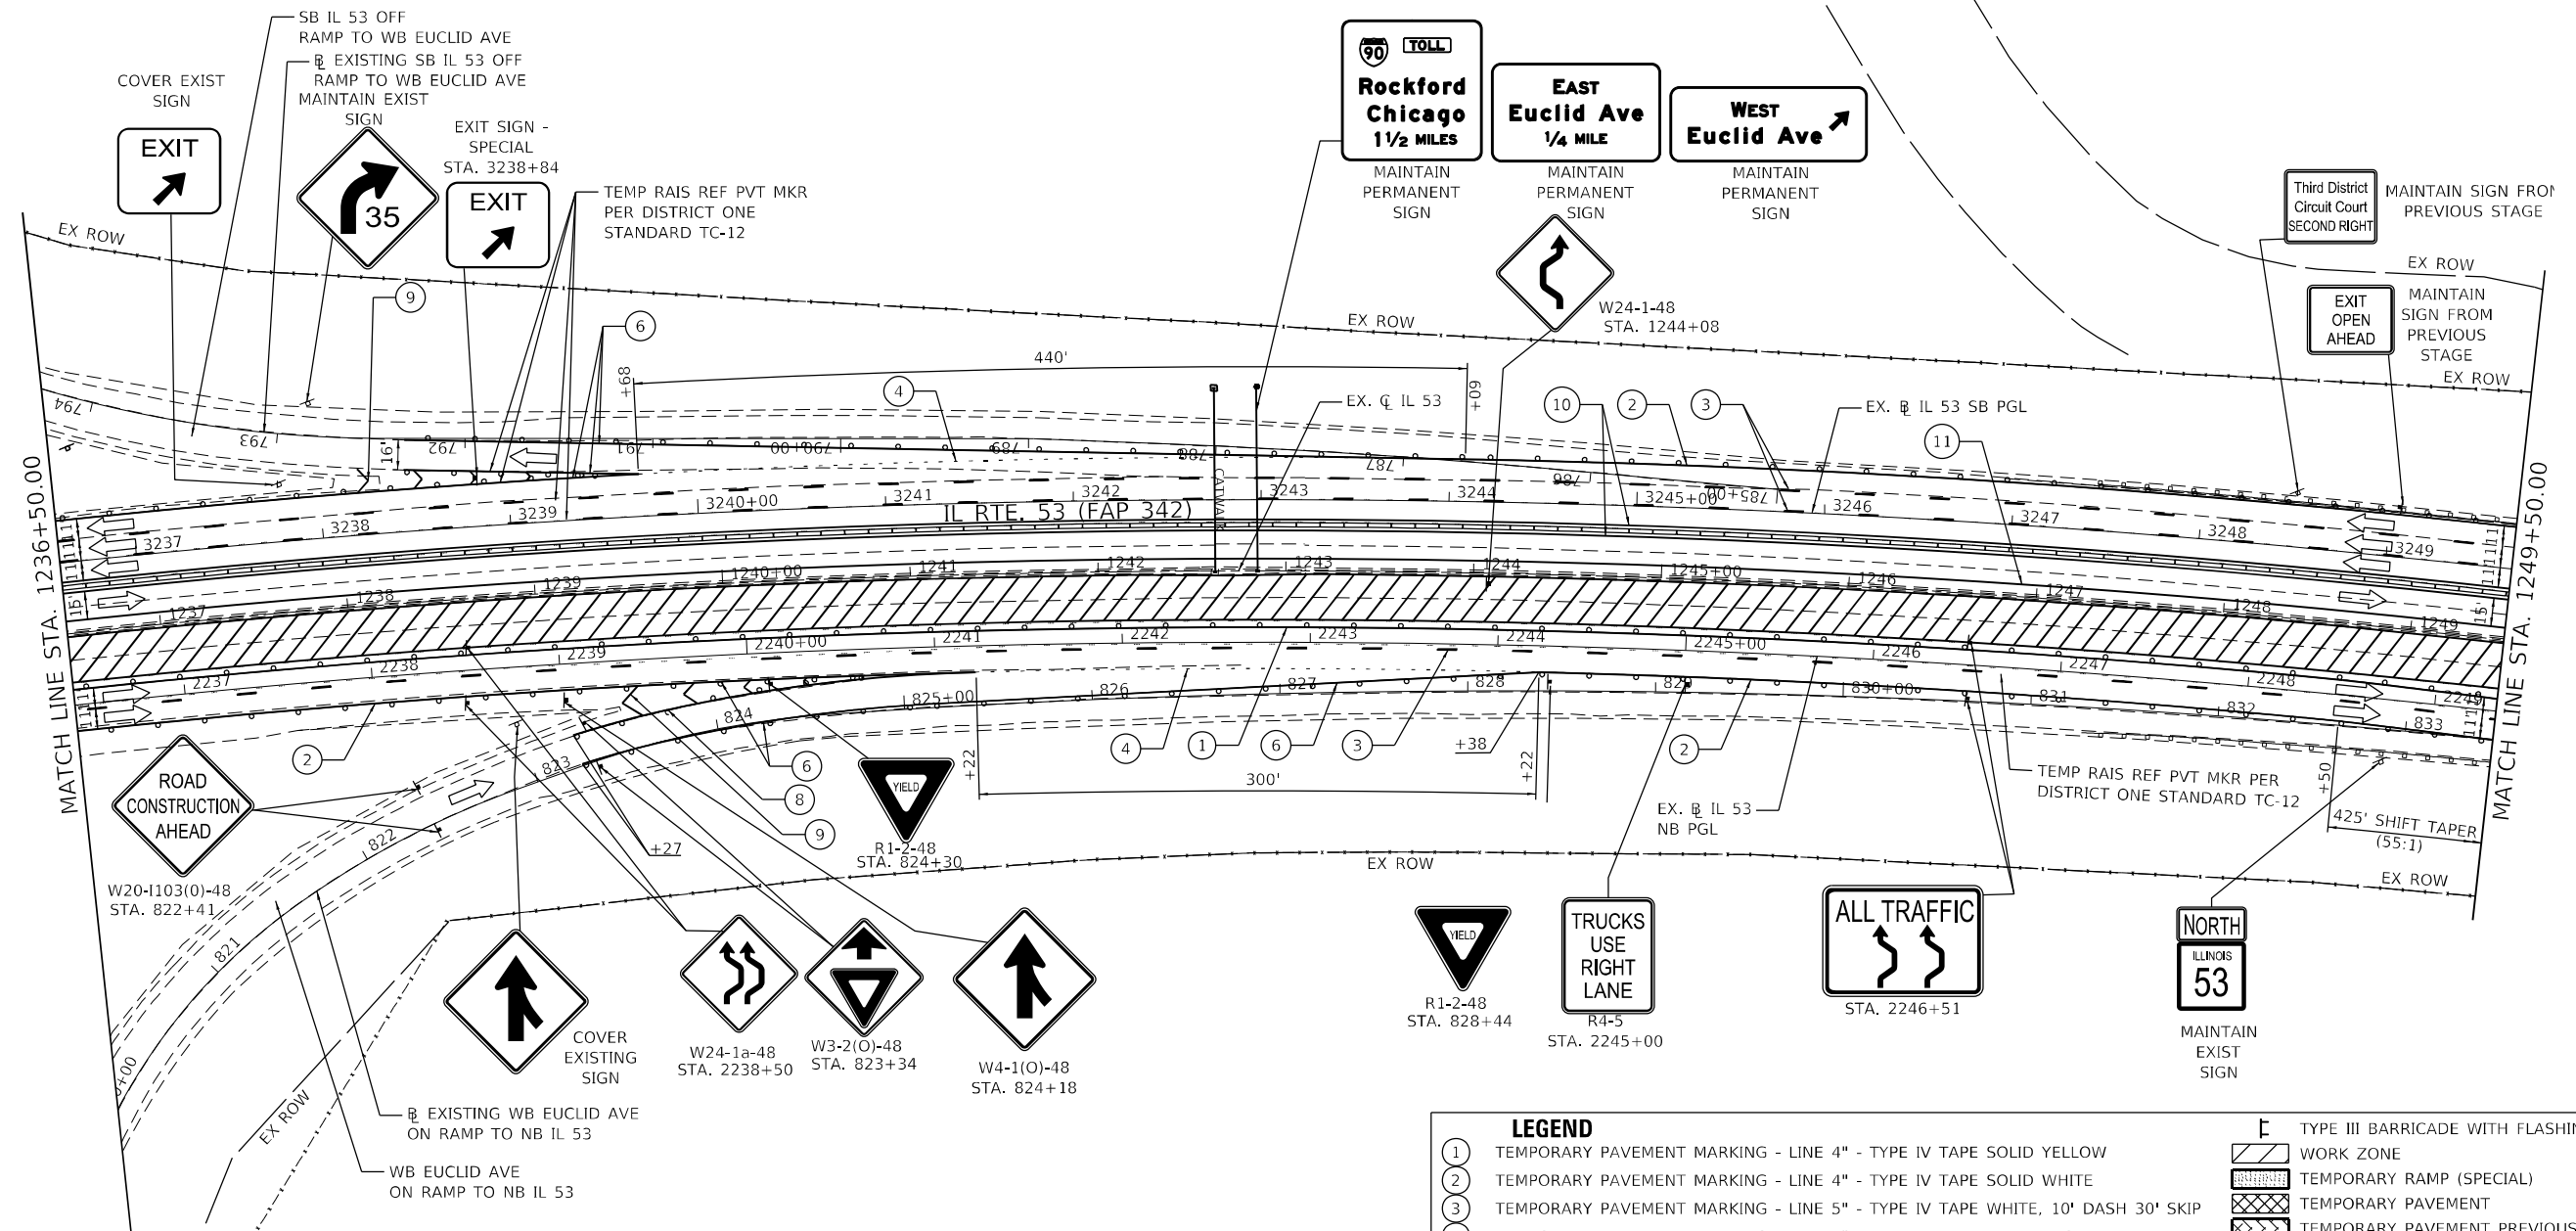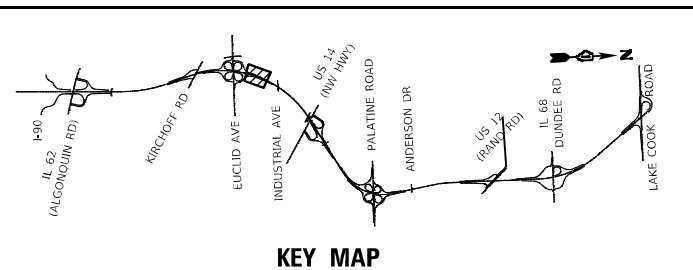

NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

LEGEND

- | LEGEND | |
|--------|--|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE
(CHEVRON MARKING SPACED 30' C-C) |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE |

- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |



MAINTAIN EXIST SIGN



MAINTAIN
EXIST SIGN

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- | | |
|--|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS |

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -


STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

**IL ROUTE 53
TRAFFIC CONTROL PLAN – STAGE 2**



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	269
		CONTRACT NO. 62W38		
ILLINOIS		FED. AID PROJECT		

MODEL: Default
FILE NAME: dw:\web-us-pw\kentley.com\wap-us-pw\ll\Documents\Project_62N9J-1JL_53_Bridge\CAD_Sheets\ID162W\38-sht-estaging-IL59-Stg2-06-VSP.dgn

MODEL: Default
FILE: \\wsp-04-epw-bentley.com\uspc4-epw-ill\Documents\Project: 62W38-01\Drawings\IL53-Stage2-07-USD.dgn



KEY MAP

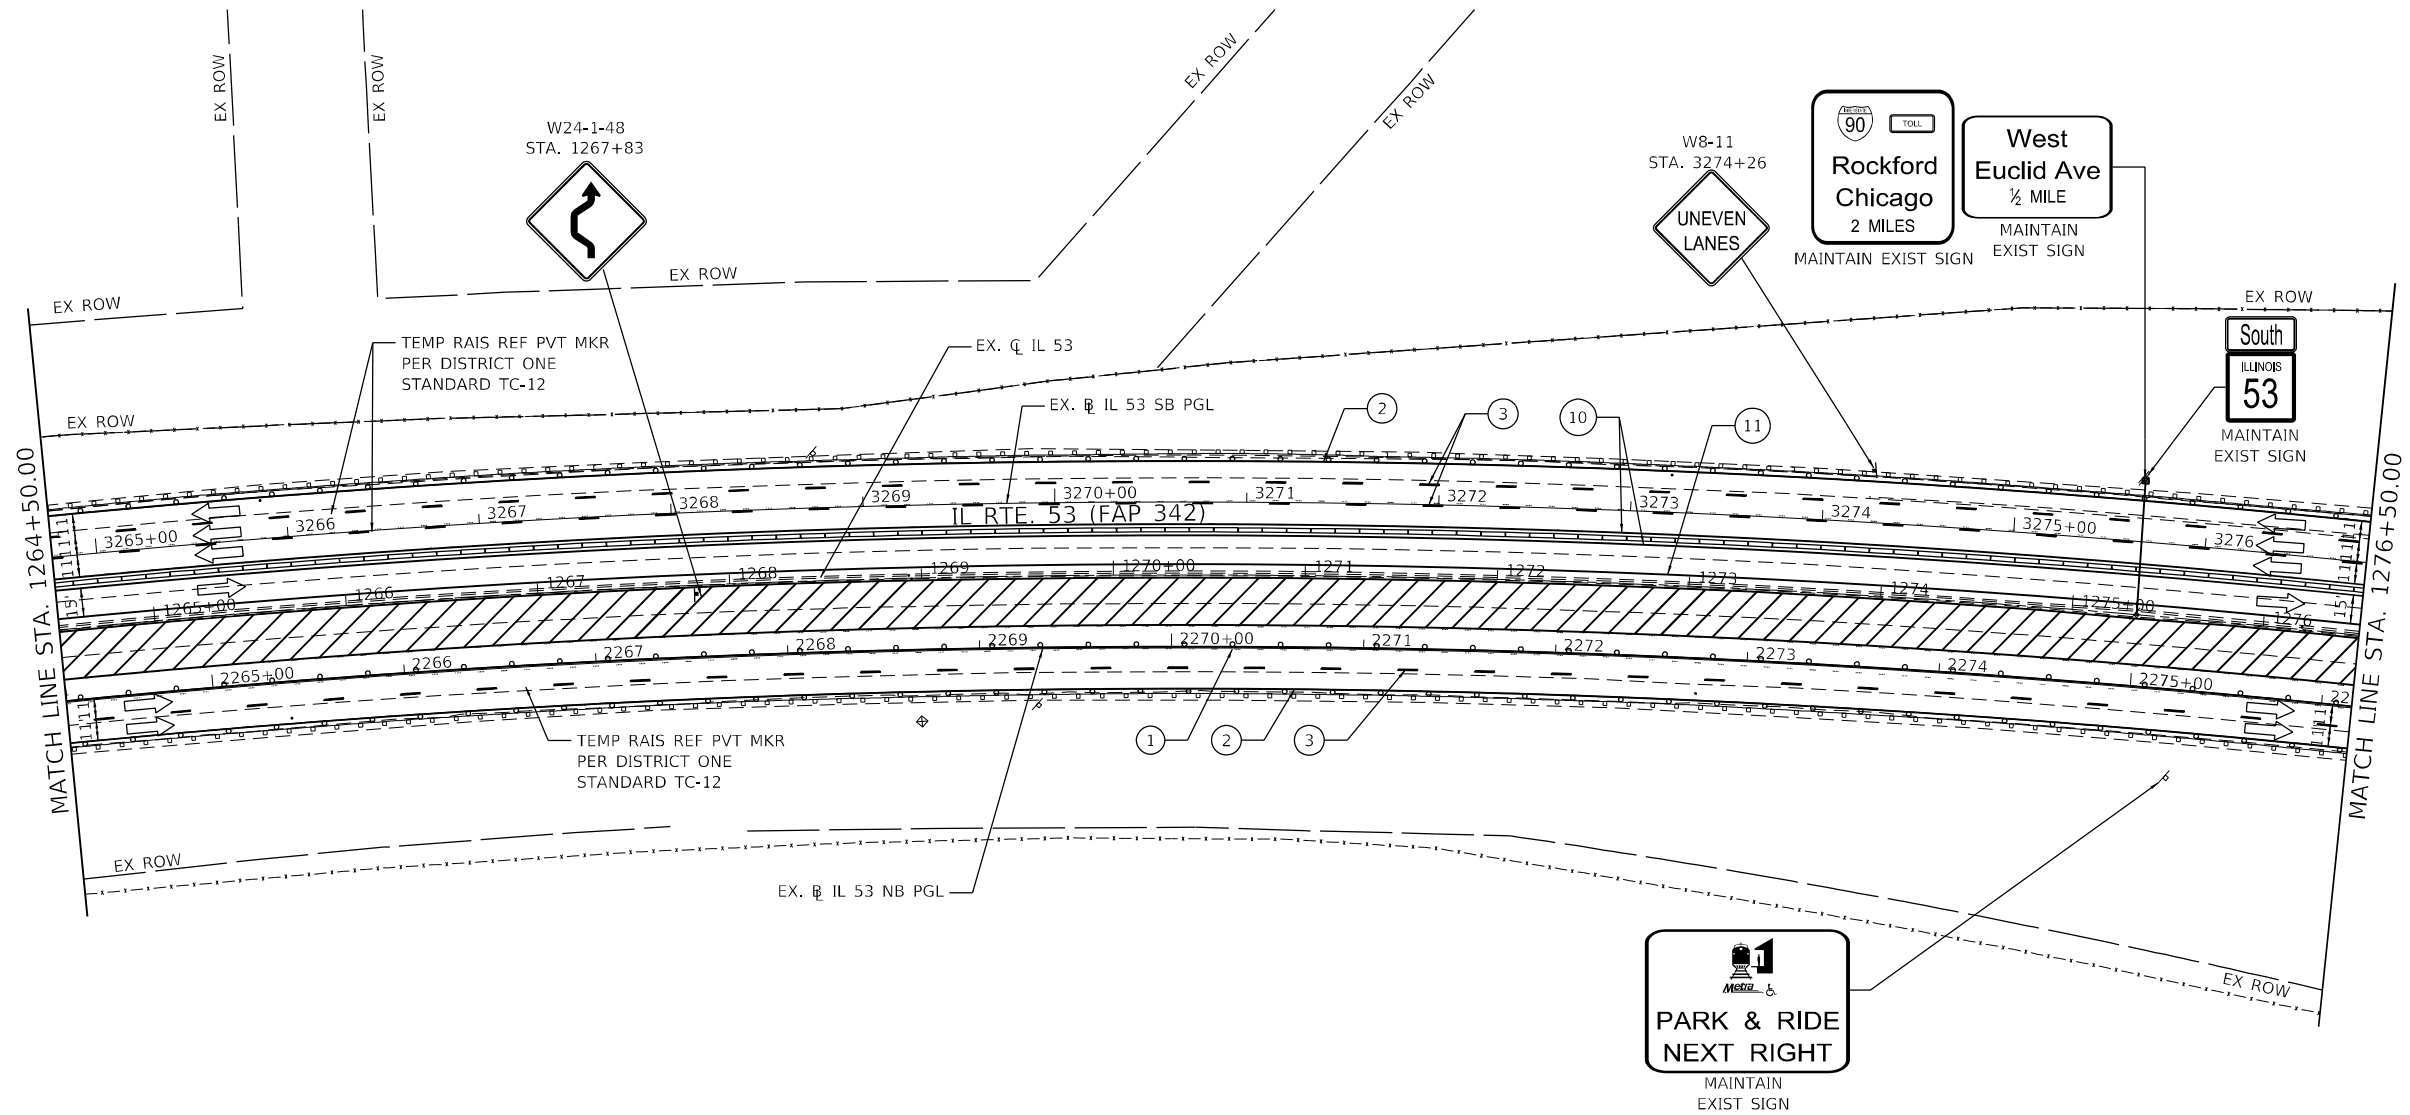

NOTES

- ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

LEGEND

- TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



USER NAME = USTC714594
PLOT SCALE = 100,0000' / in.
PLOT DATE = 9/23/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024


REVISED -
REVISED -
REVISED -
REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN - STAGE 2

SCALE: 1" = 50'
SHEET 7 OF 17 SHEETS
STA. 1264+50.00 TO STA. 1276+50.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	270
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

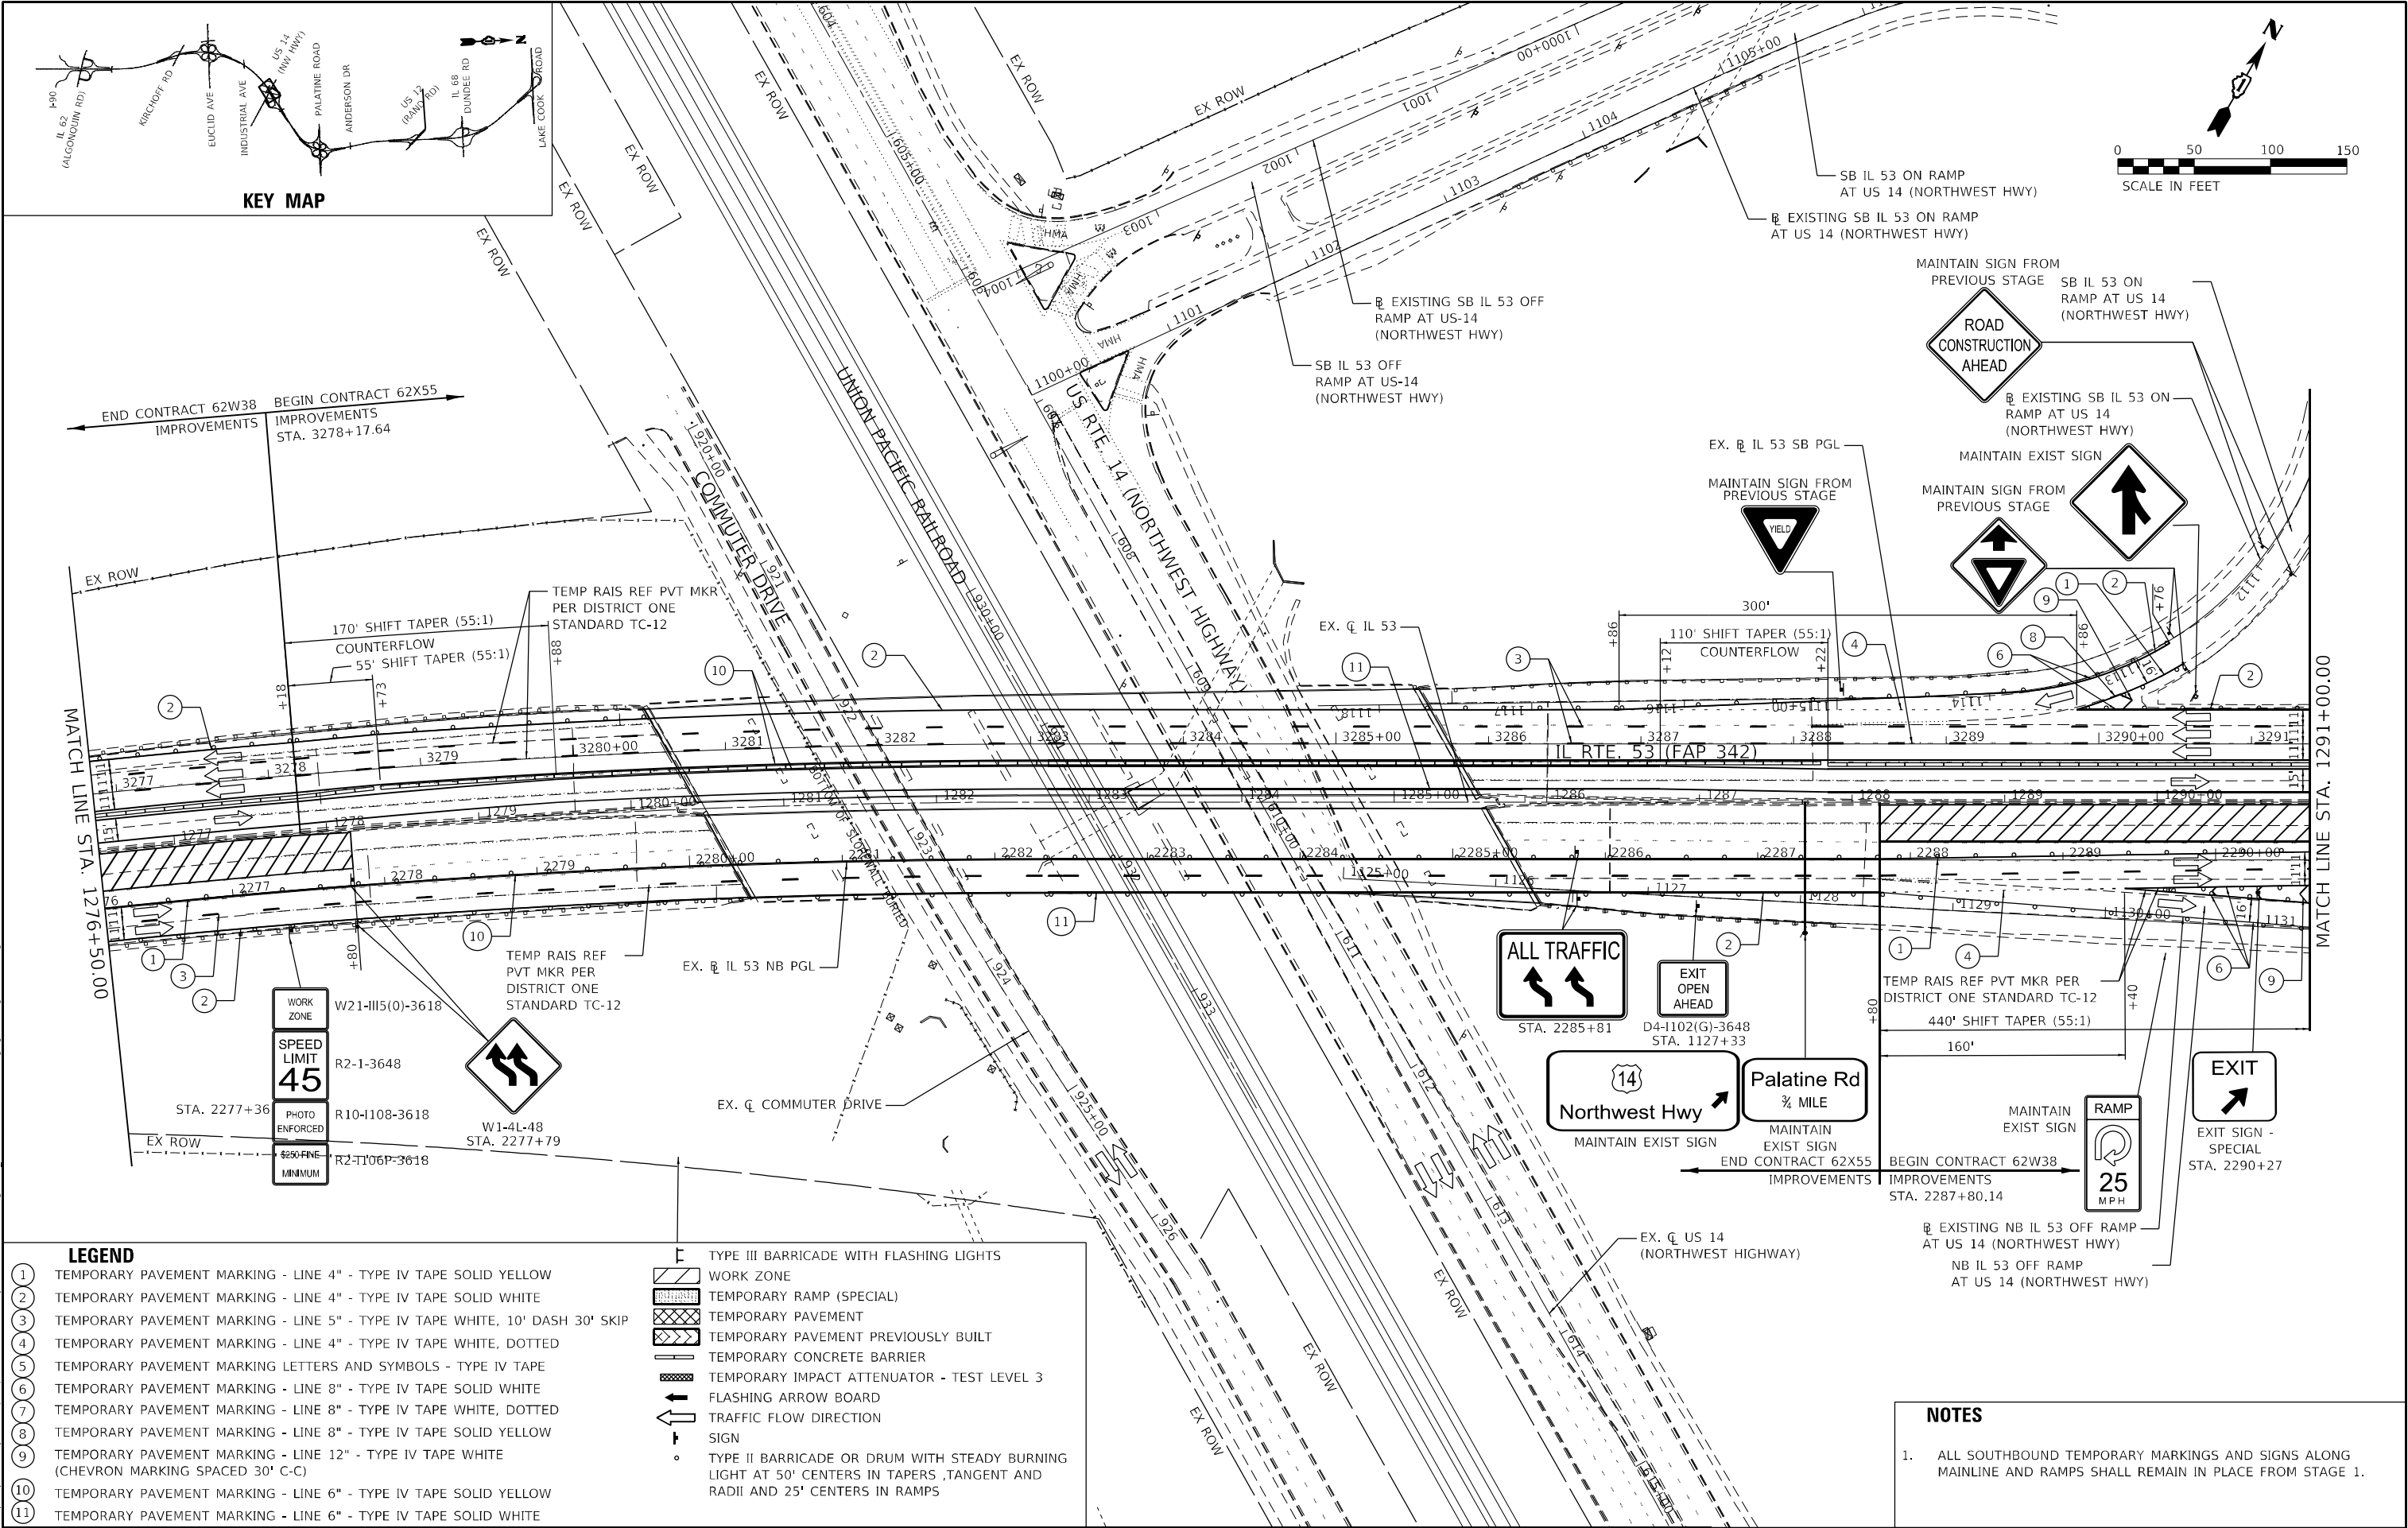

LEGEND

1

2

3

4

5

6

7

8

9

10

11

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP

TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED

TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW

TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

TYPE III BARRICADE WITH FLASHING LIGHTS

WORK ZONE

TEMPORARY RAMP (SPECIAL)

TEMPORARY PAVEMENT

TEMPORARY PAVEMENT PREVIOUSLY BUILT

TEMPORARY CONCRETE BARRIER

TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3

FLASHING ARROW BOARD

TRAFFIC FLOW DIRECTION SIGN

TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMP

	USER NAME = USTC714594	DESIGNED - MM	REVISED -
	PLOT SCALE = 100,0000' / in.	CHECKED - TC	REVISED -
	PLOT DATE = 9/23/2024	DATE - 8/23/2024	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION




IL ROUTE 53 TRAFFIC CONTROL PLAN - STAGE 2			
SCALE: 1" = 50'	SHEET 8 OF 17 SHEETS	STA. 1276+50.00 TO STA. 1291+00.00	

F.A.P. RTE. 342	SECTION (531) BR 23	COUNTY COOK	TOTAL SHEETS 1211	SHEET NO. 271
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

MODEL: Default
FILE: I:\Users\pawelpawel\OneDrive\Documents\Projects\62W38-2\Drawings\IL53-Stage2-09A-USP.dgn

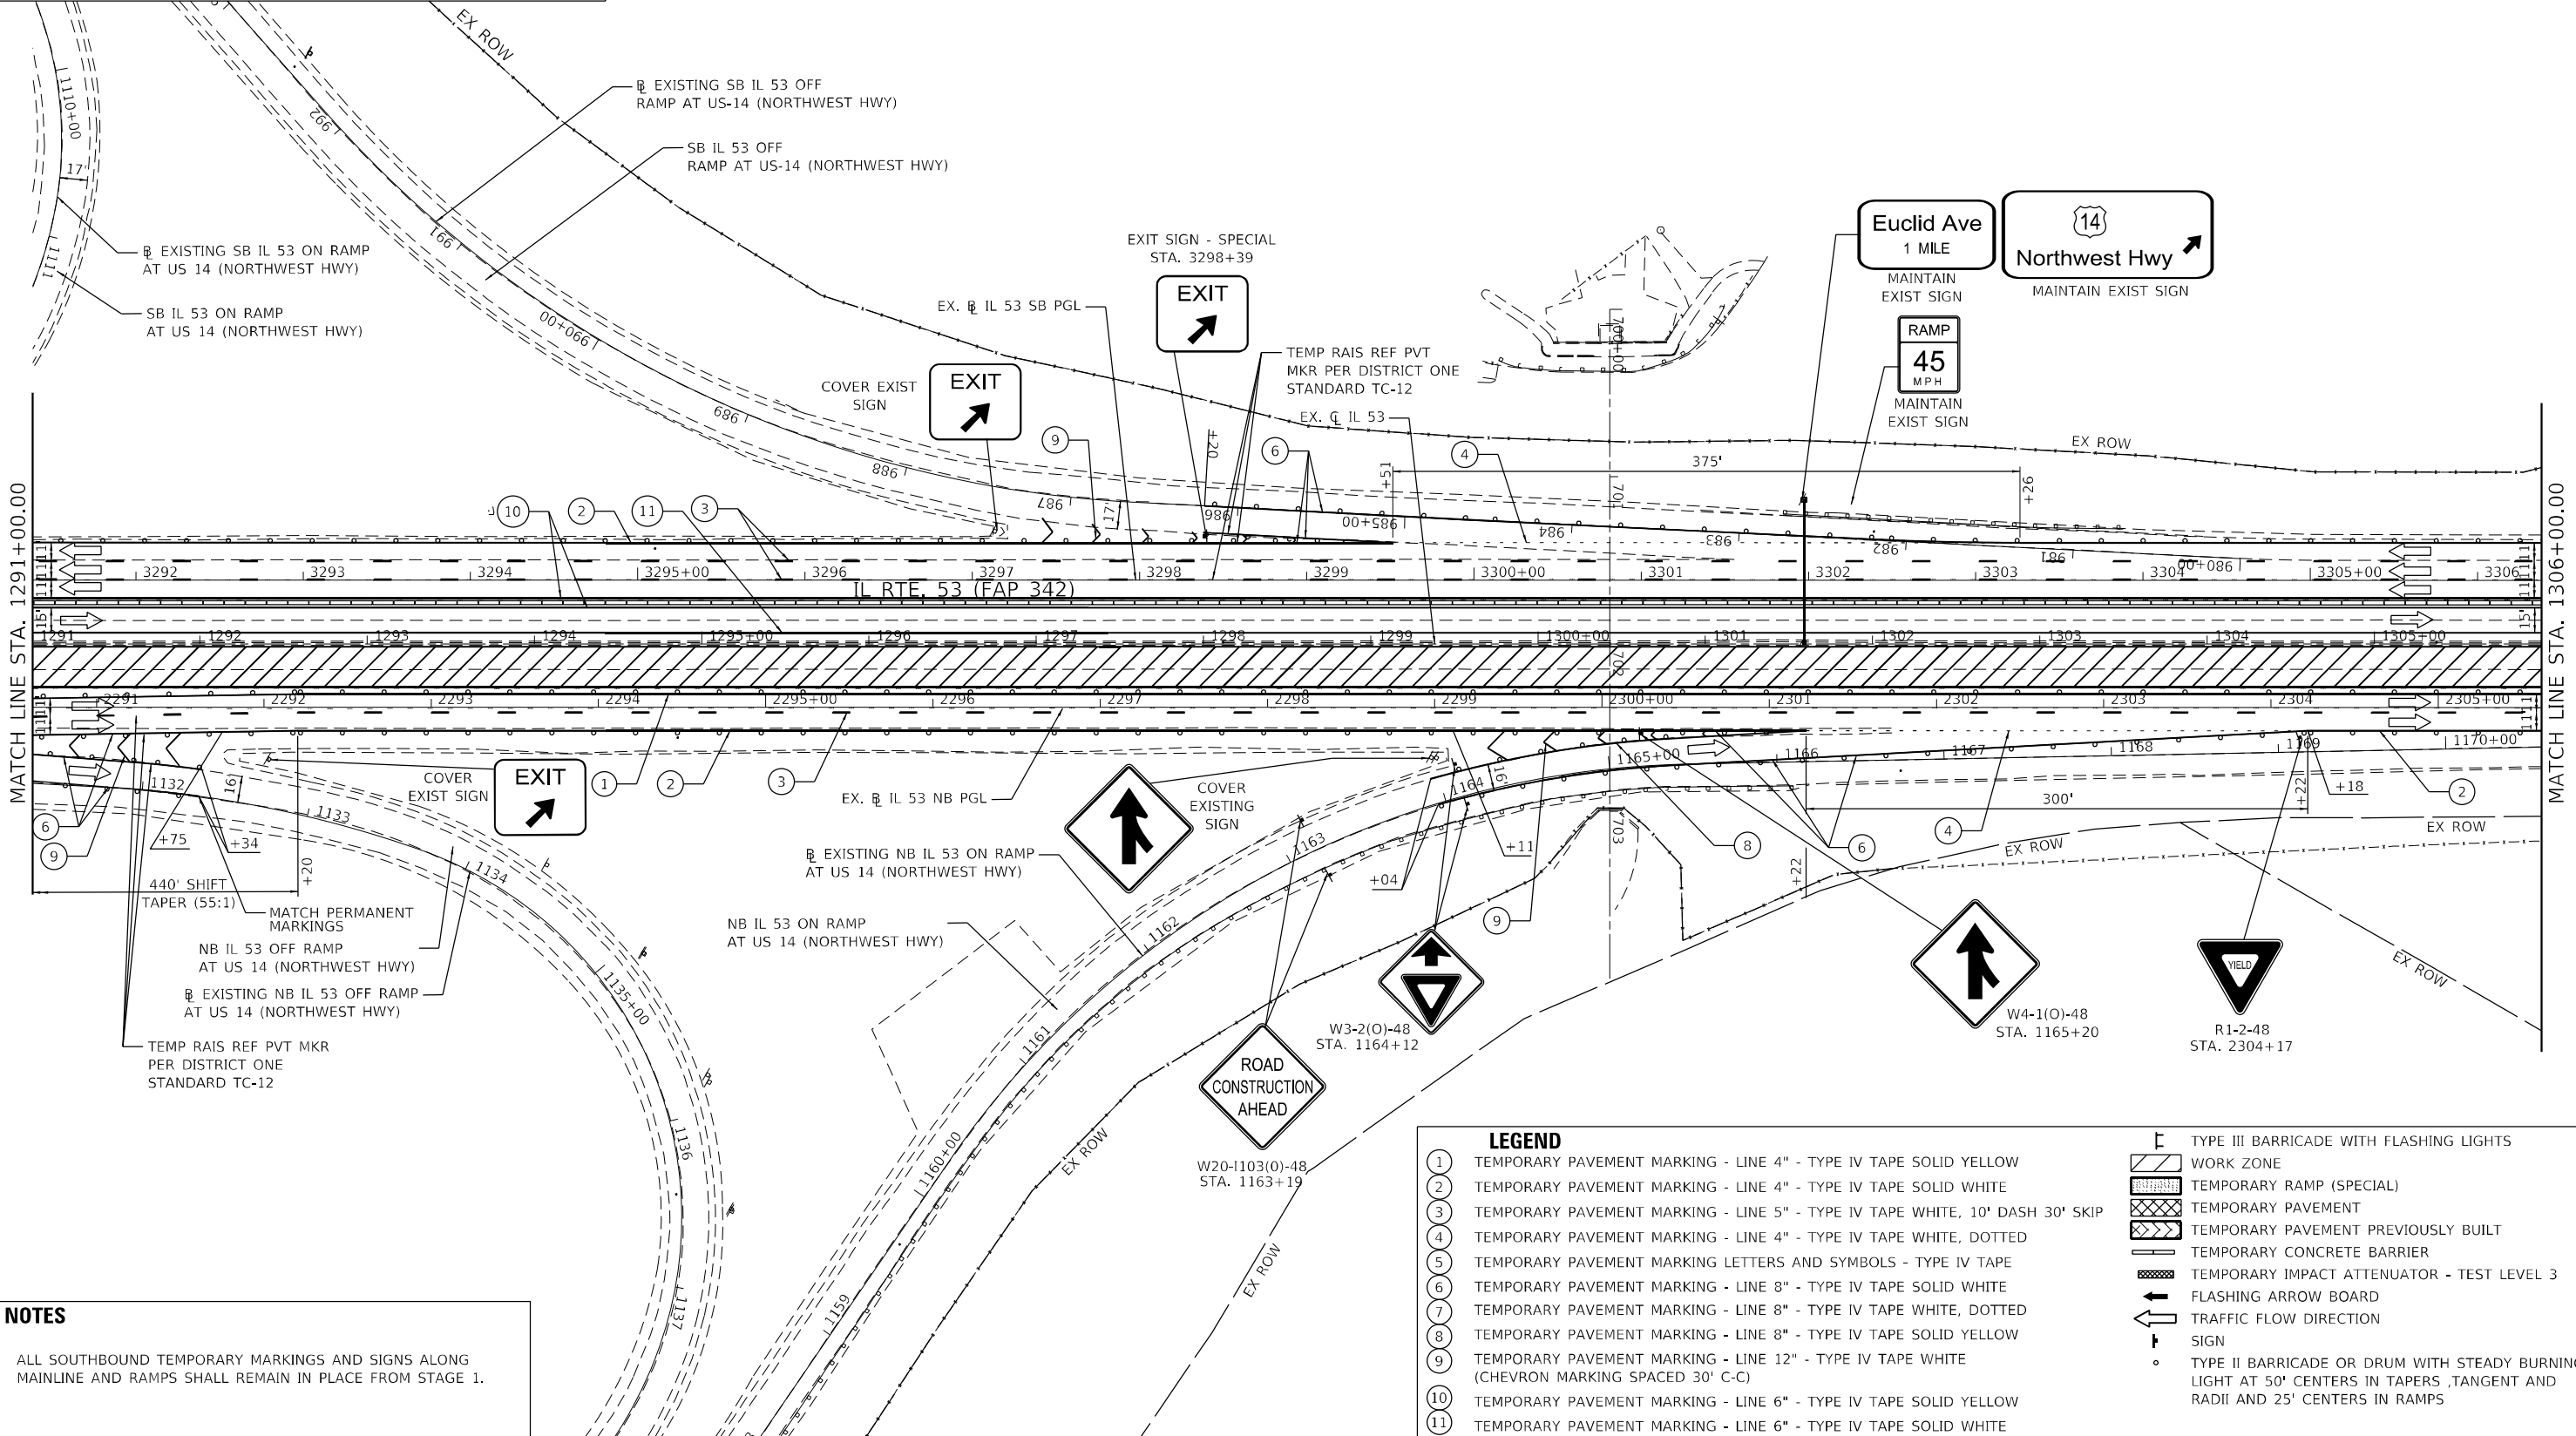

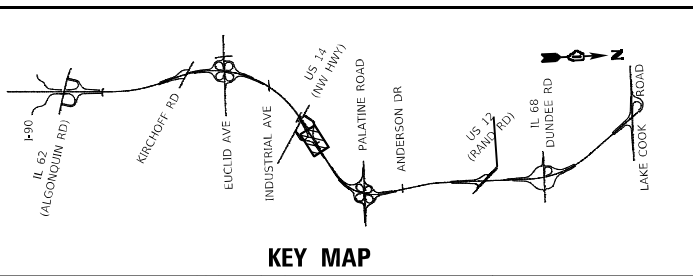


NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE
	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – STAGE 2				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	272
	PLOT SCALE = 100,000' / in.	CHECKED - TC	REVISED -						CONTRACT NO. 62W38				
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'				SHEET 9 OF 17 SHEETS	STA. 1291+00.00 TO STA. 1306+00.00	ILLINOIS FED. AID PROJECT		

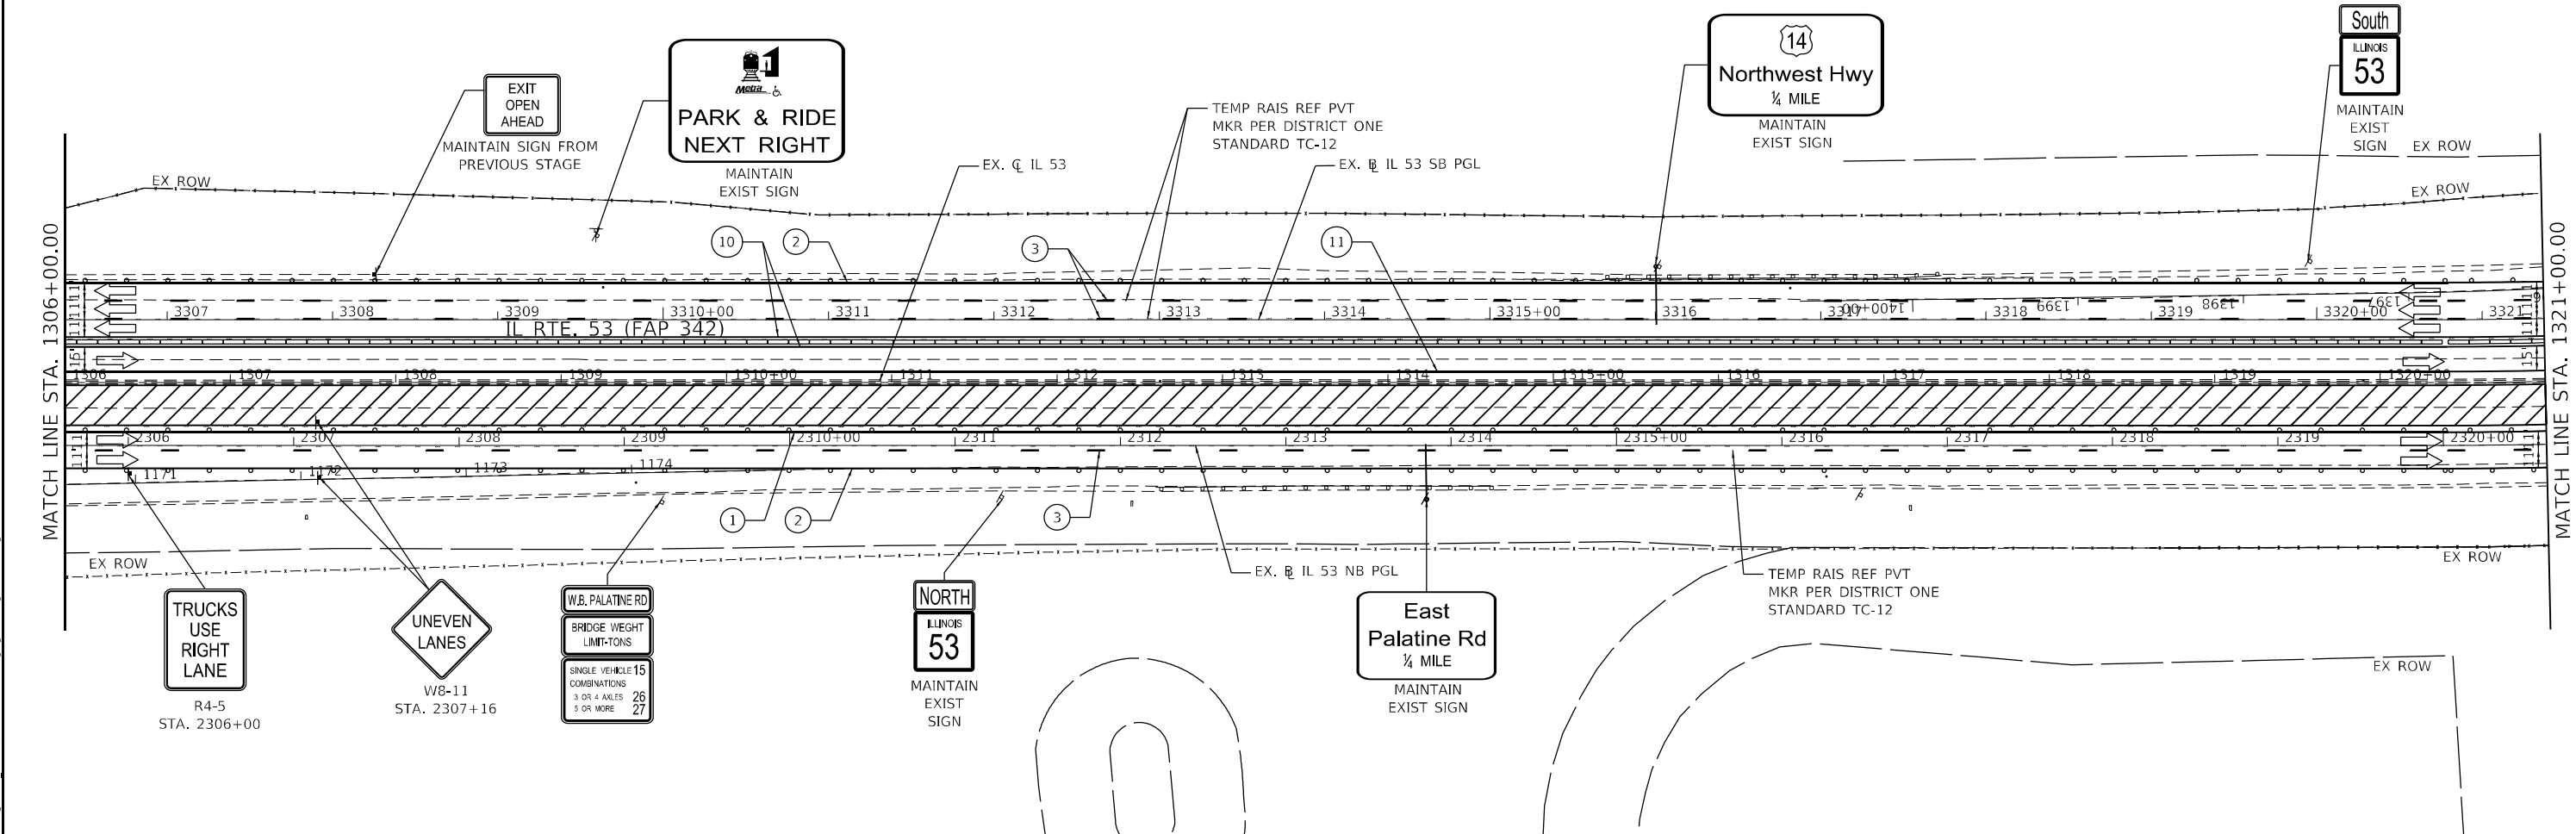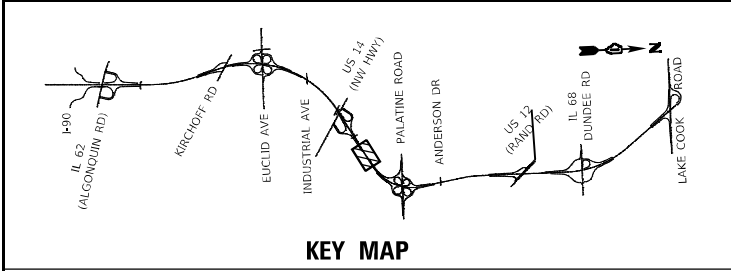


NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.



LEGEND

- 1 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
- 2 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
- 3 TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
- 4 TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
- 5 TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
- 6 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
- 7 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
- 8 TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
- 9 TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
- 10 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
- 11 TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION
- SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



KEY MAP

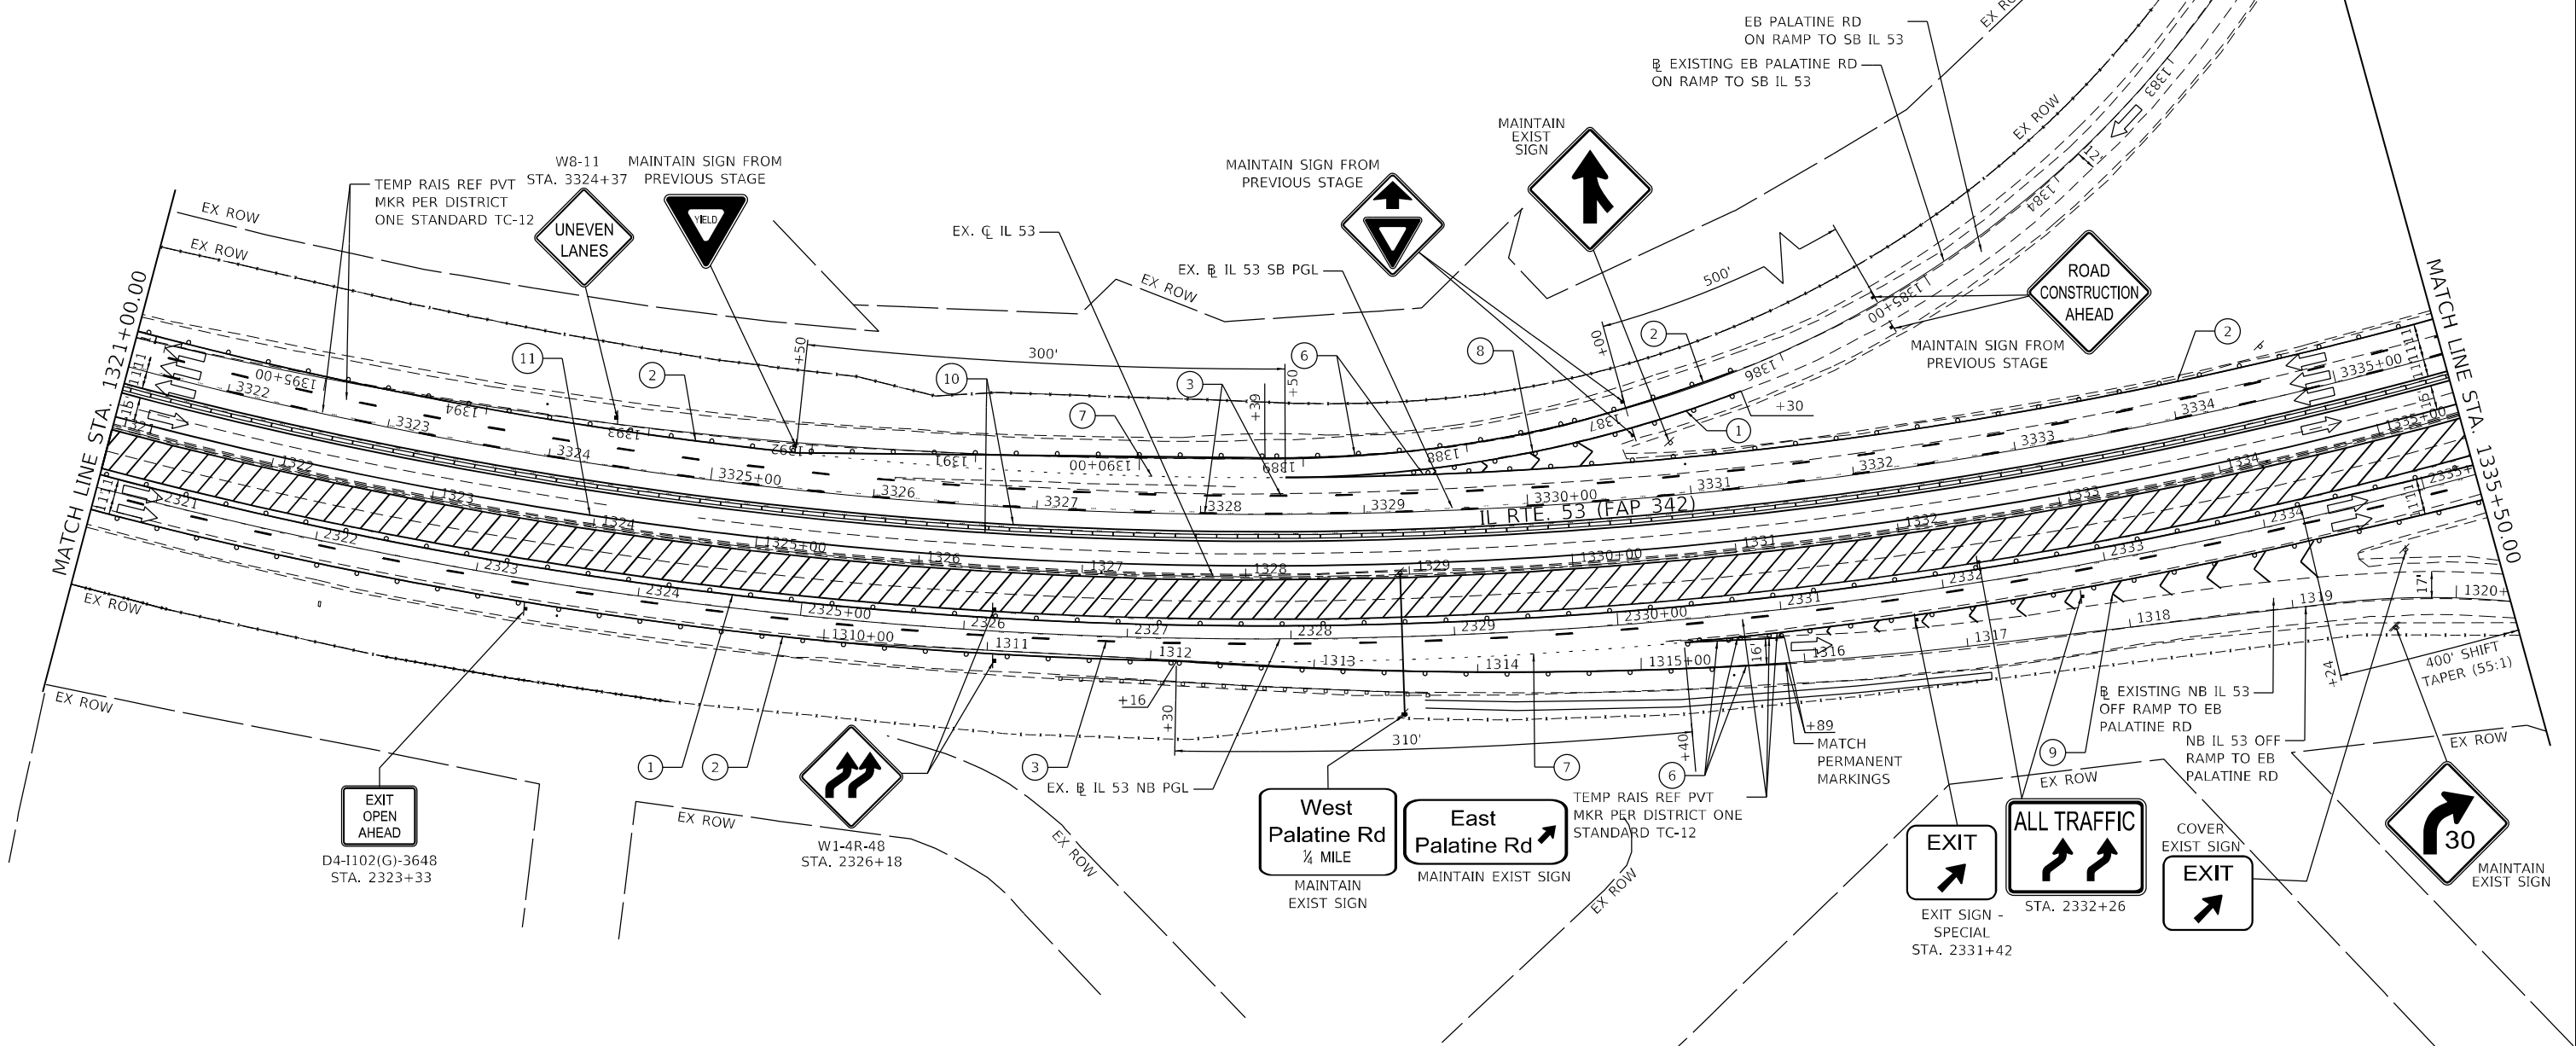


- NOTES**
- ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.



LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
2	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
3	TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
4	TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
6	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
7	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
8	TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
9	TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
10	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
11	TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



KEY MAP

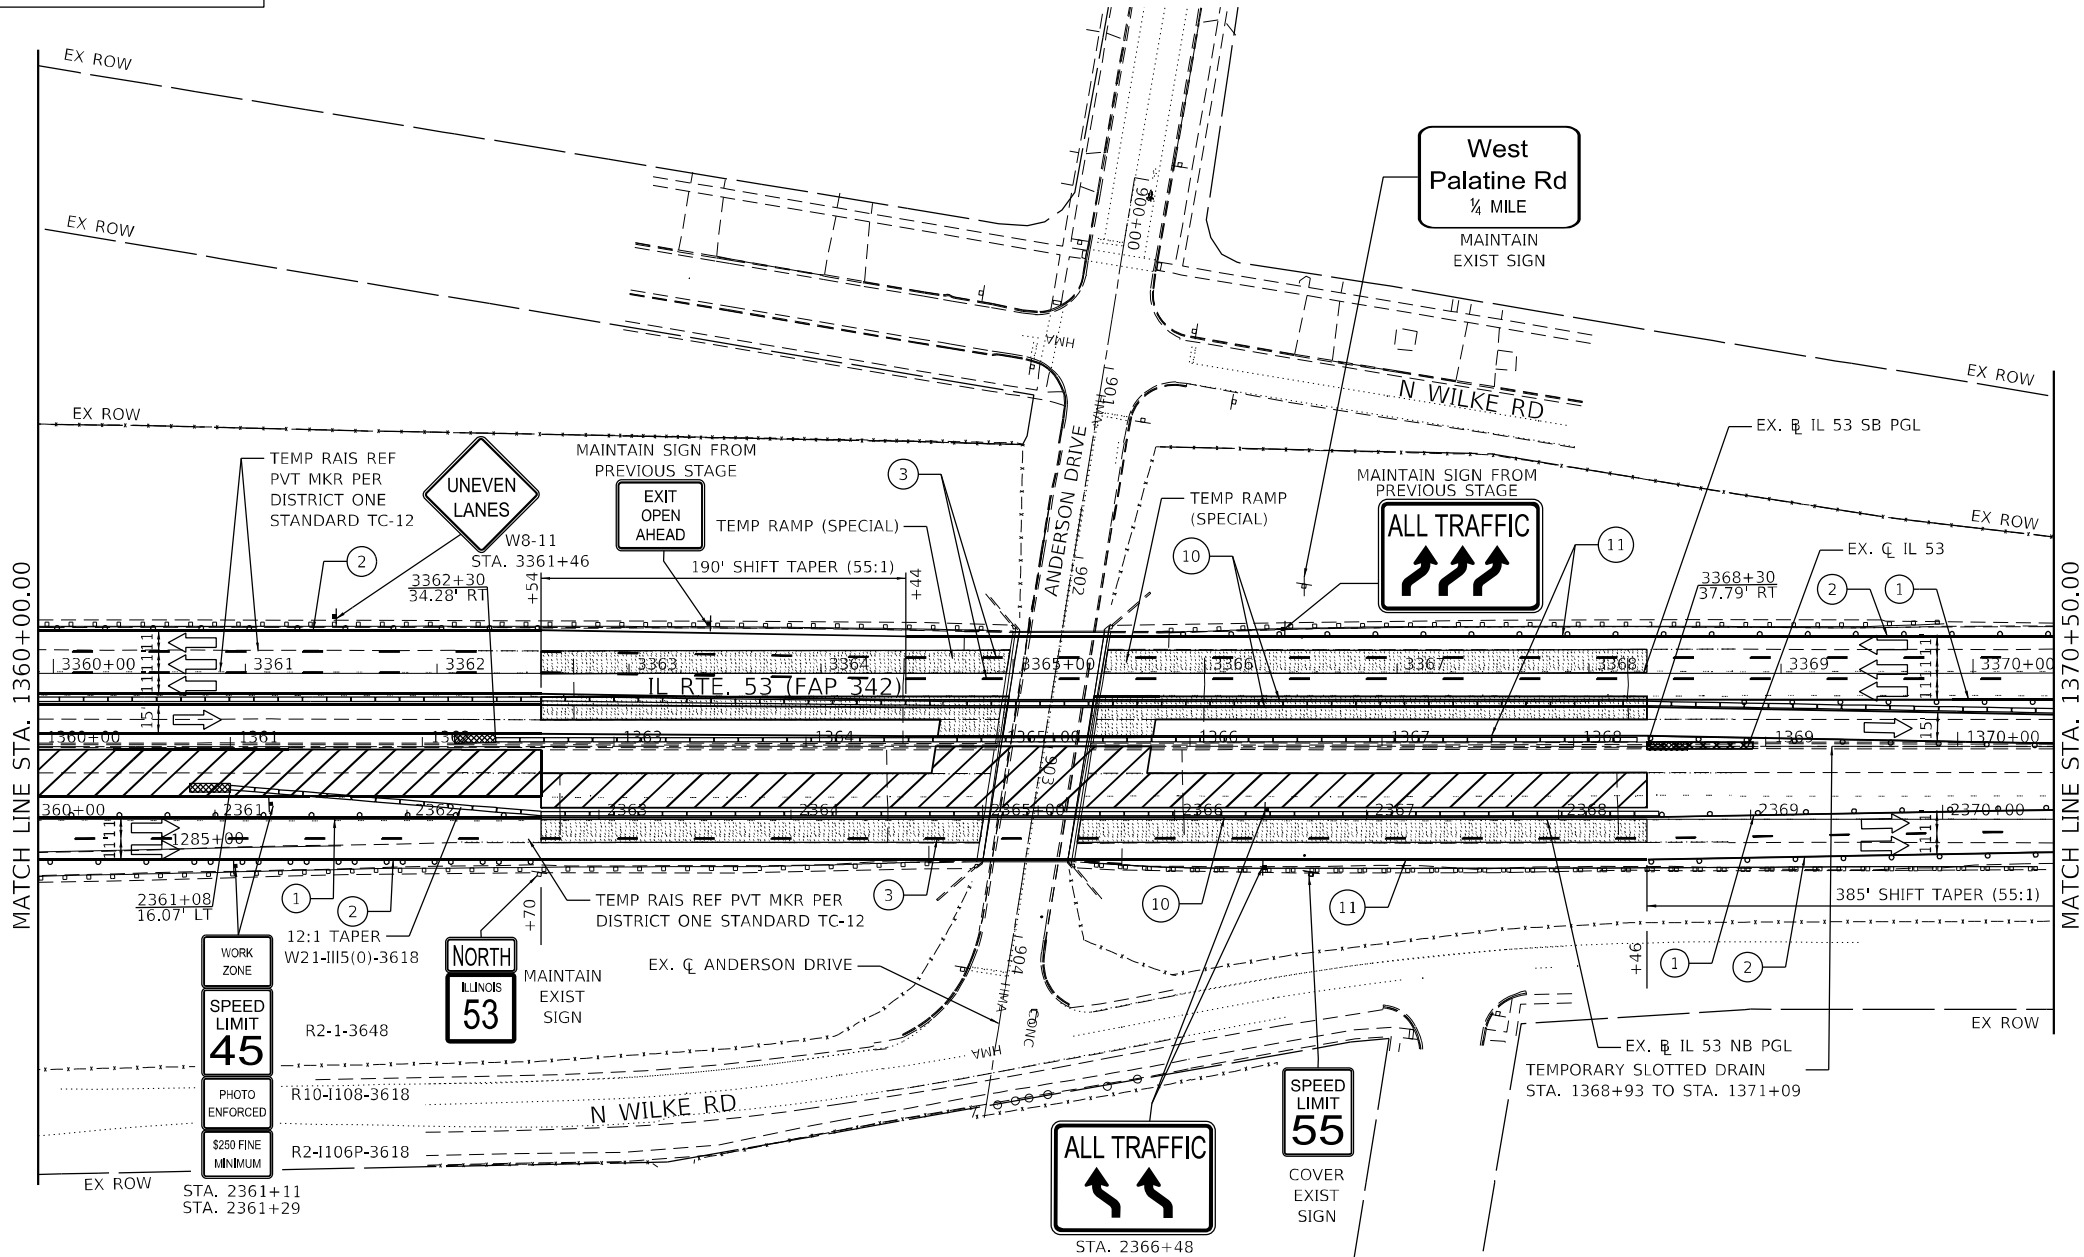

NOTES

1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

LEGEND

- ① TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID YELLOW
② TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE SOLID WHITE
③ TEMPORARY PAVEMENT MARKING - LINE 5" - TYPE IV TAPE WHITE, 10' DASH 30' SKIP
④ TEMPORARY PAVEMENT MARKING - LINE 4" - TYPE IV TAPE WHITE, DOTTED
⑤ TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - TYPE IV TAPE
⑥ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID WHITE
⑦ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE WHITE, DOTTED
⑧ TEMPORARY PAVEMENT MARKING - LINE 8" - TYPE IV TAPE SOLID YELLOW
⑨ TEMPORARY PAVEMENT MARKING - LINE 12" - TYPE IV TAPE WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩ TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID YELLOW
⑪ TEMPORARY PAVEMENT MARKING - LINE 6" - TYPE IV TAPE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
WORK ZONE
TEMPORARY RAMP (SPECIAL)
TEMPORARY PAVEMENT
TEMPORARY PAVEMENT PREVIOUSLY BUILT
TEMPORARY CONCRETE BARRIER
TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
FLASHING ARROW BOARD
TRAFFIC FLOW DIRECTION SIGN
TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS



USER NAME = USTC714594
PLOT SCALE = 100,0000' / in.
PLOT DATE = 9/23/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024

REVISED -
REVISED -
REVISED -
REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53
TRAFFIC CONTROL PLAN - STAGE 2

SCALE: 1" = 50' SHEET 14 OF 17 SHEETS STA. 1360+00.00 TO STA. 1370+00.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	277
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				





- נספח

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION



SCALE: 1" = 50'	SHEET 15 OF 17 SHEETS	STA. 1370+50.00 TO STA. 1378+50.00
-----------------	-----------------------	------------------------------------

ILLINOIS	FED. AID PROJECT
----------	------------------

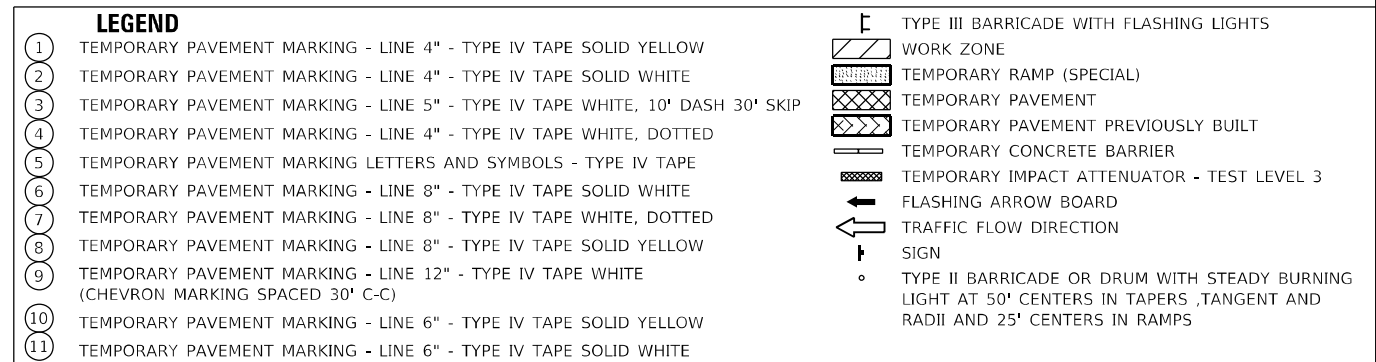



1. ALL SOUTHBOUND TEMPORARY MARKINGS AND SIGNS ALONG MAINLINE AND RAMPS SHALL REMAIN IN PLACE FROM STAGE 1.

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – STAGE 2					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -							342	(531) BR 23	COOK	1211	279
	PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -							CONTRACT NO. 62W38				
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -											
						SCALE: 1" = 50'	SHEET 16 OF 17 SHEETS	STA. 1378+50.00 TO STA. 1391+50.00						

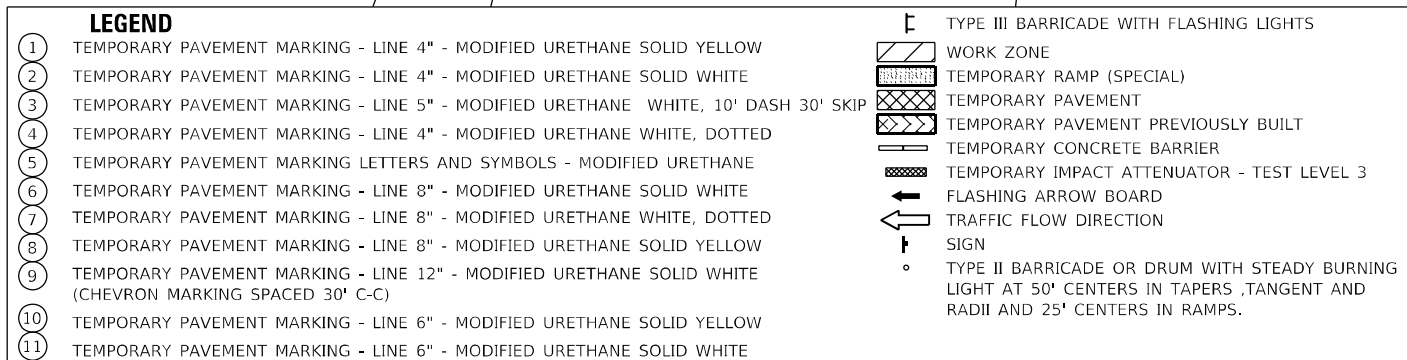

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN				F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -						342	(531) BR 23	COOK	1211	28
	PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -						CONTRACT NO. 62W31				
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 1 OF 16 SHEETS	STA. 1186+00.00 TO STA. 1199+00.00						
									ILLINOIS	FED. AID PROJECT			

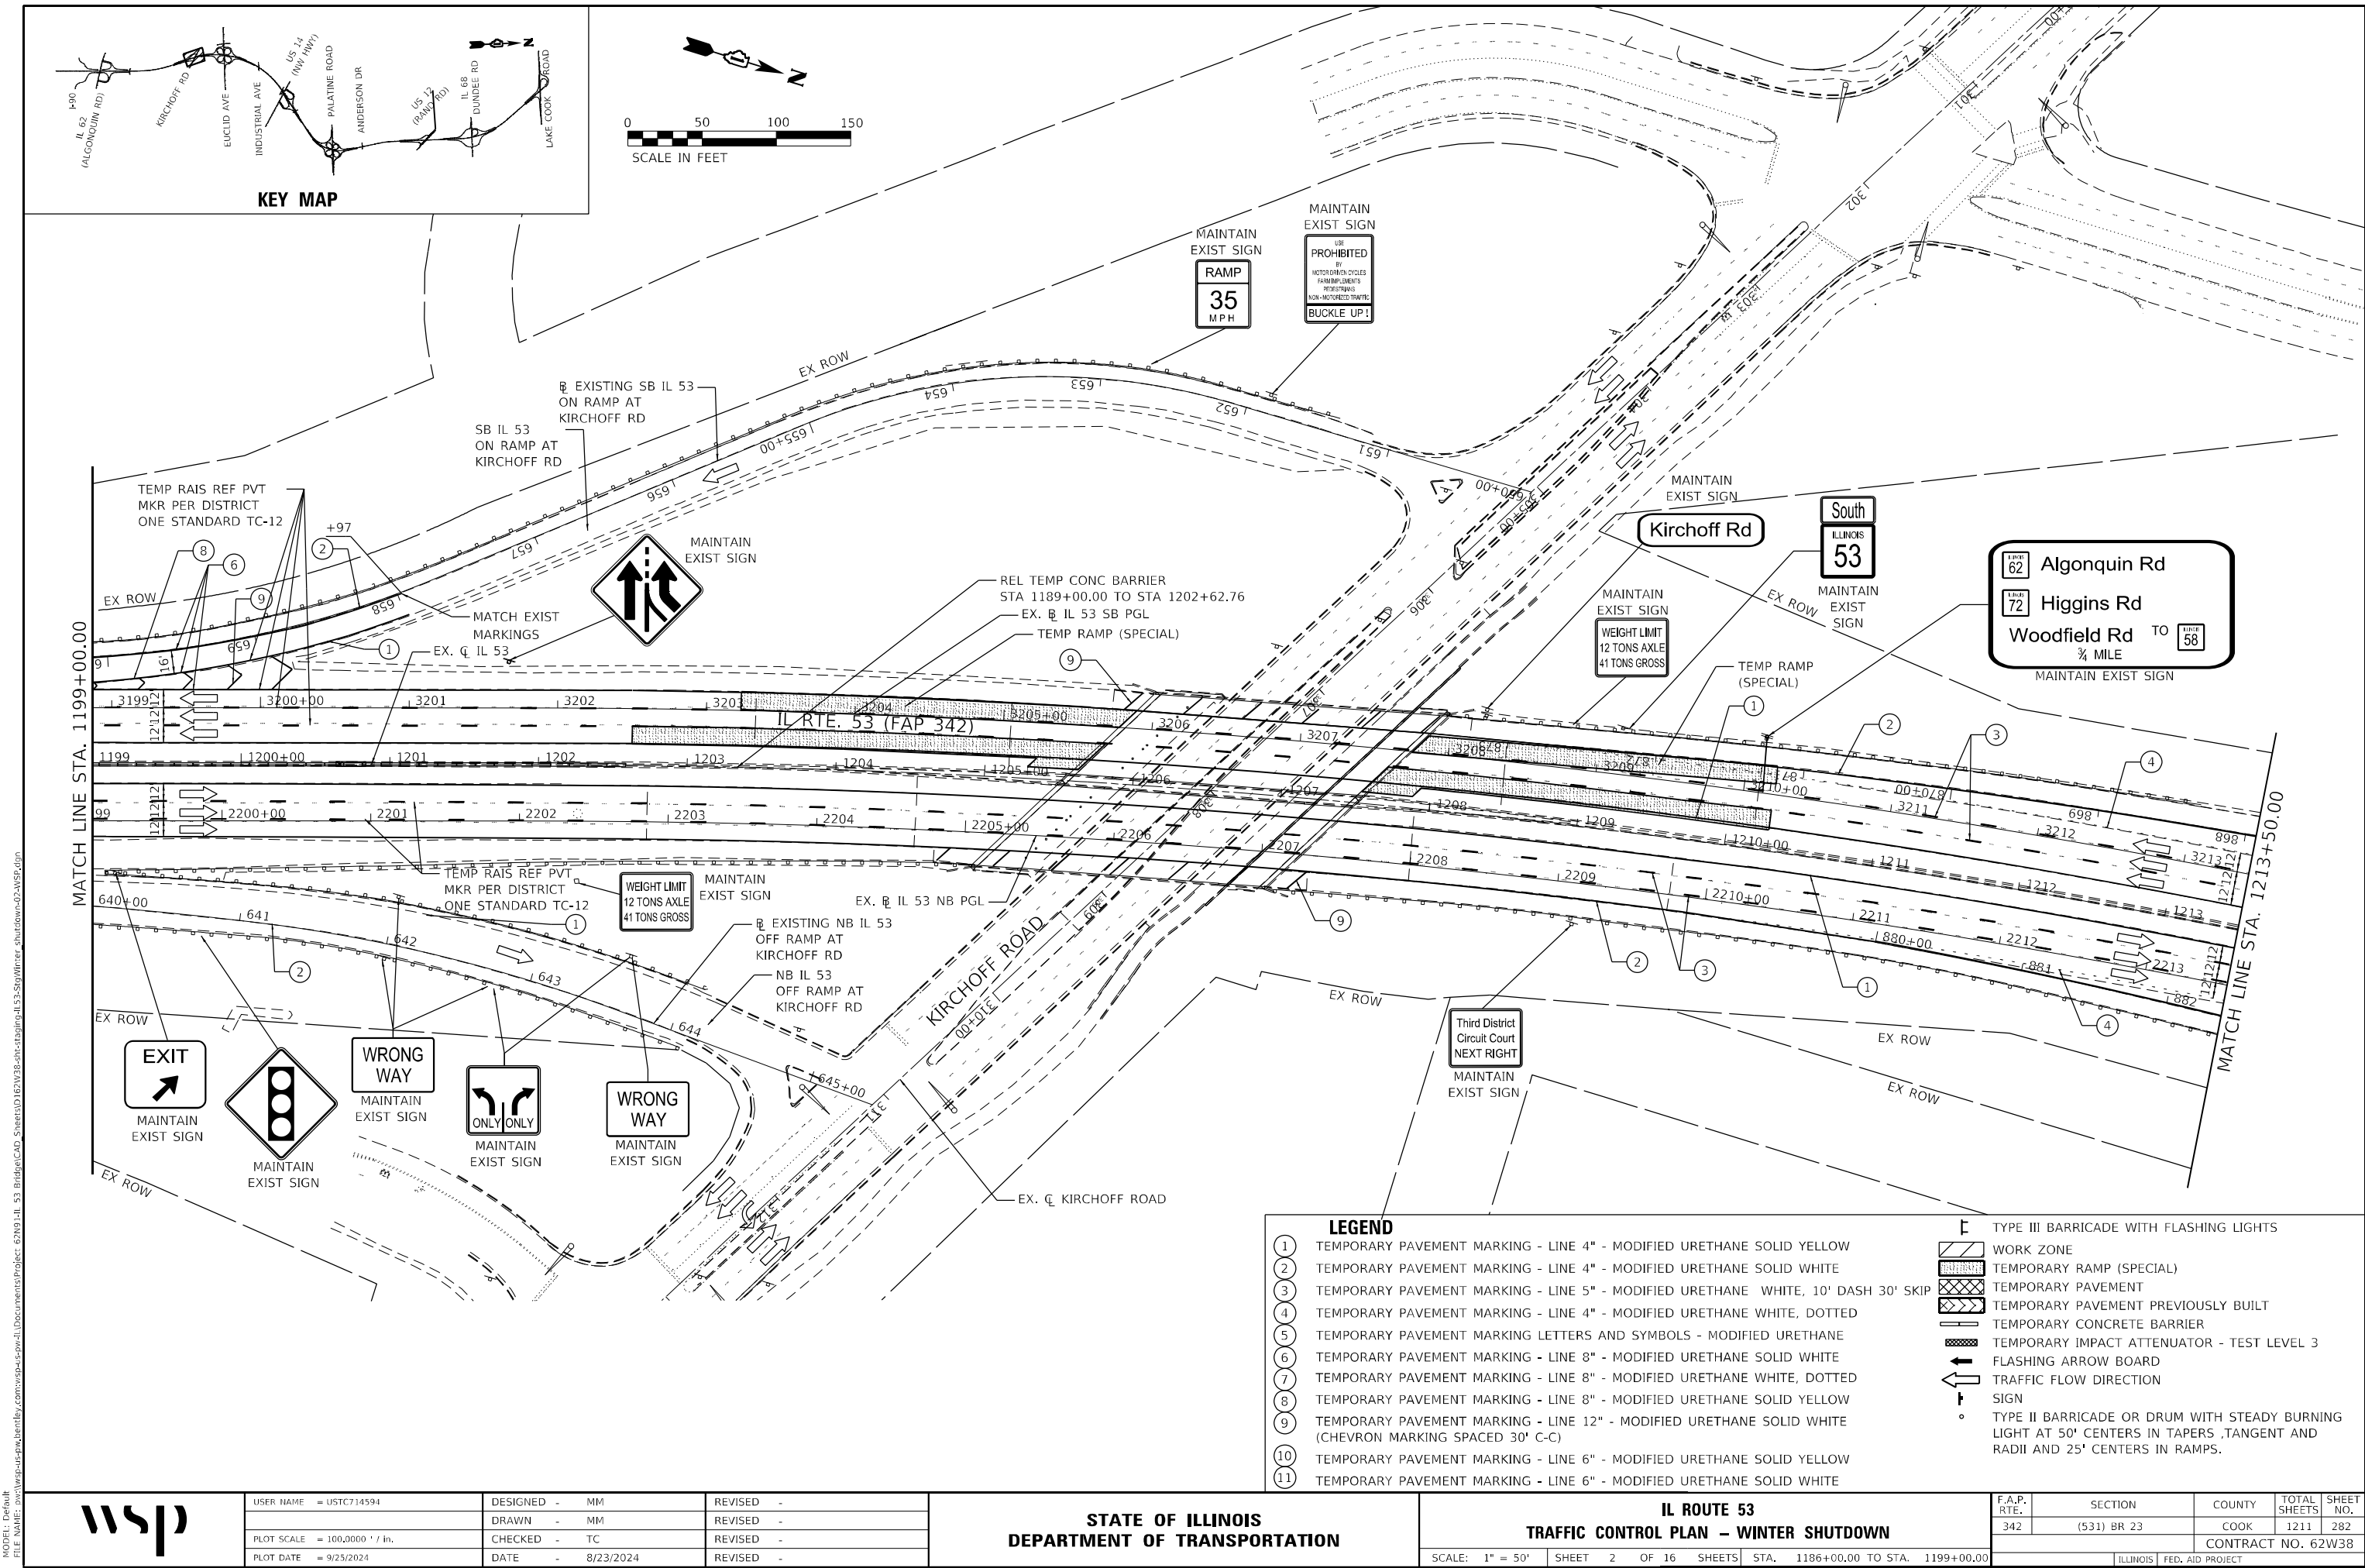

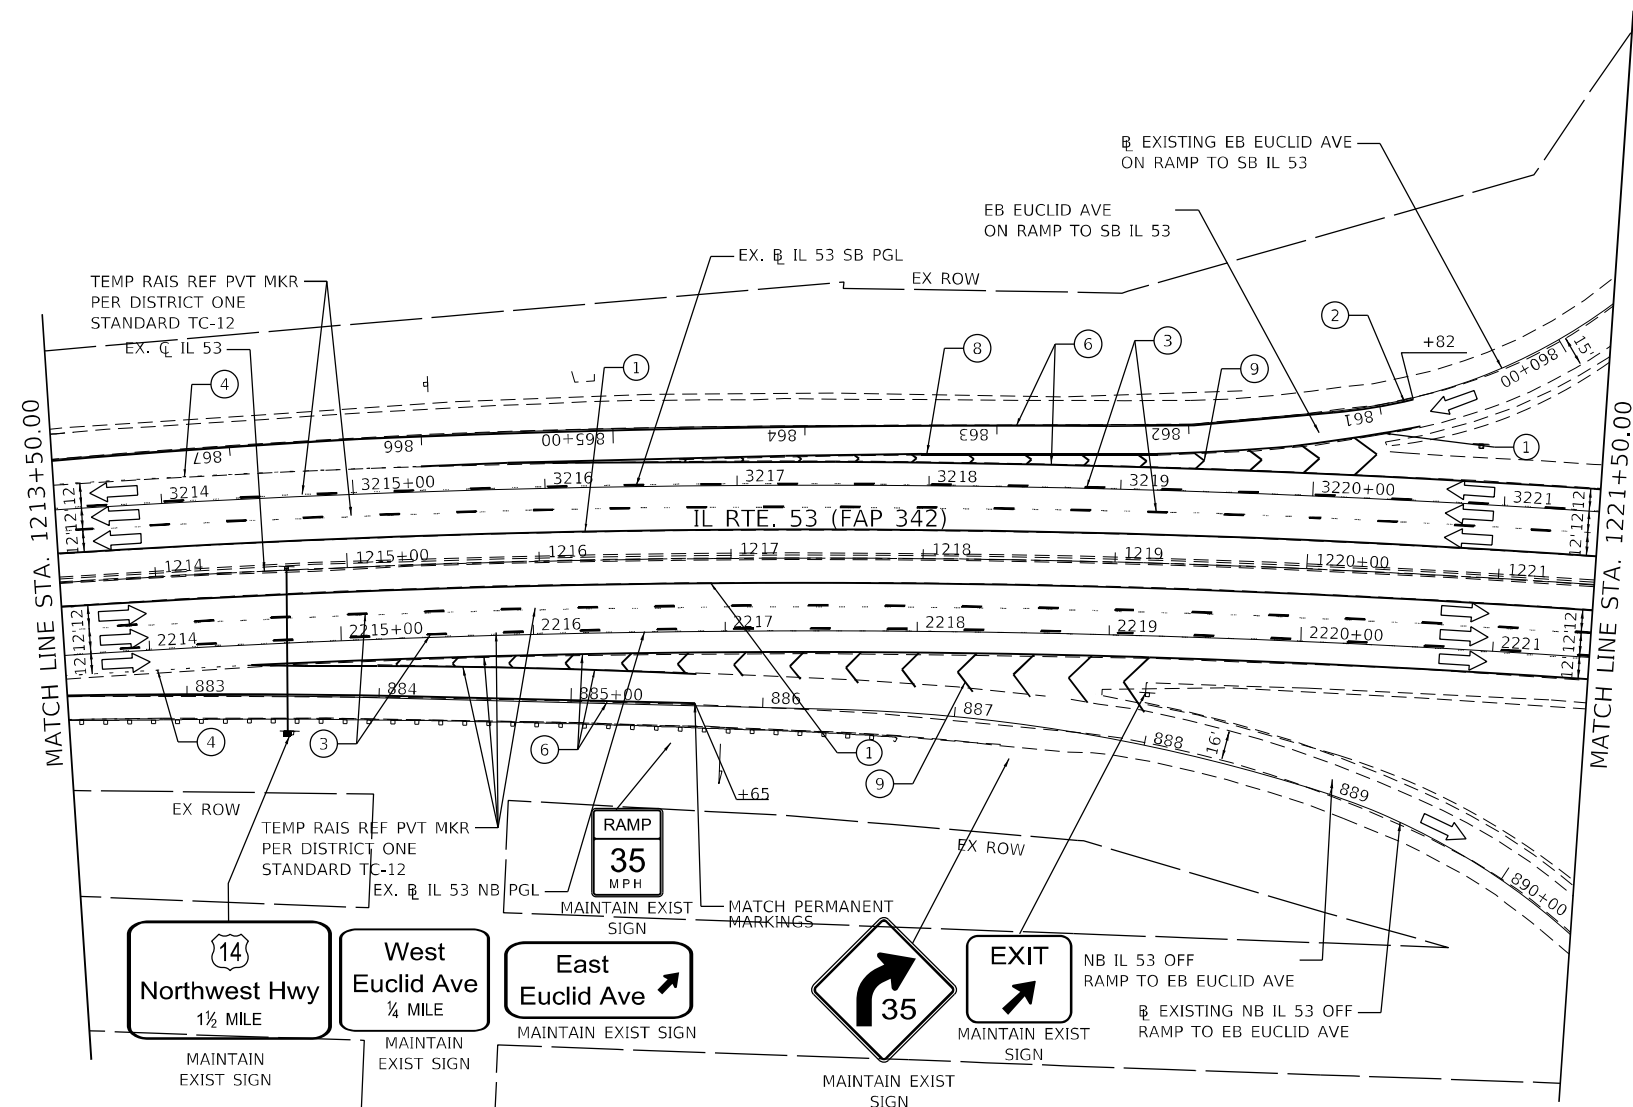

LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE

- | | |
|---|---|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS. |




USER NAME = USTC714594	DESIGNED - MM	REVISED -
	DRAWN - MM	REVISED -
PLOT SCALE = 100,0000 ' / in.	CHECKED - TC	REVISED -
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -

STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION

IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN

SCALE: 1" = 50'	SHEET 3 OF 16 SHEETS	STA. 1213+50.00 TO STA. 1221+50.00
-----------------	----------------------	------------------------------------

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	283
		CONTRACT NO. 62W38		

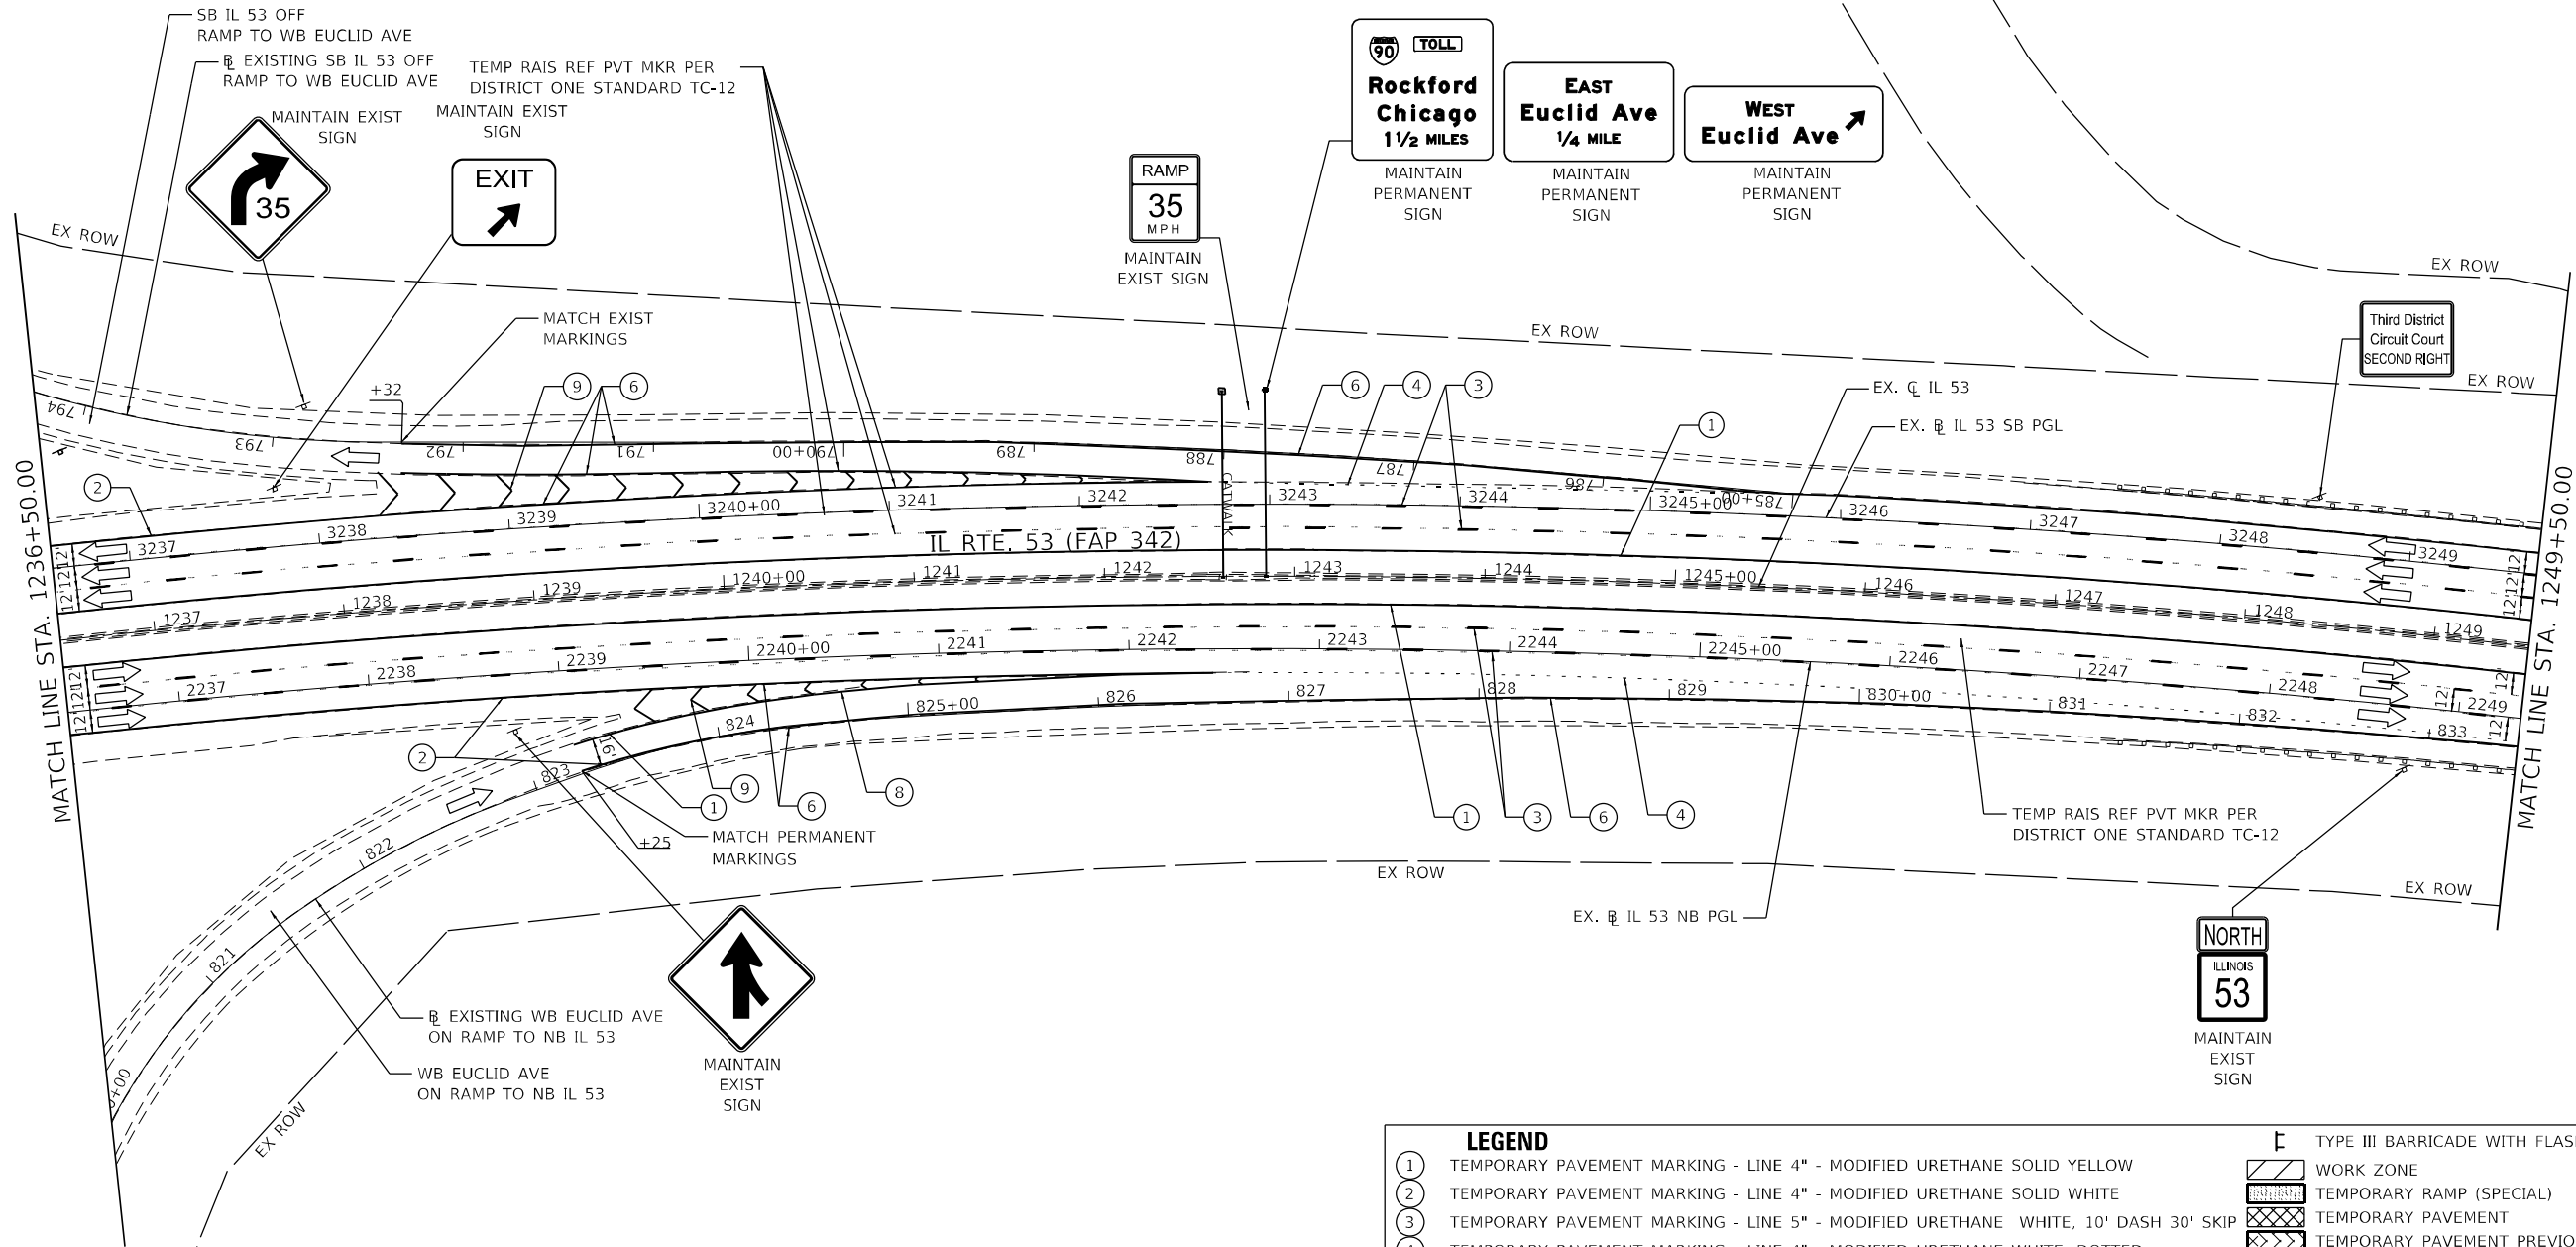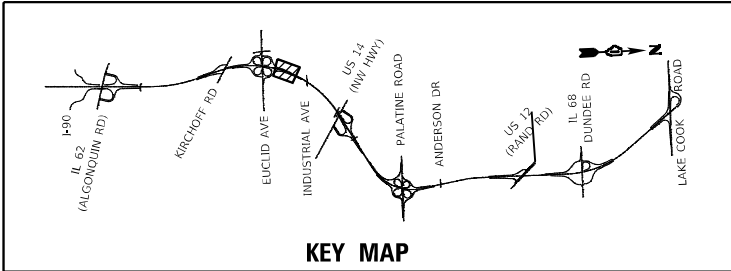

LEGEND

1	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW	11	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE
2	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE		
3	TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP		
4	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED		
5	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE		
6	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE		
7	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED		
8	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW		
9	TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C)		
10	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW		

	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS.



MAINTAIN EXIST SIGN



MAINTAIN	
EXIST SIGN	

LEGEND

- | LEGEND | |
|--------|---|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE
(CHEVRON MARKING SPACED 30' C-C) |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE |

- | | |
|---|--|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
|  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADIAL AND 25' CENTERS IN RAMPS. |



USER NAME	= USTC714594
PLOT SCALE	= 100.0000 ' /
PLOT DATE	= 9/25/2024

DESIGNED	-	MM
DRAWN	-	MM
CHECKED	-	TC
DATE	-	8/23/2024

REVISED	-
REVISED	-
REVISED	-
REVISED	-

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**


IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN

SCALE: 1" = 50'	SHEET 6 OF 16 SHEETS	STA. 1249+50.00 TO STA. 1264+50.00
-----------------	----------------------	------------------------------------



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	286
		CONTRACT NO. 62W38		

MODEL: Default
 FILE F NAME: ou:\wpst-rc\pwbent\flex\com\wpd\cso\j1\Documents\Project_62\04_L11_53_Bridges\CAD_Savers\0162W38\38-sh-station\j1-53-StnWinter_shutdown-06-WSP.dwg

MODEL: Default
FILE: \\wsp-usp4-uspw-bentley.com\usp4-uspw-illinois\Documents\Project: 62W38-01-03 Bridge\CAD Sheets\11-53 Bridge\CAD Sheets\11-53-Stop\Winter_shutdown-07-NSP.dgn





KEY MAP

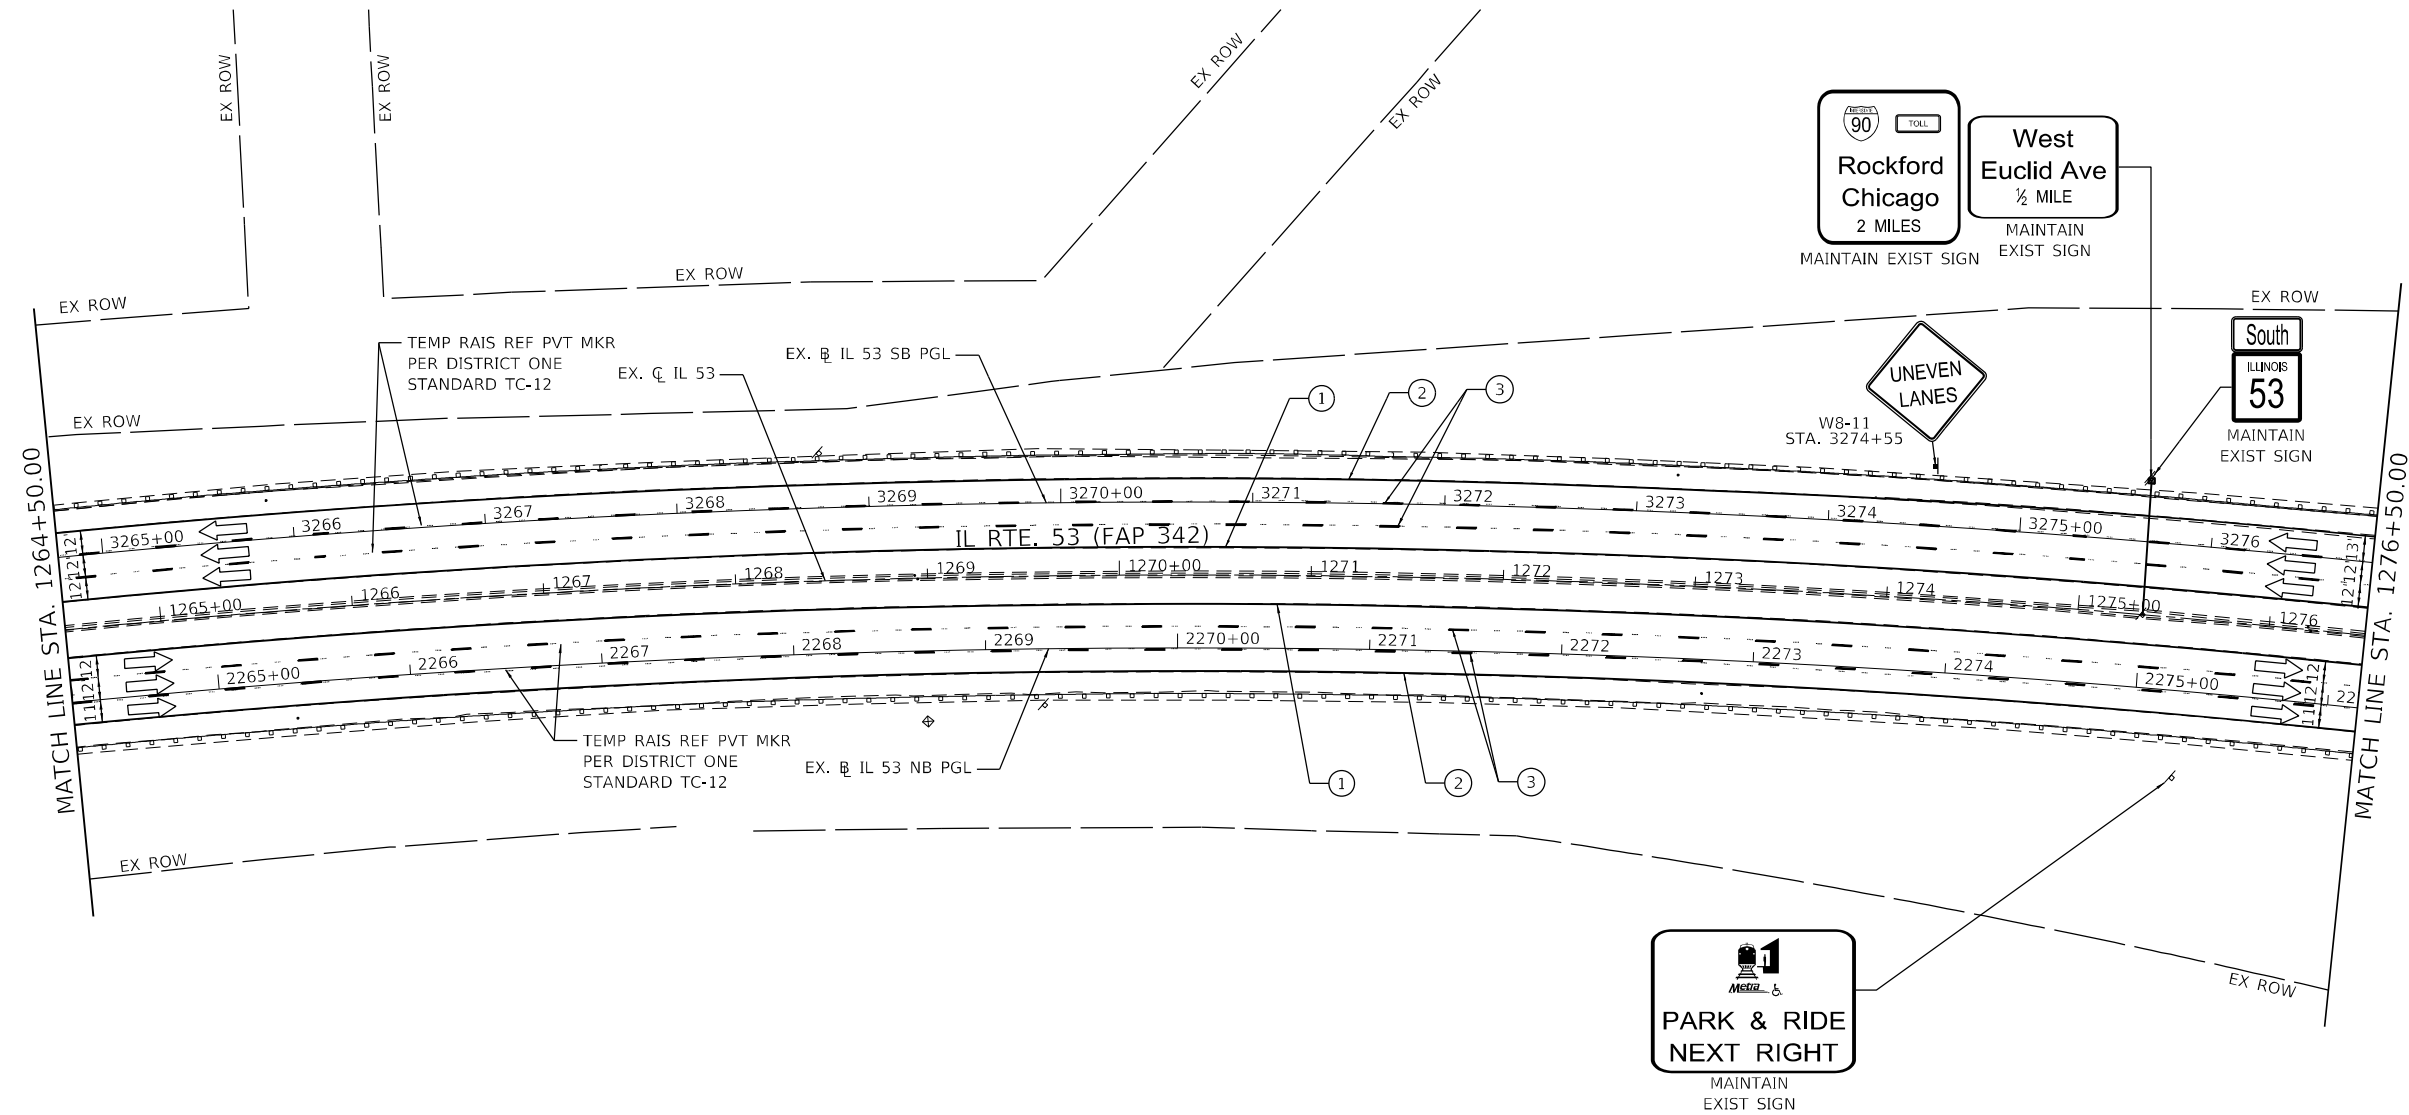

LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE
	TYPE III BARRICADE WITH FLASHING LIGHTS
	WORK ZONE
	TEMPORARY RAMP (SPECIAL)
	TEMPORARY PAVEMENT
	TEMPORARY PAVEMENT PREVIOUSLY BUILT
	TEMPORARY CONCRETE BARRIER
	TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
	FLASHING ARROW BOARD
	TRAFFIC FLOW DIRECTION
	SIGN
	TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS.

	USER NAME = USTC714594			DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - WINTER SHUTDOWN			F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	DRAWN - MM			CHECKED - TC	REVISED -		SCALE: 1" = 50'			342	(531) BR 23	COOK	1211	287
	PLOT SCALE = 100,0000' / in.			DATE - 8/23/2024	REVISED -		SHEET 7 OF 16 SHEETS			CONTRACT NO. 62W38				
	PLOT DATE = 9/23/2024						STA. 1264+50.00 TO STA. 1276+50.00			ILLINOIS FED. AID PROJECT				

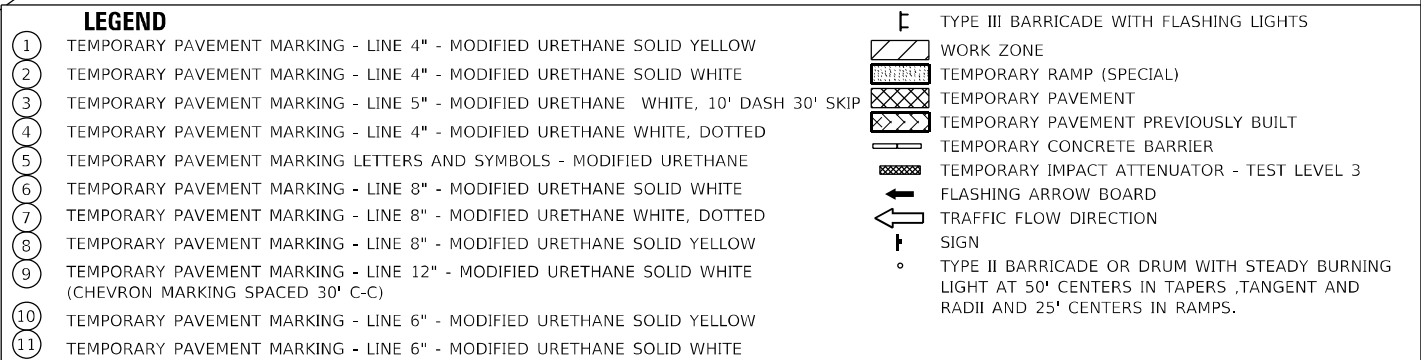

FILE NAME: D:\wsp



	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -			342	(531) BR 23	COOK	1211	289				
	PLOT SCALE = 100,000 ' / in.	CHECKED - TC	REVISED -		CONTRACT NO. 62W38									
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 9 OF 16 SHEETS	STA. 1291+00.00 TO STA. 1306+00.00	ILLINOIS	FED. AID PROJECT					



- | LEGEND | | | |
|--------|--|---|---|
| ① | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW |  | TYPE III BARRICADE WITH FLASHING LIGHTS |
| ② | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE |  | WORK ZONE |
| ③ | TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP |  | TEMPORARY RAMP (SPECIAL) |
| ④ | TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED |  | TEMPORARY PAVEMENT |
| ⑤ | TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE |  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
| ⑥ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE |  | TEMPORARY CONCRETE BARRIER |
| ⑦ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED |  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
| ⑧ | TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW |  | FLASHING ARROW BOARD |
| ⑨ | TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C) |  | TRAFFIC FLOW DIRECTION |
| ⑩ | TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW |  | SIGN |
| ⑪ | TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE |  | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS. |


FILE NAME: 2024

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN					F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -							342	(531) BR 23	COOK	1211	291
	PLOT SCALE = 100,000' / in.	CHECKED - TC	REVISED -		CONTRACT NO. 62W38									
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 11 OF 16 SHEETS	STA. 1321+00.00 TO STA. 1335+50.00	ILLINOIS FED. AID PROJECT						

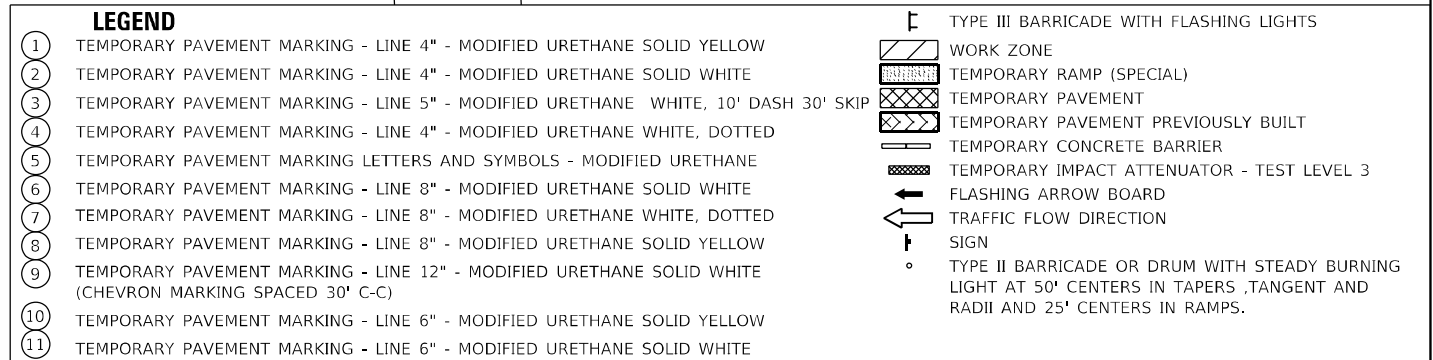

FILE NAME: 

USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN – WINTER SHUTDOWN			F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
	DRAWN - MM	REVISED -					342	(531) BR 23	COOK	1211	293
PLOT SCALE = 100,000' / in.	CHECKED - TC	REVISED -		CONTRACT NO. 62W38							
PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -		SCALE: 1" = 50'	SHEET 13 OF 16 SHEETS	STA. 1350+50.00 TO STA. 1360+00.00	ILLINOIS FED. AID PROJECT				

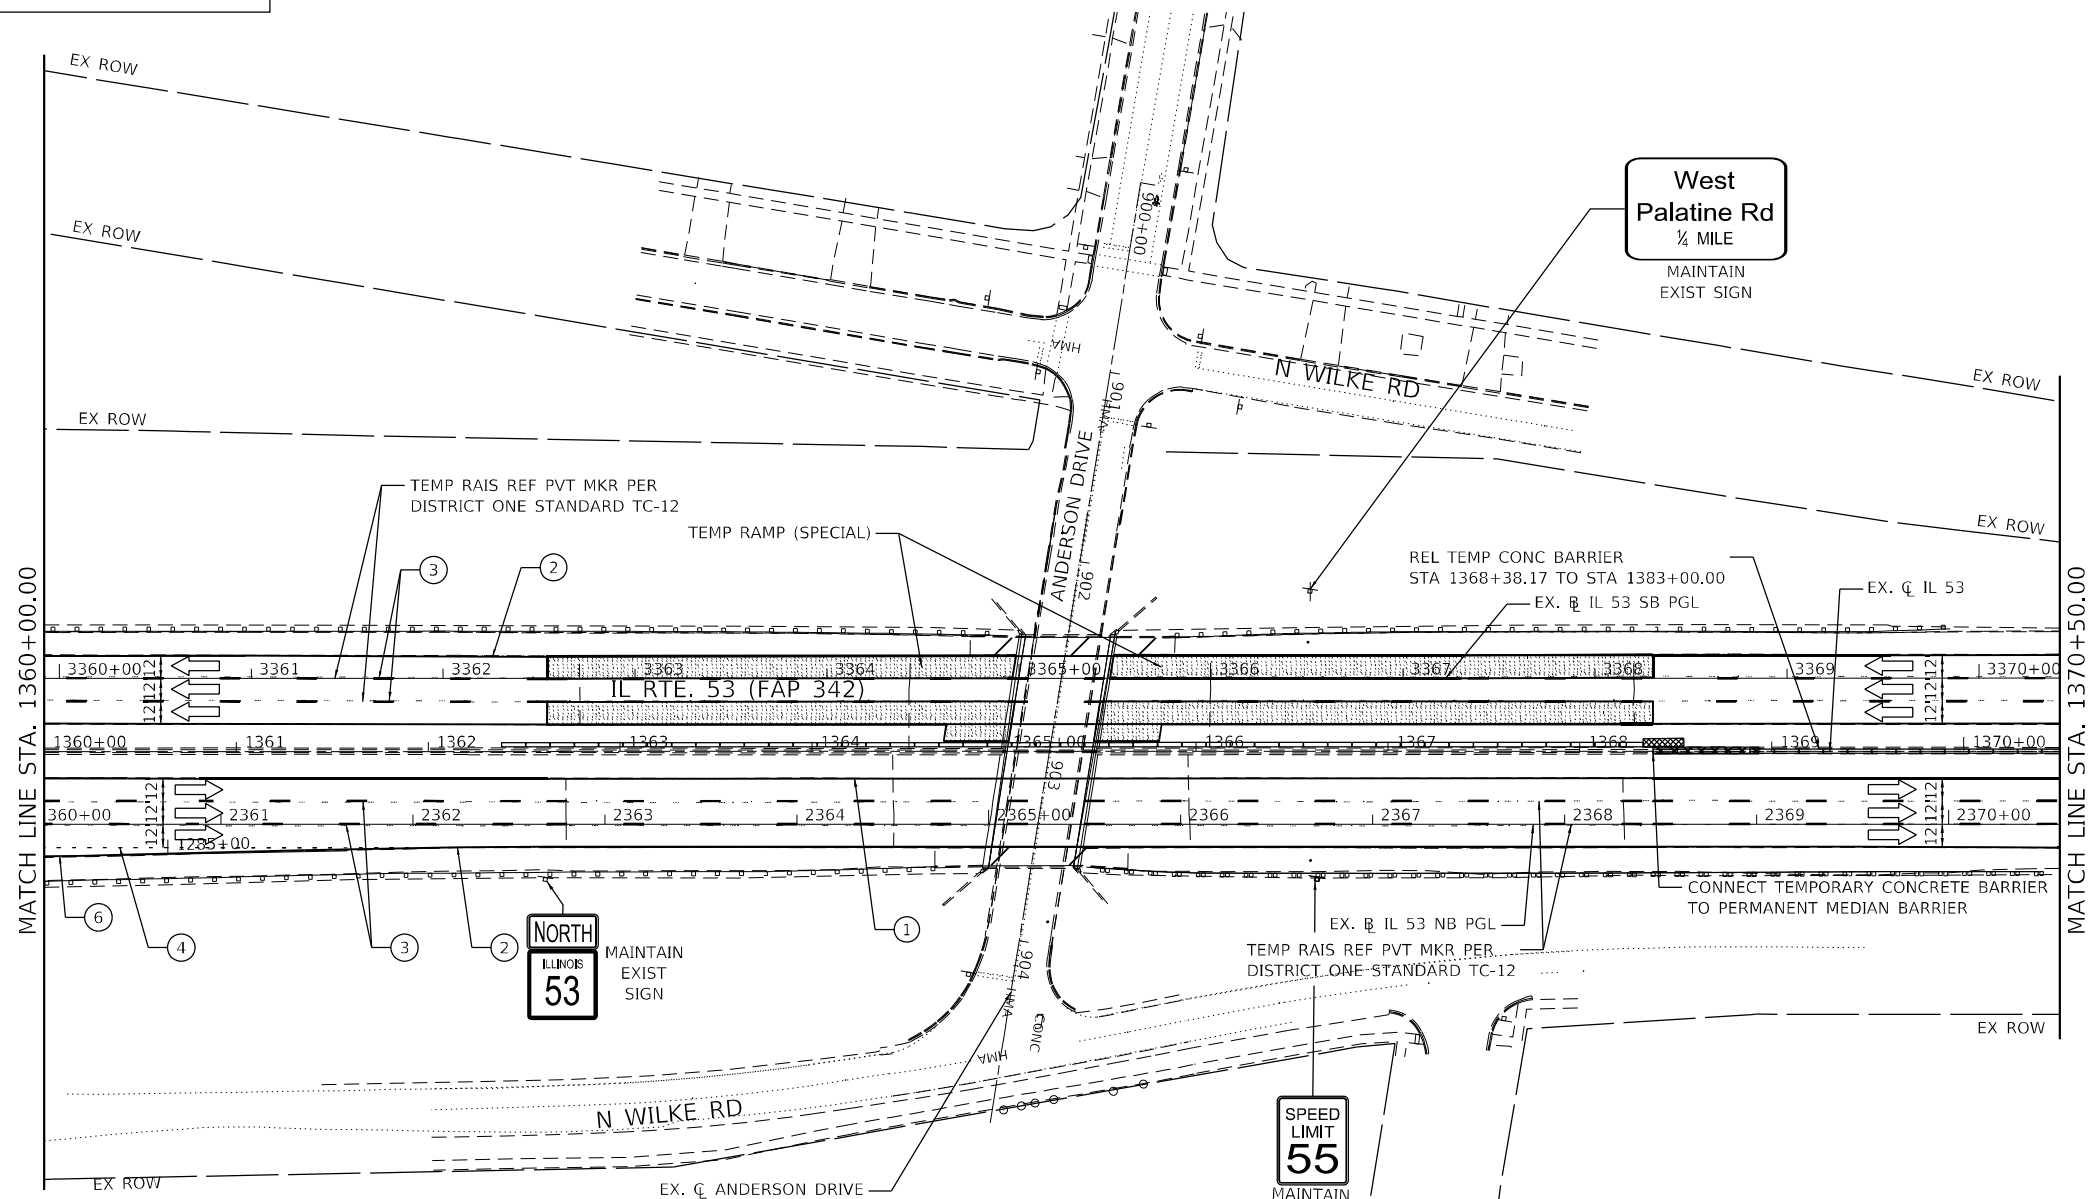

LEGEND	
①	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
②	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
③	TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP
④	TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED
⑤	TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE
⑥	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE
⑦	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED
⑧	TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW
⑨	TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C)
⑩	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW
⑪	TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE

- | | |
|---|---|
|  | TYPE III BARRICADE WITH FLASHING LIGHTS |
|  | WORK ZONE |
|  | TEMPORARY RAMP (SPECIAL) |
|  | TEMPORARY PAVEMENT |
|  | TEMPORARY PAVEMENT PREVIOUSLY BUILT |
|  | TEMPORARY CONCRETE BARRIER |
|  | TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3 |
|  | FLASHING ARROW BOARD |
|  | TRAFFIC FLOW DIRECTION |
|  | SIGN |
| ◦ | TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS. |



USER NAME	= USTC714594
PLOT SCALE	= 100,0000 ' /
PLOT DATE	= 9/25/2024

DESIGNED	-	MM
DRAWN	-	MM
CHECKED	-	TC
DATE	-	8/23/2024

REVISED	-
REVISED	-
REVISED	-
REVISED	-

**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

IL ROUTE 53


TRAFFIC CONTROL PLAN – WINTER SHUTDOWN

SCALE: 1" = 50'	SHEET 14 OF 16 SHEETS	STA. 1360+00.00 TO STA. 1370+00.00
-----------------	-----------------------	------------------------------------



F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	294
		CONTRACT NO. 62W38		
00	ILLINOIS	FED. AID PROJECT		

MODEL: Default
FILE NAME: pw:\wsp-us-pw.bentley.com:wsp-us-pw-ll\Documents\Project_62N9-IL_53 Bridge\CAD Sheets\0162W38-sht-staging-IL-53-SigWriter_shutdown-1A-WSP.dgn

MODEL: Default
FILE: \\nautilus-pw-bentley.com\usps4-cpw-ill\Documents\Project_62W38-2ht-ctb\figs-IL53-Stop\Winter_shutdown-15.WSP.dgn



KEY MAP

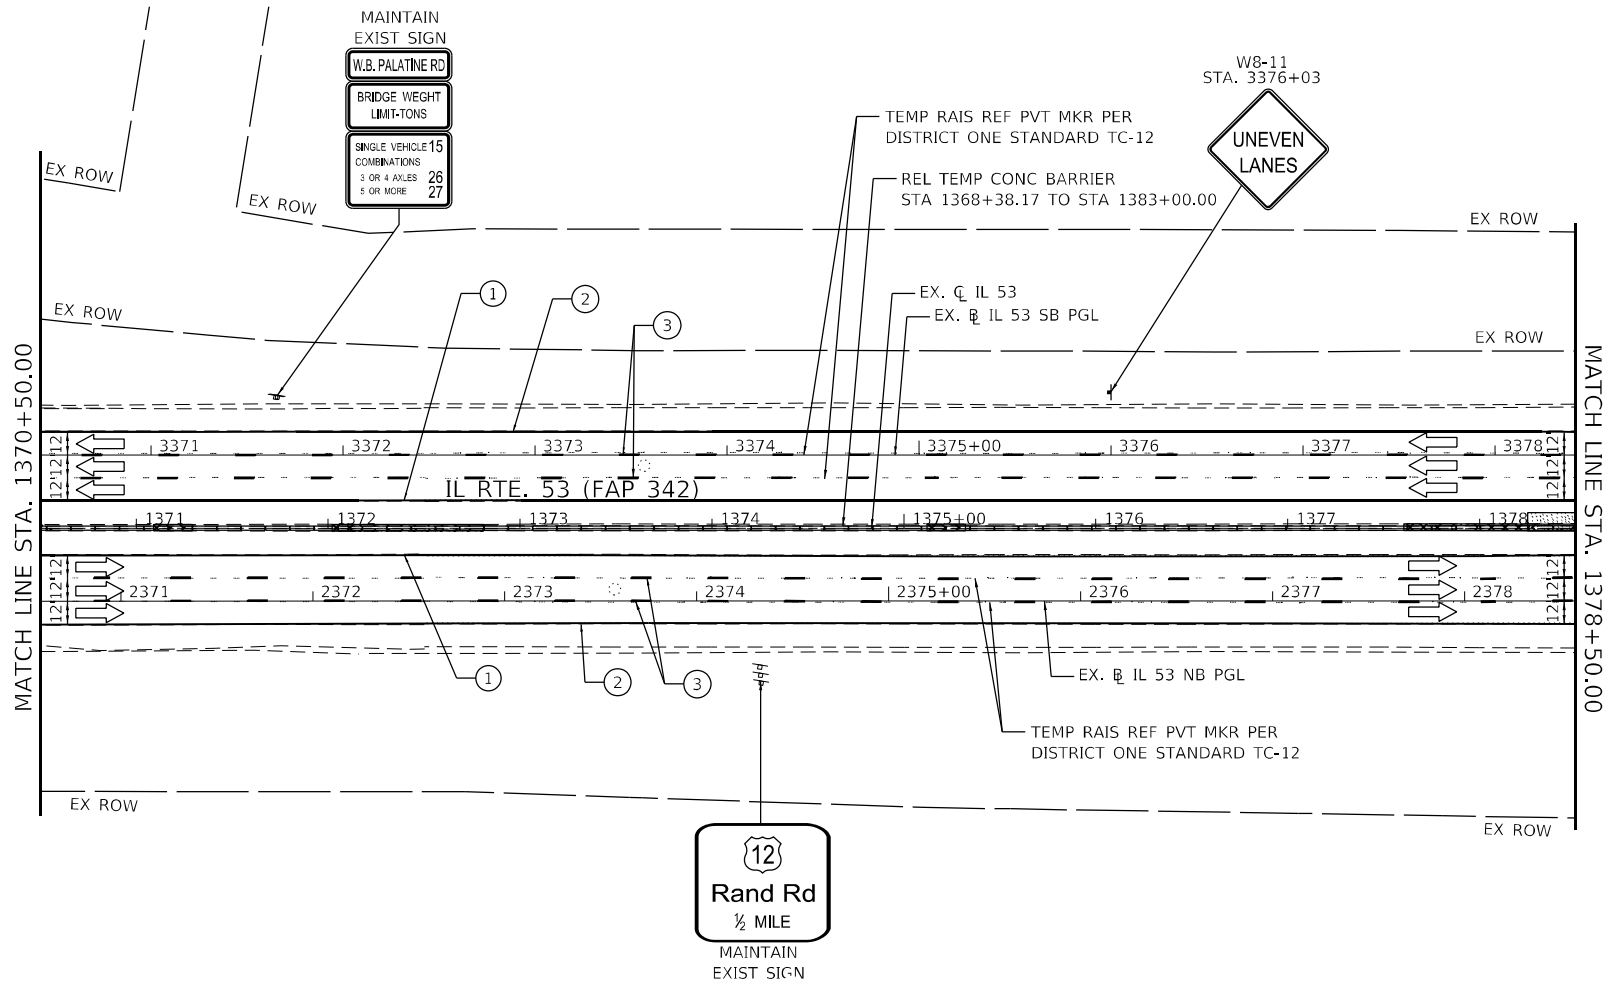

LEGEND

- ① TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID YELLOW
- ② TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE SOLID WHITE
- ③ TEMPORARY PAVEMENT MARKING - LINE 5" - MODIFIED URETHANE WHITE, 10' DASH 30' SKIP
- ④ TEMPORARY PAVEMENT MARKING - LINE 4" - MODIFIED URETHANE WHITE, DOTTED
- ⑤ TEMPORARY PAVEMENT MARKING LETTERS AND SYMBOLS - MODIFIED URETHANE
- ⑥ TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID WHITE
- ⑦ TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE WHITE, DOTTED
- ⑧ TEMPORARY PAVEMENT MARKING - LINE 8" - MODIFIED URETHANE SOLID YELLOW
- ⑨ TEMPORARY PAVEMENT MARKING - LINE 12" - MODIFIED URETHANE SOLID WHITE (CHEVRON MARKING SPACED 30' C-C)
- ⑩ TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID YELLOW
- ⑪ TEMPORARY PAVEMENT MARKING - LINE 6" - MODIFIED URETHANE SOLID WHITE

- TYPE III BARRICADE WITH FLASHING LIGHTS
- WORK ZONE
- TEMPORARY RAMP (SPECIAL)
- TEMPORARY PAVEMENT
- TEMPORARY PAVEMENT PREVIOUSLY BUILT
- TEMPORARY CONCRETE BARRIER
- TEMPORARY IMPACT ATTENUATOR - TEST LEVEL 3
- FLASHING ARROW BOARD
- TRAFFIC FLOW DIRECTION
- SIGN
- TYPE II BARRICADE OR DRUM WITH STEADY BURNING LIGHT AT 50' CENTERS IN TAPERS, TANGENT AND RADII AND 25' CENTERS IN RAMPS.



USER NAME = USTC714594
PLOT SCALE = 100,0000 ' / in.
PLOT DATE = 9/23/2024

DESIGNED - MM
DRAWN - MM
CHECKED - TC
DATE - 8/23/2024



REVISED -
REVISED -
REVISED -
REVISED -



**STATE OF ILLINOIS
DEPARTMENT OF TRANSPORTATION**

**IL ROUTE 53
TRAFFIC CONTROL PLAN - WINTER SHUTDOWN**

SCALE: 1" = 50' SHEET 15 OF 16 SHEETS STA. 1370+50.00 TO STA. 1378+50.00

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
342	(531) BR 23	COOK	1211	295
CONTRACT NO. 62W38				
ILLINOIS FED. AID PROJECT				

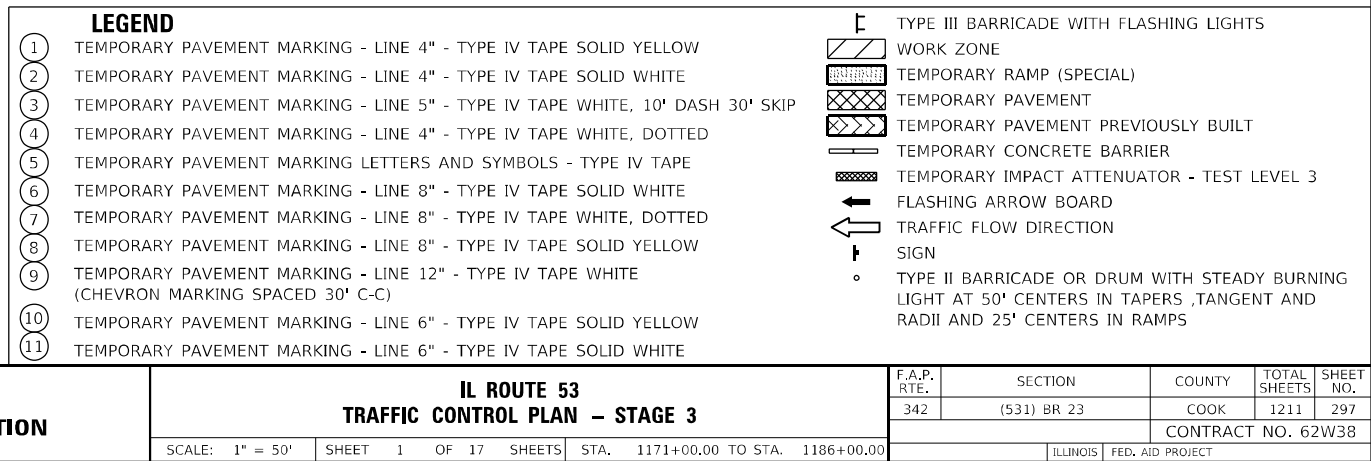

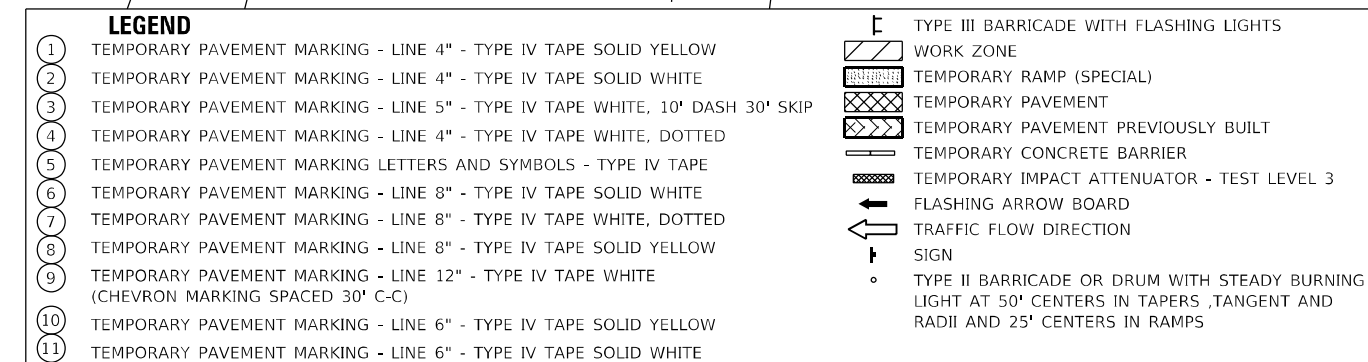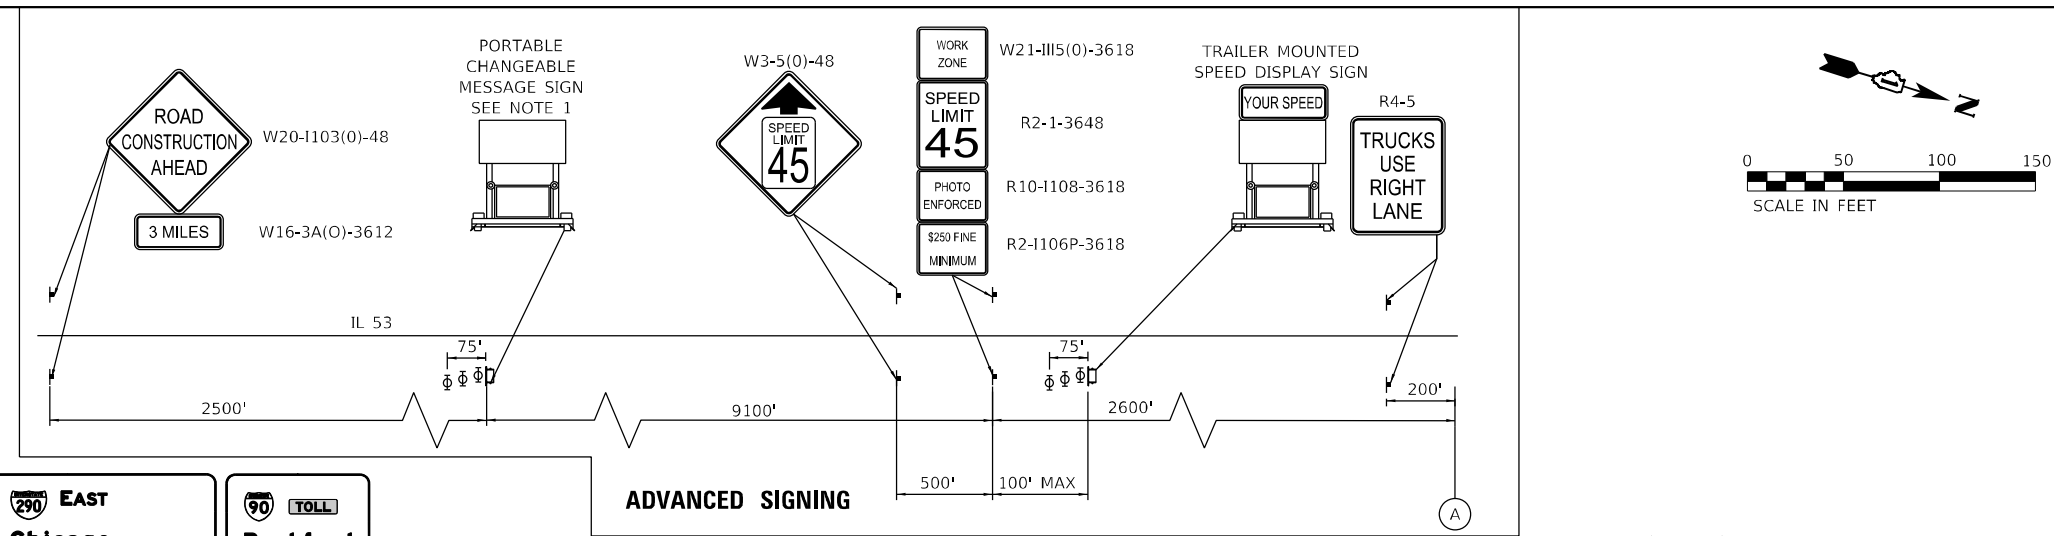

1. PORTABLE CHANGEABLE MESSAGE SIGN WORDING WILL BE DETERMINED BY THE ENGINEER.

	USER NAME = USTC714594	DESIGNED - MM	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	IL ROUTE 53 TRAFFIC CONTROL PLAN - STAGE 3			F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN - MM	REVISED -					342	(531) BR 23	COOK	1211	298
	PLOT SCALE = 100,000' / in.	CHECKED - TC	REVISED -					CONTRACT NO. 62W38				
	PLOT DATE = 9/25/2024	DATE - 8/23/2024	REVISED -					SCALE: 1" = 50'	SHEET 2 OF 17 SHEETS	STA. 1186+00.00 TO STA. 1199+00.00	ILLINOIS FED. AID PROJECT	

