

BENCH MARKS

BM DA 1114:
 FOUND CHISELED '□' IN TOP OF EXPOSED REBAR NEAR CENTER OF CONCRETE HEADWALL ON SOUTH SIDE OF US 136, 0.50 MILES EAST OF T.R. 2930E.
 APPROXIMATE STA. 158+20
 ELEVATION: 504.183 FT



BM DA 1116A (RESET):
 SET 60D NAIL IN POWER POLE ON THE NORTH SIDE OF US 136, 1.0 MILES EAST OF T.R. 2930E.
 STA. 184+99.4, 38.6' LT
 ELEVATION: 504.183 FT

BM TA - 11:
 FOUND CHISELED '□' IN SOUTH EDGE OF GRAIN BIN CONCRETE FOUNDATION ON THE NORTH SIDE OF US 136, 0.41 MILES WEST OF T.R. 3100E.
 STA. 202+57.6, 58.0' LT
 ELEVATION: 523.088 FT

BM DA 1121:
 FOUND CHISELED '□' ON EAST END OF CONCRETE HEADWALL ON SOUTH SIDE OF US 136, 0.52 MILES EAST OF T.R. 3100E.
 STA. 251+77.7, 23.4' RT.
 ELEVATION: 505.917 FT.

BM 102:
 FOUND CHISELED '□' SET IN NORTHWEST ABUTMENT OF BRIDGE #063-3601 AT ALLENS GROVE DITCH, LOCATED ON T.R. 3300E, SOUTH SIDE OF US136.
 STA. 330+89.7, 54.8' RT.
 ELEVATION: 511.462 FT.

BM DA 1123:
 FOUND 60D NAIL IN POWER POLE, 139 FT EAST OF T.R. 3200E ON NORTH SIDE OF US 136.
 STA. 279+10.4, 39.3' LT.
 ELEVATION: 521.901 FT.

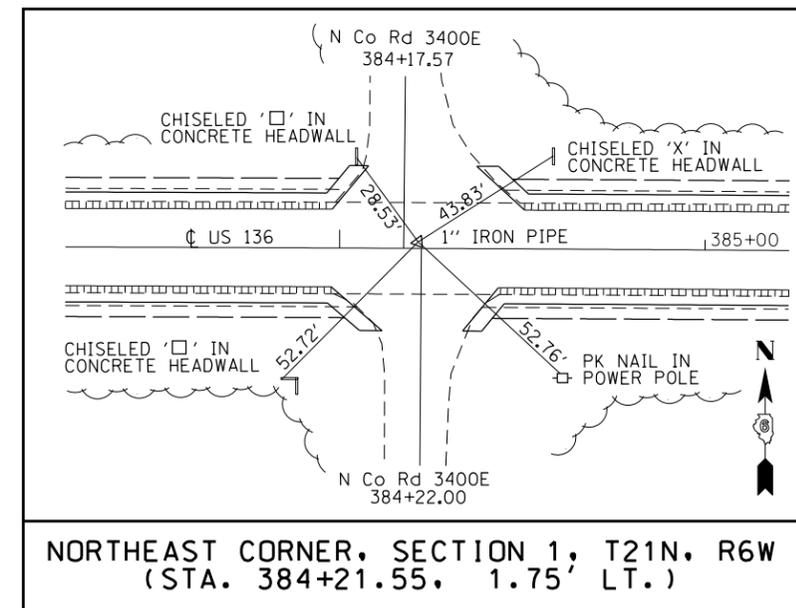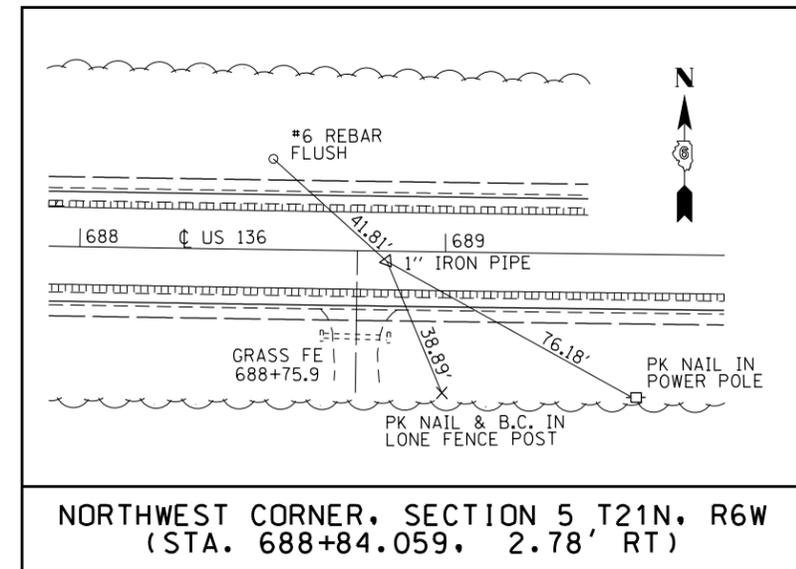

**PLACEMENT FOR PROPOSED PERMANENT
 SURVEY MARKERS, TYPE 1 (#66700205)
 (REMOVE & REPLACE EXISTING 1" IRON PIPES WITH
 PROPOSED PERMANENT SURVEY MARKERS)**

FILE NAME =	USER NAME = sparksgw	DESIGNED -	RTS	REVISED -	
ct:\pw\work\p\dot\sparksgw\0219881\0672093-sht-ATB.dgn		DRAWN -	RTS	REVISED -	
	PLOT SCALE = 100.0000' / 1" =	CHECKED -		REVISED -	
	PLOT DATE = Apr-18-2014 02:00:33PM	DATE -	04-01-14	REVISED -	

**STATE OF ILLINOIS
 DEPARTMENT OF TRANSPORTATION**

BENCH MARKS, SURVEY MARKERS

SCALE: SHEET 1 OF 1 SHEETS STA. TO STA.

F.A.P. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
315	(123) I-1	MASON	64	12
CONTRACT NO. 72C93			ILLINOIS FED. AID PROJECT	
