CONTRACT NO. 76A72

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
70	82-(1,2,3,4)RS-1	ST CLAIR	43	40
STA.	TO STA.			
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

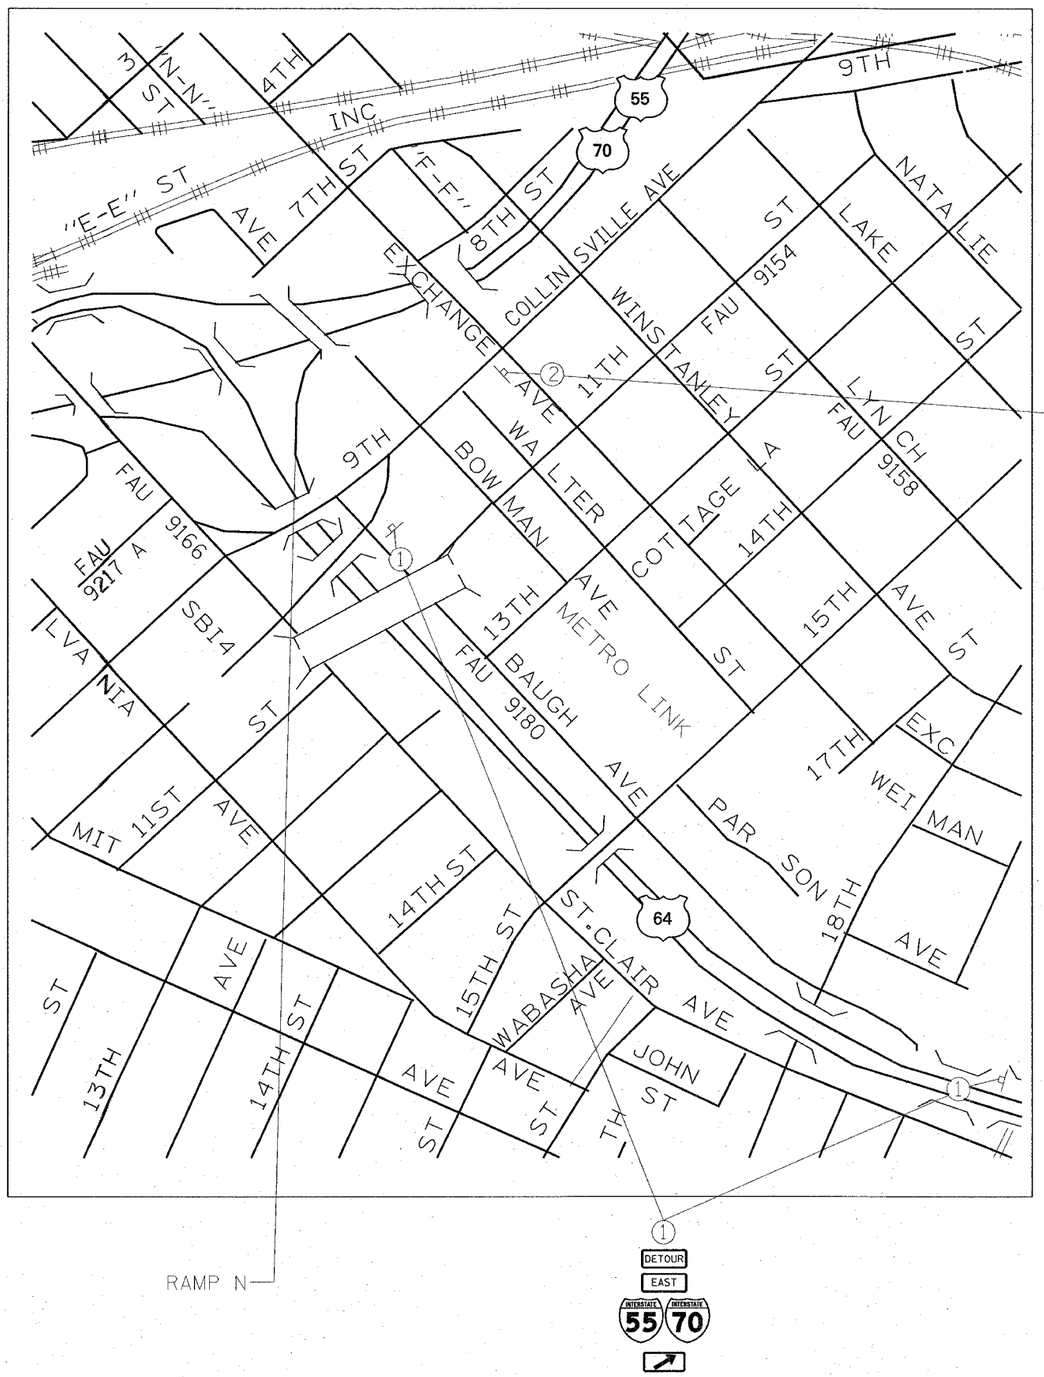

RAMP N DETOUR ROUTE

1. WEST BOUND 64 TO BAUGH AVE
2. BAUGH AVE TO 9TH ST
3. 9TH ST TO COLLINSVILLE AVE
4. COLLINSVILLE AVE TO EXCHANGE AVE
5. EXCHANGE AVE TO EAST BOUND 55/70

NOTES:

1. CONTRACTOR SHALL SUPPLY ALL DETOUR SIGNS.
2. ALL SIGNS SHALL HAVE REFLECTORIZED BACKGROUND.
3. ONE CHANGEABLE MESSAGE BOARD SHALL BE PLACED AT THE CLOSURE FOR NOTIFICATION. ONE CHANGEABLE MESSAGE SIGN SHALL BE PLACED AT THE LOCATION OF THE NEXT EXPECTED CLOSURE FOR ADVANCE NOTIFICATION. THE EXACT LOACTIONS WILL BE DETERMINED BY THE ENGINEER
4. CONTRACTOR WILL FURNISH THE POSTS AND ERECT THE SIGNS AT THE LOCATIONS SHOWN ON THIS SHEET, AS DIRECTED BY THE RESIDENT ENGINEER/TECHNICIAN.
5. UPON COMPLETION OF THE CLOSURE, THE CONTRACTOR SHALL REMOVE THE SIGNS AND POSTS. THE SIGNS AND POSTS WILL REMAIN THE PROPERTY OF THE CONTRACTOR.
6. DURING THE CLOSURE, TYPE 3 BARRICADES WITH ROAD CLOSED SIGNS ATTACHED SHALL SHUT-OFF ACCESS. TRAFFIC CONES SHALL ALSO BE PLACED TO DELINEATE ROAD CLOSURE, AT THE DIRECTION OF THE ENGINEER.
7. THE ABOVE NOTED WORK SHALL BE INCLUDED IN THE CONTRACT UNIT PRICE LUMP SUM FOR TRAFFIC CONTROL AND PROTECTION (SPECIAL) AND NO OTHER COMPENSATION WILL BE ALLOWED.

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

TRAFFIC CONTROL AND PROTECTION (SPECIAL)

RAMP N CLOSURE

FAI 55/70/64

SECTION 82-(1,2,3,4)RS-1

ST CLAIR COUNTY

SCALE: VERT. HORIZ.

DATE

DRAWN BY

CHECKED BY

PLOT DATE = 2/15/2007
FILE NAME = c:\pwworking\dot84\ed84307\plan\plnb84307bcdgn
PLOT SCALE = 50.0000 ' / IN.
REFERENCE = REF
