| F.A.I. RTE. | SECTION | COUNTY | TOTAL SHEETS | SHEET NO. |
|---|---|---|---|---|
| 90/94 | 2004-067L | COOK | 35 | 7 |
| STA. | | TO STA. | | |
| FED. ROAD DIST. NO. 1 | ILLINOIS | FED. AID PROJECT | | |

62806

| ACTIVITY ID | ACTIVITY DESCRIPTION | EARLY START | EARLY FINISH | ORIG DUR |
|---|---|---|---|---|
| **CONTRACT 9C8 (62840) - 63RD STREET TRAFFIC SIGNALS** | | | | |
| 63RD STREET & WENTWORTH AVENUE | | | | |
| 1 | INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS | 02-May-05 | 23-Nov-05 | |
| 63RD STREET & WELLS STREET | | | | |
| 1 | INSTALL AND MAINTAIN TEMPORARY TRAFFIC SIGNALS, REMOVE EXISTING AND INSTALL NEW LIGHTING AND TRAFFIC SIGNALS | 02-May-05 | 11-Nov-05 | |
| **CONTRACT 9C11 (62841) - SEWER TELEVISING** | | | | |
| WENTWORTH AVENUE | | | | |
| 1 | TELEVISE EXISTING SEWER | 02-May-05 | 13-May-05 | |
| 2 | TELEVISE EXISTING AND PROPOSED SEWER | 14-Nov-05 | 23-Nov-05 | |
| WELLS STREET | | | | |
| 1 | TELEVISE EXISTING SEWER | 02-May-05 | 13-May-05 | |
| 2 | TELEVISE EXISTING AND PROPOSED SEWER | 31-Oct-05 | 11-Nov-05 | |
| **CONTRACT 9C12 (62842) - CONDUIT & LIGHT POLE FOUNDATIONS** | | | | |
| STAGE 2 - WENTWORTH AVENUE | | | | |
| 1 | CONSTRUCT NEW LIGHTING FOUNDATIONS | 17-Oct-05 | 23-Nov-05 | |
| STAGE 2 - WELLS STREET | | | | |
| 1 | CONSTRUCT NEW LIGHTING FOUNDATIONS | 26-Sep-05 | 28-Oct-05 | |

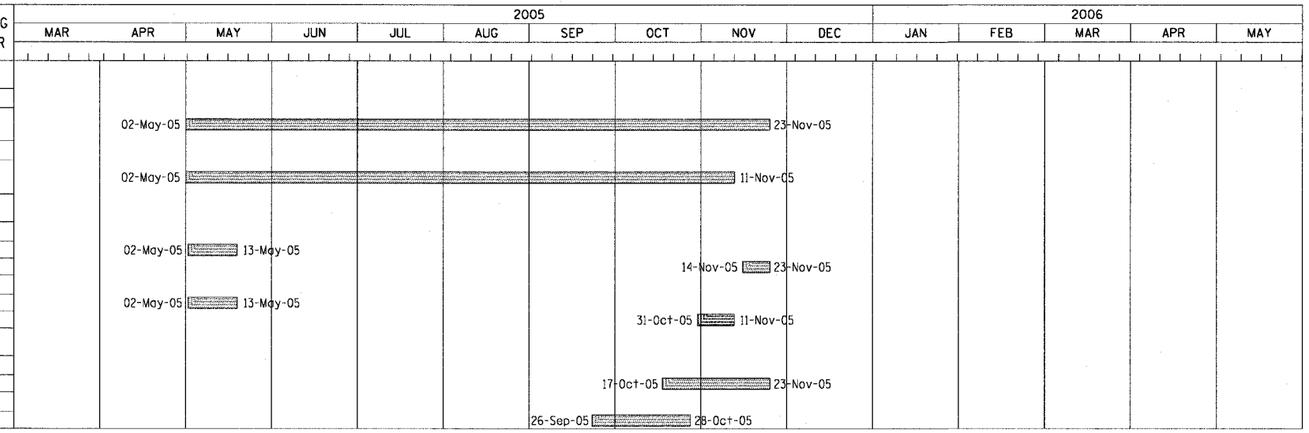


NOTE: DATES ASSOCIATED WITH WORK ITEMS MAY CHANGE BASED ON OTHER CONTRACTS AND/OR THE ENGINEER. NO ADDITIONAL COMPENSATION WILL BE CONSIDERED DUE TO CHANGES OR EXTENSIONS IN THE SCHEDULE.

LEGEND:

WORK PERFORMED IN CONTRACTS BY OTHERS

WORK PERFORMED AS PART OF THIS CONTRACT


CTE ENGINEERS
CONSOER TOWNSEND ENVIRODYNE ENGINEERS, INC.
303 EAST WACKER DRIVE, SUITE 600
CHICAGO ILLINOIS 60601-5212, PHONE: (312) 938-0300




| REVISIONS | |
|---|---|
| NAME | DATE |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |

ILLINOIS DEPARTMENT OF TRANSPORTATION
F.A.I. 90/94 (DAN RYAN EXPRESSWAY)
59th ST TO 47th ST (FRONTAGE ROAD)
CITY OF CHICAGO LIGHTING CONDUIT & FOUNDATIONS
WELLS STREET

SUGGESTED CONSTRUCTION SCHEDULE

SCALE: NONE | DRAWN BY: AMM
DATE: February 11, 2005 | CHECKED BY: RMG

\\cteeh1-nt7\p40468\p40468\eleclN4-cntr-9-sht\contract 9b2\cs09b20052.dgn
02/02/2005 09:01:43 AM
