F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
94	•	COOK	36	5
STA. 91+00		TO STA. 118+20		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		
• 2005-014L				62937

CONTRACT 62304

ID	Task Name	# Crews	Duration	Start	Finish
1	PUBLIC NOTIFICATION (2 weeks)	-	0 days	Mon 4/30/07	Mon 4/30/07
2	traffic control and protection	-	360 days	Mon 7/17/06	Fri 11/30/07
3	BEGIN SB I-94 STAGE 3	-	0 days	Tue 5/15/07	Tue 5/15/07
4	pavement marking removal	2	8 days	Tue 5/15/07	Thu 5/24/07
5	temporary pvmt markings	1	6 days	Thu 5/17/07	Thu 5/24/07
6	temporary concrete barrier	2	12 days	Tue 5/22/07	Wed 6/6/07
7	CTA NOTIFICATION FOR SINGLE TRACKING	-	42 days	Wed 4/4/07	Fri 6/1/07
8	concrete barrier removal	1	8 days	Fri 6/1/07	Tue 6/12/07
9	curb & gutter removal	1	2 days	Thu 6/7/07	Fri 6/8/07
10	pavement removal	2	17 days	Wed 5/30/07	Thu 6/21/07
11	paved shoulder removal	1	15 days	Wed 5/30/07	Tue 6/19/07
12	structure excavation (concrete barrier facing)	1	1 day	Fri 6/22/07	Fri 6/22/07
13	timber lagging (concrete barrier facing)	1	4 days	Mon 6/25/07	Thu 6/28/07
14	drill and set soldier piles (concrete barrier facing)	1	11 days	Fri 6/29/07	Fri 7/13/07
15	structure excavation (sewer saddle)	1	1 day	Fri 6/22/07	Fri 6/22/07
16	reinf. bars epoxy ctd. (sewer saddle)	1	3 days	Mon 6/25/07	Wed 6/27/07
17	concrete structures (sewer saddle)	1	4 days	Thu 6/28/07	Tue 7/3/07
18	earth excavation	2	8 days	Mon 6/18/07	Wed 6/27/07
19	sign panels	1	1 day	Thu 6/28/07	Thu 6/28/07
20	catch basins	2	22 days	Tue 6/12/07	Wed 7/11/07
21	manholes	1	7 days	Fri 6/22/07	Mon 7/2/07
22	storm sewer 12" to 30"	2	18 days	Tue 6/19/07	Thu 7/12/07
23	storm sewer 36 "to 42"	1	3 days	Tue 7/10/07	Thu 7/12/07
24	trench backfill	3	21 days	Fri 6/29/07	Fri 7/27/07
25	subbase gran. mat. 24"	2	14 days	Thu 7/19/07	Tue 8/7/07
26	stabilized subbase 6"	2	10 days	Wed 8/1/07	Tue 8/14/07
27	CRC pavement, 14"	2	10 days	Wed 8/8/07	Tue 8/21/07
28	PCC shoulders, 14"	2	6 days	Fri 8/17/07	Fri 8/24/07
29	concrete curb & gutter	1	2 days	Mon 8/27/07	Tue 8/28/07
30	concrete median surface	1	1 day	Wed 8/29/07	Wed 8/29/07
31	concrete barrier base	2	21 days	Tue 8/21/07	Tue 9/18/07
32	concrete barrier	2	42 days	Wed 8/29/07	Thu 10/25/07
33	reinf. bars epoxy ctd. (concrete barrier facing)	1	5 days	Mon 8/27/07	Fri 8/31/07
34	concrete structures (concrete barrier facing)	1	14 days	Thu 8/30/07	Tue 9/18/07
35	bituminous surface removal	1	3 days	Fri 10/5/07	Tue 10/9/07
36	bituminous binder course	1	1 day	Wed 10/10/07	Wed 10/10/07
37	bituminous surface course	1	2 days	Thu 10/11/07	Fri 10/12/07
38	topsoil furnish & place	1	3 days	Fri 10/26/07	Tue 10/30/07
39	seeding class 2A	1	1 day	Wed 10/31/07	Wed 10/31/07
40	erosion control blanket	2	6 days	Thu 11/1/07	Thu 11/8/07
41	pavement marking removal	2	5 days	Fri 10/26/07	Thu 11/1/07
42	pavement markings	1	8 days	Tue 10/30/07	Thu 11/8/07
43	raised refl pavement markers	2	9 days	Mon 11/5/07	Thu 11/15/07
44	STAGE 3 COMPLETION DATE	-	0 days	Thu 11/15/07	Thu 11/15/07

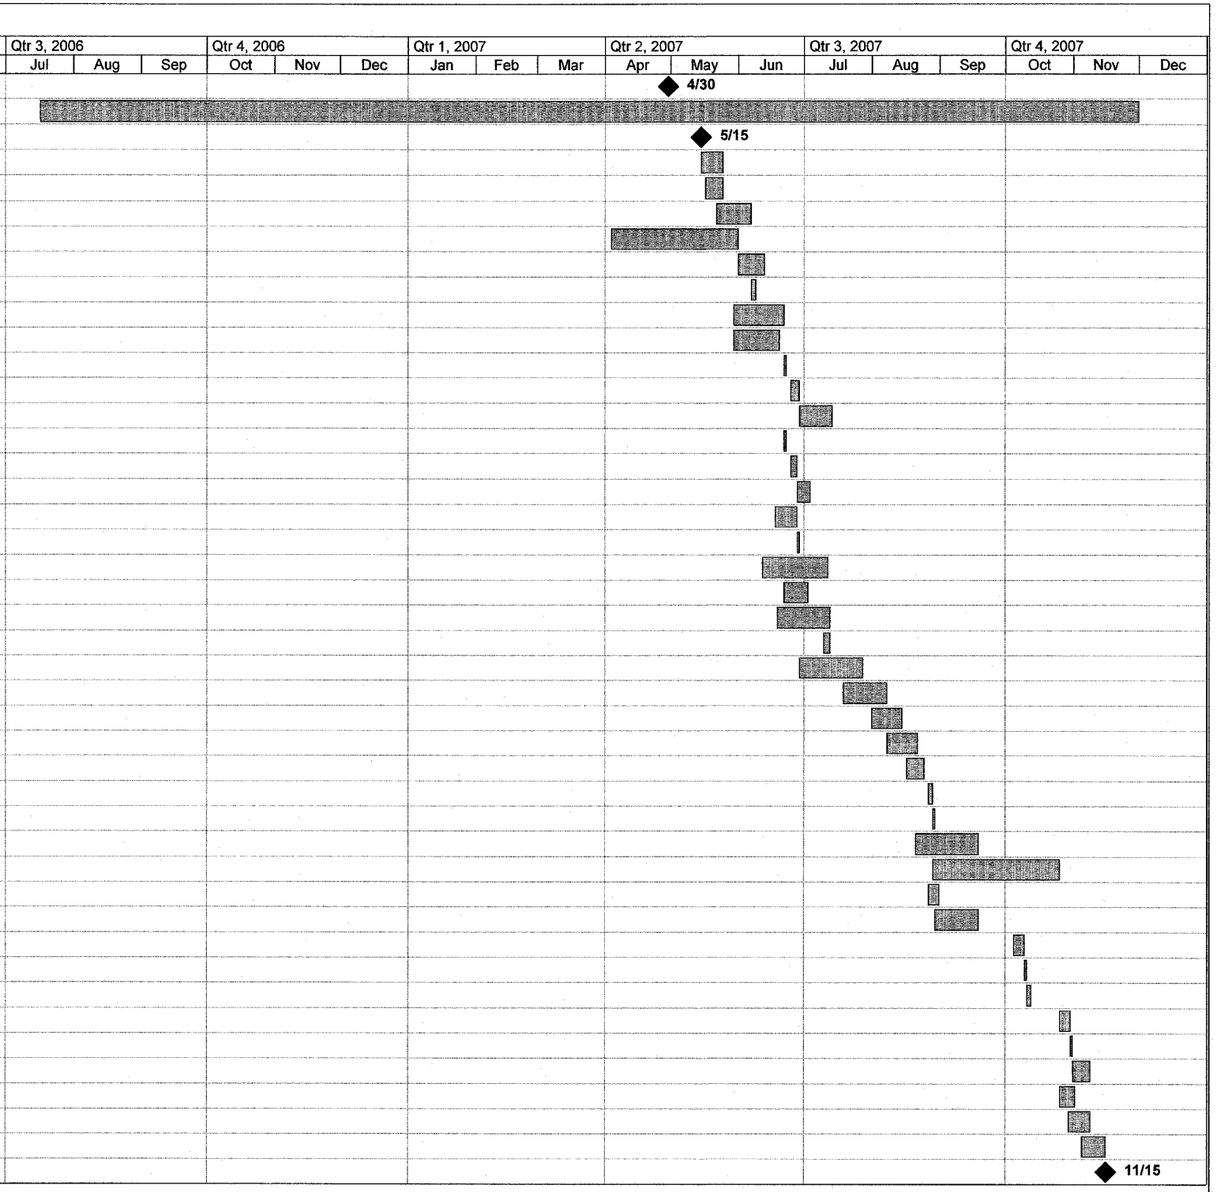

Project:20 Construction Schedule
Date: Thu 11/3/05

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary

FOR INFORMATION ONLY

TY·LIN INTERNATIONAL

NOTES:

1. COORDINATION OF CONSTRUCTION WITH CONTRACT 62304 WILL BE REQUIRED AND SHALL BE CONSIDERED A HIGH PRIORITY.
2. CONCRETE BARRIER WORK SHALL BE COORDINATED WITH CONTRACT 62593 TO ALLOW FOR CONSTRUCTION ON BOTH CONTRACTS 62593 AND 62304 WHILE MAINTAINING CTA SINGLE TRACKING

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

F.A.I. 94 (DAN RYAN EXPRESSWAY)

CONTRACT 20
SUGGESTED CONSTRUCTION SEQUENCE
STAGE 3

SCALE: NONE DRAWN BY: JJS

DATE: JANUARY 13, 2006 CHECKED BY: TGB
