F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
94	*	COOK	36	9
STA. 91+00		TO STA. 118+20		
FED. ROAD DIST. NO.	ILLINOIS	FED. AID PROJECT		

* 2005-014L

62937

CONTRACT 62593

ID	Task Name	# Crews	Duration	Start	Finish
1	PUBLIC NOTIFICATION (2 weeks)	-	0 days	Mon 4/30/07	Mon 4/30/07
2	traffic control and protection	-	349 days	Mon 7/17/06	Thu 11/15/07
3	BEGIN SB I-94 STAGE 3	-	0 days	Tue 5/15/07	Tue 5/15/07
4	temporary pavement (MOT) (pre-stage)	1	3 days	Tue 5/15/07	Thu 5/17/07
5	pavement marking removal (pre-stage)	2	8 days	Tue 5/15/07	Thu 5/24/07
6	temporary pvmt markings (pre-stage)	2	4 days	Mon 5/21/07	Thu 5/24/07
7	temporary concrete barrier (pre-stage)	3	13 days	Mon 5/21/07	Wed 6/6/07
8	curb & gutter removal	1	5 days	Tue 6/5/07	Mon 6/11/07
9	CTA NOTIFICATION FOR SINGLE TRACKING	-	42 days	Fri 4/6/07	Tue 6/5/07
10	concrete barrier removal	1	19 days	Tue 6/5/07	Fri 6/29/07
11	pavement removal	2	21 days	Tue 6/5/07	Tue 7/3/07
12	paved shoulder removal	1	13 days	Tue 6/5/07	Thu 6/21/07
13	formed concrete repair	1	22 days	Wed 7/4/07	Thu 8/2/07
14	structure excavation	1	1 day	Wed 7/4/07	Wed 7/4/07
15	reinf. bars epoxy ctd.	1	8 days	Thu 7/5/07	Mon 7/16/07
16	concrete structures	1	10 days	Tue 7/17/07	Mon 7/30/07
17	earth excavation	1	13 days	Wed 6/27/07	Fri 7/13/07
18	overhead sign foundations	1	4 days	Mon 7/16/07	Thu 7/19/07
19	fabricate structural steel (4 months)	-	80 days	Fri 3/30/07	Fri 7/20/07
20	overhead sign structures	1	3 days	Fri 7/20/07	Tue 7/24/07
21	sign panels	1	1 day	Wed 7/25/07	Wed 7/25/07
22	braced excavation	1	8 days	Wed 6/27/07	Fri 7/6/07
23	junction chambers	1	16 days	Mon 7/9/07	Mon 7/30/07
24	manholes	1	11 days	Wed 6/27/07	Wed 7/11/07
25	drop manholes	1	4 days	Wed 6/27/07	Mon 7/2/07
26	catch basins	3	19 days	Wed 6/27/07	Mon 7/23/07
27	storm sewer 12" to 30"	3	18 days	Wed 7/11/07	Fri 8/3/07
28	trench backfill	3	21 days	Wed 7/11/07	Wed 8/8/07
29	subbase gran. mat. 24"	2	15 days	Tue 7/31/07	Mon 8/20/07
30	stabilized subbase 6"	2	11 days	Tue 8/14/07	Tue 8/28/07
31	CRC pavement, 14"	2	11 days	Fri 8/24/07	Fri 9/7/07
32	PCC shoulders, 14"	2	7 days	Wed 9/5/07	Thu 9/13/07
33	concrete curb and gutter	2	3 days	Wed 9/12/07	Fri 9/14/07
34	conc. median surf.	1	3 days	Mon 9/17/07	Wed 9/19/07
35	concrete barrier base	2	18 days	Wed 9/12/07	Fri 10/5/07
36	concrete barrier facing	1	26 days	Mon 9/17/07	Mon 10/22/07
37	concrete barrier	3	30 days	Tue 9/18/07	Mon 10/29/07
38	bituminous surface removal	1	5 days	Tue 9/4/07	Mon 9/10/07
39	bituminous binder course	1	2 days	Tue 9/11/07	Wed 9/12/07
40	bituminous surface course	1	3 days	Thu 9/13/07	Mon 9/17/07
41	topsoil furnish & place	1	2 days	Tue 10/9/07	Wed 10/10/07
42	seeding class 2A	1	1 day	Thu 10/11/07	Thu 10/11/07
43	erosion control blanket	2	3 days	Fri 10/12/07	Tue 10/16/07
44	pavement marking removal	2	5 days	Tue 10/30/07	Mon 11/5/07
45	pavement markings	2	4 days	Thu 11/1/07	Tue 11/6/07
46	raised refl pavement markers	2	9 days	Mon 11/5/07	Thu 11/15/07
47	STAGE 3 COMPLETION DATE	-	0 days	Thu 11/15/07	Thu 11/15/07

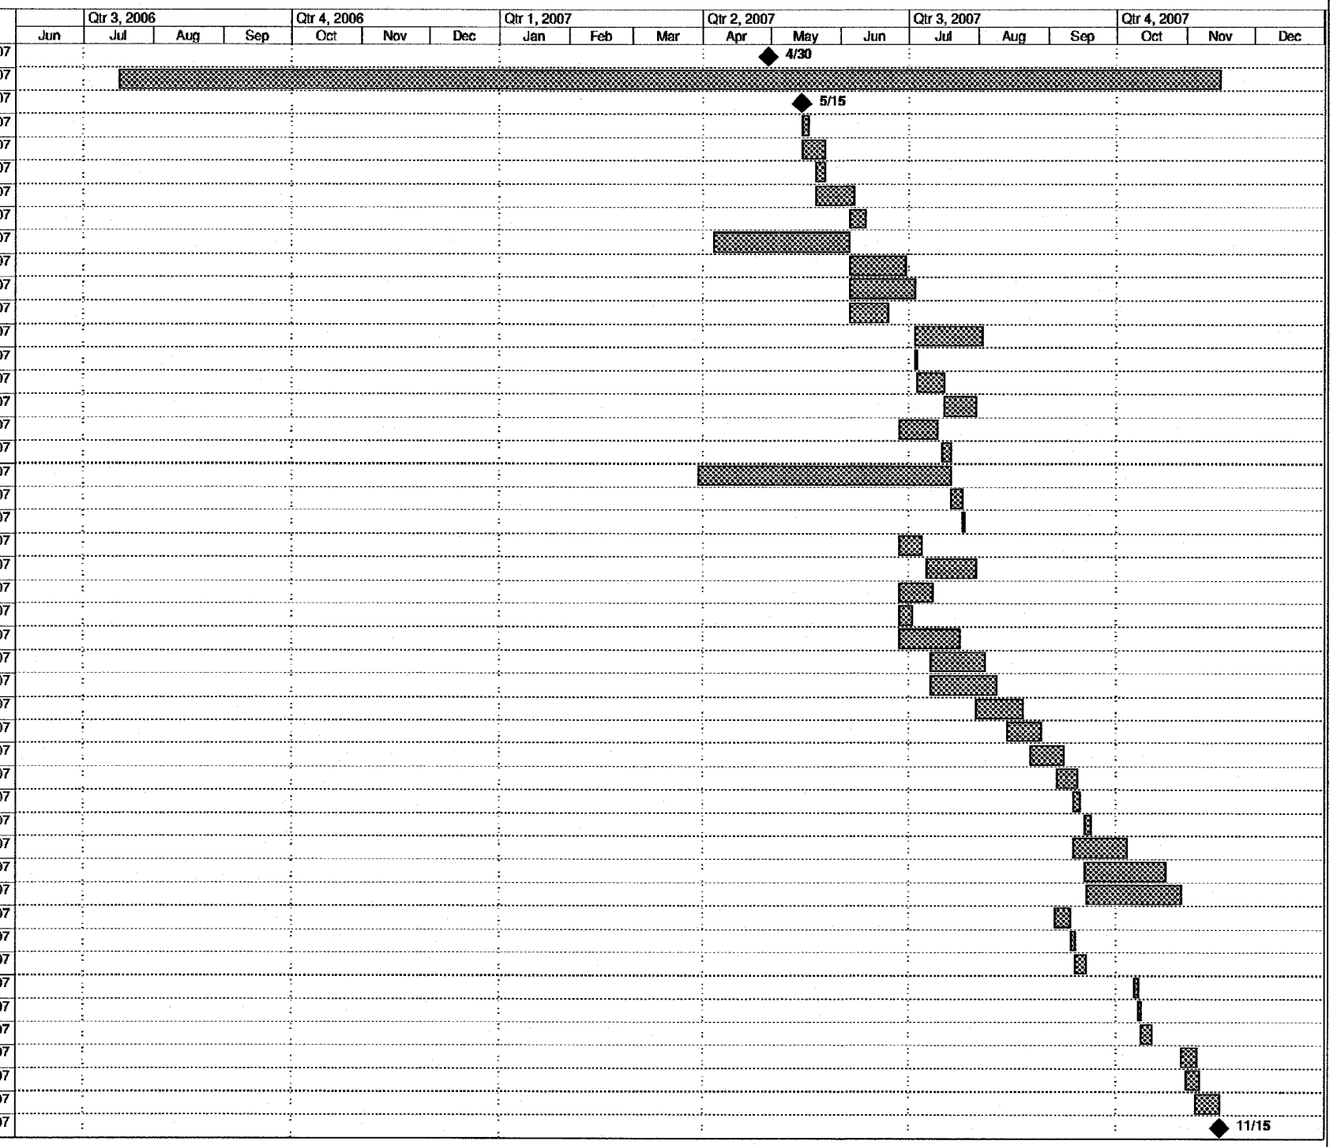

Project:23 Construction Schedule
Date: Mon 10/24/05

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary

Page 1

NOTES:

1. COORDINATION OF CONSTRUCTION WITH CONTRACT 62304 WILL BE REQUIRED AND SHALL BE CONSIDERED A HIGH PRIORITY.
2. CONCRETE BARRIER WORK SHALL BE COORDINATED WITH CONTRACT 62304 TO ALLOW FOR CONSTRUCTION ON BOTH CONTRACTS 62593 AND 62304 WHILE MAINTAINING CTA SINGLE TRACKING

FOR INFORMATION ONLY

TY·LIN INTERNATIONAL

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

F.A.I. 94 (DAN RYAN EXPRESSWAY)

CONTRACT 23
SUGGESTED CONSTRUCTION SEQUENCE
STAGE 3

SCALE: NONE | DRAWN BY: JJS
DATE: JANUARY 13, 2006 | CHECKED BY: TGB
