ILLINOIS DEPARTMENT OF TRANSPORTATION

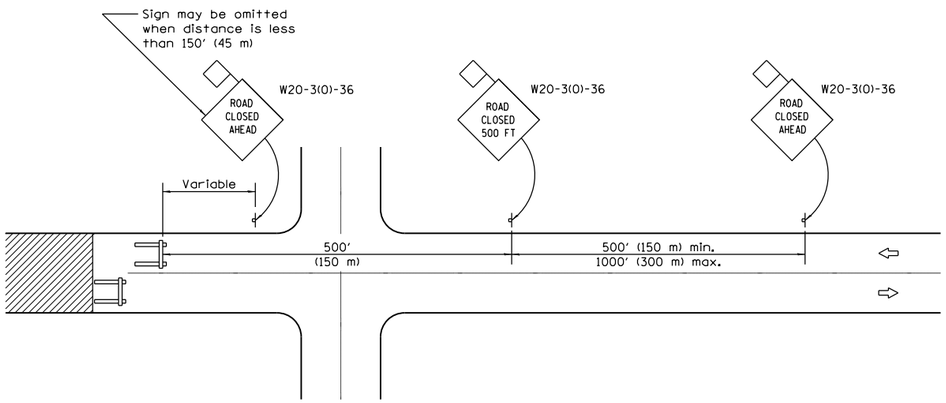

GENERAL NOTES

Two Type A Low Intensity Flashing Lights shall be used on each approach in advance of the work area during hours of darkness. One light shall be installed above the barricades and the other above the first advance warning sign.

All signs shall be post mounted if the closure time exceeds four days.

All warning signs shall have minimum dimensions of 36 x 36 (900 x 900) and have a black legend on an orange reflectorized background.

All work zone signs are required to meet, as a minimum, Type B reflectivity requirements of Table 1091-2 in Article 1091.02 of the Standard Specifications.

When fluorescent signs are used, orange flags are not required.

Longitudinal dimensions may be adjusted to fit field conditions.

When the distance between the barricade and the intersection is between 1500' (450 m) and 2000' (600 m), the advance sign shall be placed at the intersection. When the distance between the barricade and the intersection is over 2000' (600 m), an additional sign shall be placed at the intersection. The additional sign shall give the distance to the barricade in miles or fractions of a mile.

All dimensions are in inches (millimeters) unless otherwise shown.

Two (2) message board shall be placed on US 150 for one (1) week prior to the closure of US 150 to inform motorists of the start date of the closure. (see special provisions)

SYMBOLS

Work area

Type III Barricade

Sign with 18x18 (450x450) min. orange flag attached

CONDITION I

When distance from closure to crossroad is less than 1500' (450 m)

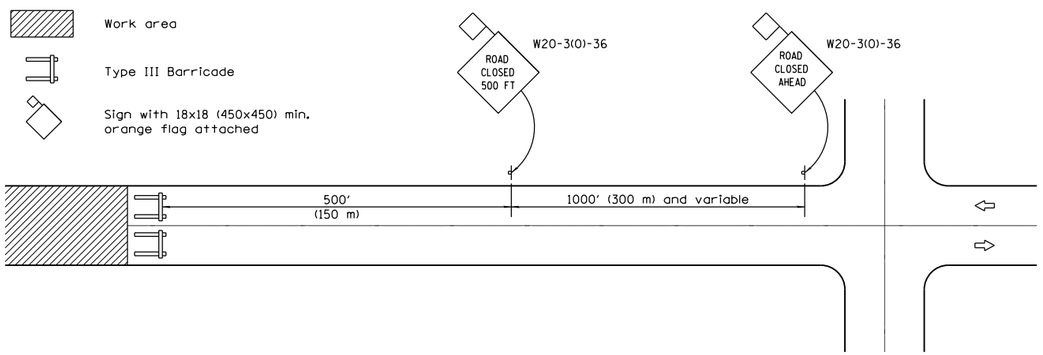

CONDITION II

When distance from closure to crossroad is greater than 1500' (450 m)

US150 and
Condition I

Type III Barricades and R11-4-6030 signs shall be positioned as shown in the "Road Closed To Thru Traffic" detail on Highway Standard 701901

US150 and
Condition II

Type III Barricades and R11-2-4830 signs shall be positioned as shown in the "Road Closed To All Traffic" detail on Highway Standard 701901

NOTE:

ROAD SHALL BE OPEN TO TRAFFIC AFTER 60 CALENDAR DAYS STARTING FROM THE FIRST DAY OF CLOSURE

FILE NAME =	USER NAME =	DESIGNED -	REVISED -	STATE OF ILLINOIS DEPARTMENT OF TRANSPORTATION	DETOUR AND ROAD CLOSURE	F.A. RTE. FAS 2402	SECTION (110,111,112,113)RS-3; 114RS-4;112C-2	COUNTY	TOTAL SHEETS	SHEET NO.
		DRAWN -	REVISED -			U.S. 150		PEORIA	76	45
	PLOT SCALE =	CHECKED -	REVISED -							
	PLOT DATE = 3/20/2013	DATE -	REVISED -		SCALE: SHEET NO. OF SHEETS STA. TO STA.	FED AID PROJECT		CONTRACT NO. 68614		
