CONTRACT NO. 62636

F.A.I. RTE.	SECTION	COUNTY	TOTAL SHEETS	SHEET NO.
94	2003-071 RS	COOK	91	13
STA.		TO STA.		
FED. ROAD DIST. NO. 1	ILLINOIS	FED. AID PROJECT		

STAGE I: 2007

WEEKDAY OPERATIONS:

WORK SEQUENCE:

APPLY TEMPORARY PAVEMENT MARKING LANES 1 & 2
(LANE CLOSURES ALLOWED AS DETAILED IN THE SPECIAL PROVISIONS)
COMPLETE PATCH OPERATIONS LANE 3 AND OUTSIDE SHOULDER WHERE SPECIFIED
COMPLETE JOINT REPAIR BETWEEN LANE 3 AND SHOULDER AT LOCATIONS SPECIFIED IN THE SCHEDULE
REMOVE TEMPORARY PAVEMENT MARKING LANES 1 & 2

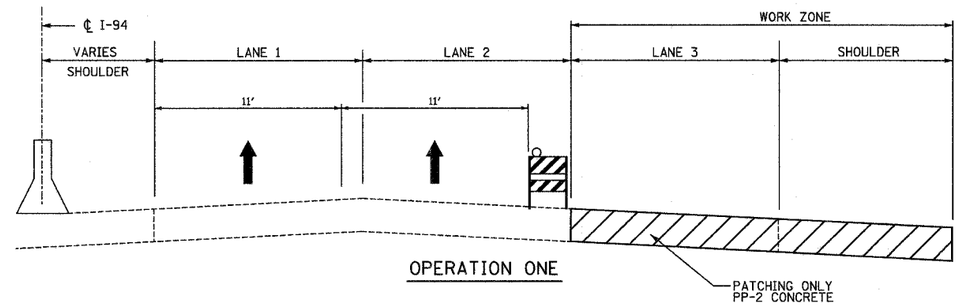

OPERATION ONE

WEEKEND OPERATIONS:

APPLY TEMPORARY PAVEMENT MARKING LANE 1
(LANE CLOSURES ALLOWED AS DETAILED IN THE SPECIAL PROVISIONS)
COMPLETE PATCH OPERATIONS LANE 2 USING PP-5 CONCRETE
REMOVE TEMPORARY PAVEMENT MARKING LANES 1



OPERATION TWO

PATCHING REQUIRED IN LANE 2

REVISIONS	
NAME	DATE

ILLINOIS DEPARTMENT OF TRANSPORTATION

N.T.S.

TRAFFIC CONTROL
AND PROTECTION
F.A.I. 94 EDENS EXPRESSWAY
TYPICAL SECTIONS PER SEGMENT

SCALE: DRAWN BY
DATE JUNE 2007 CHECKED BY

PLOT DATE = 06/18/2007
FILE NAME = $FILEL$
PLOT SCALE = $SCALE$
USER NAME = GeYoLi+

Edens I 94 Resurfacing Project
